



07131

CR3 Outage Containment Repair Project - Level 3 Schedule

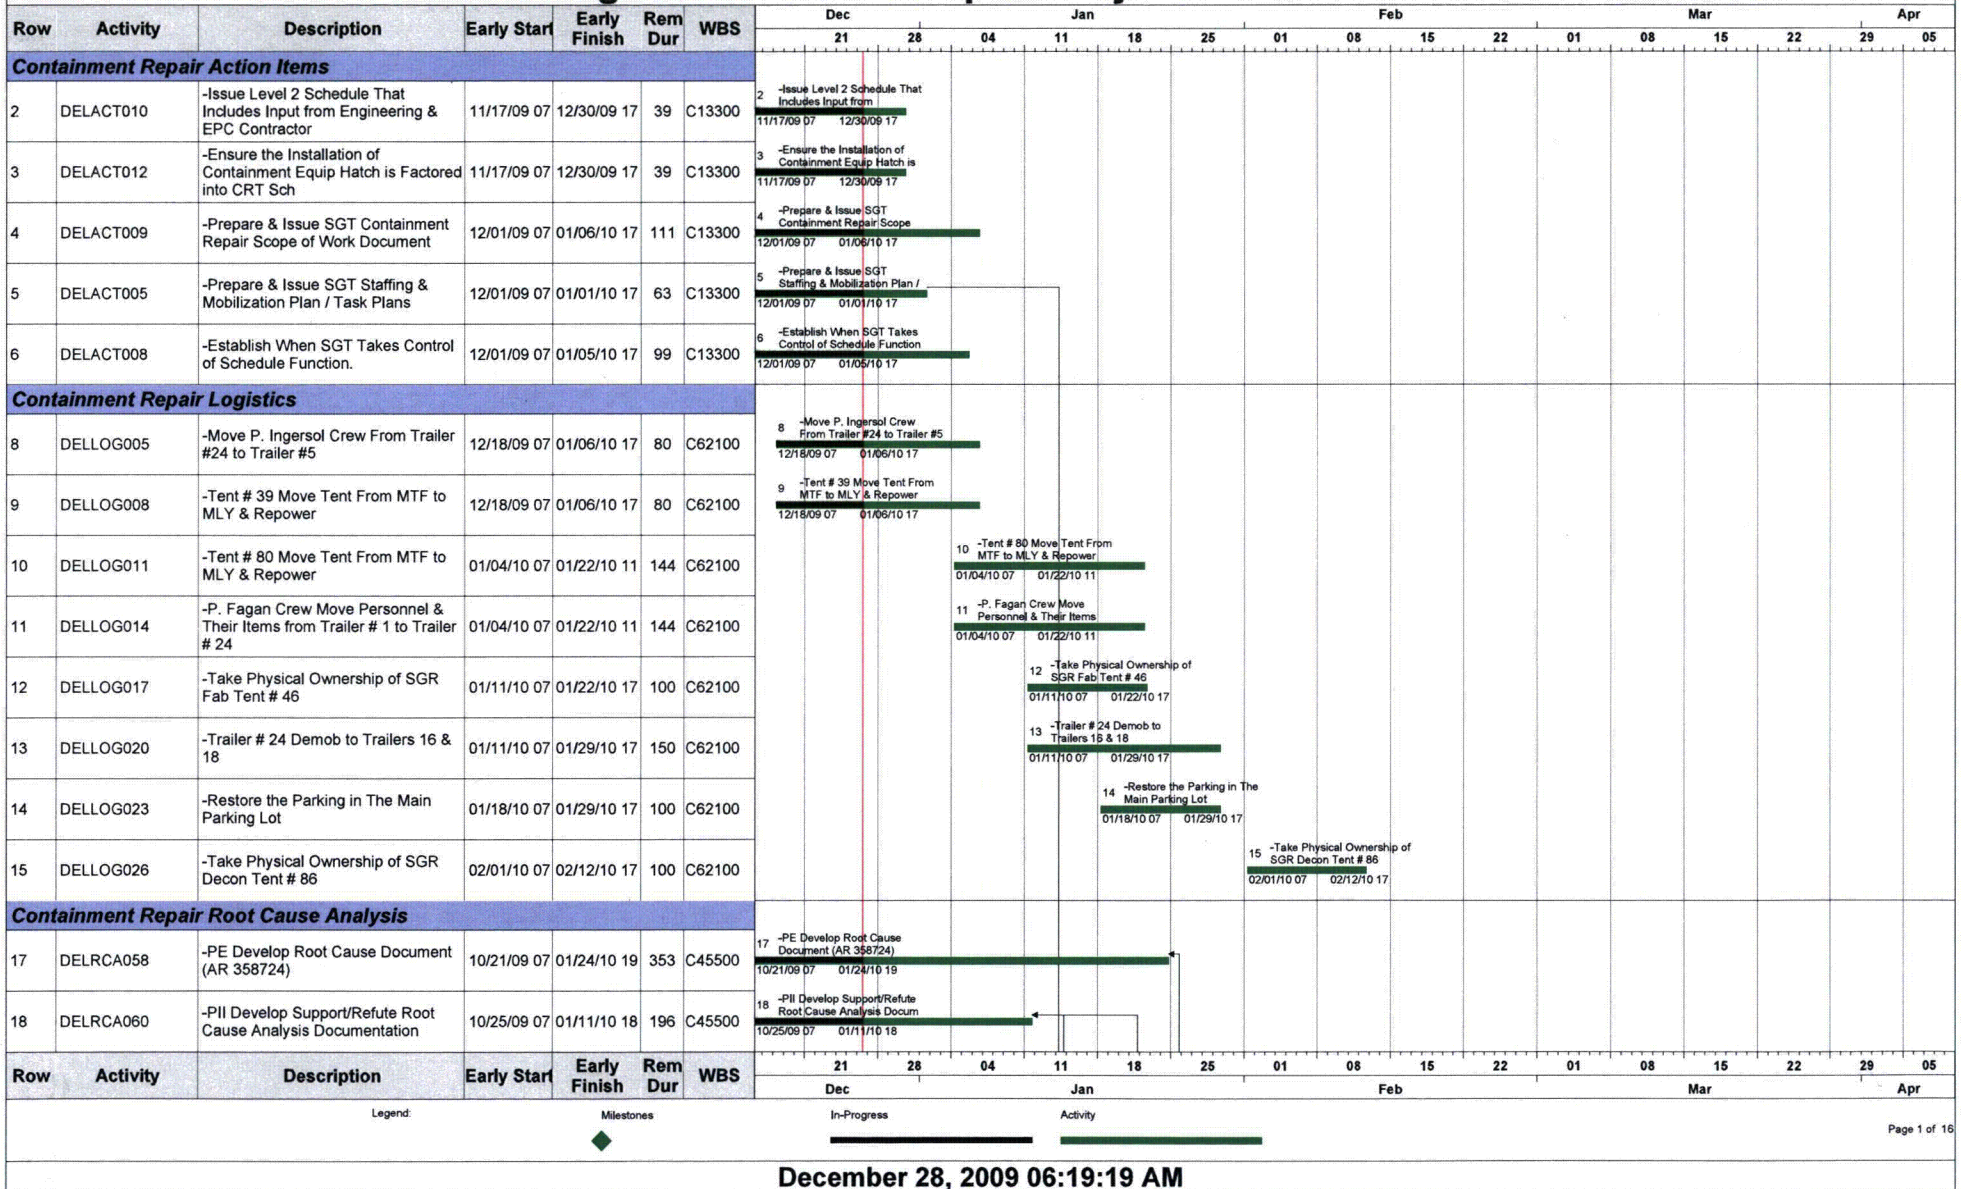

December 28, 2009 06:19:19 AM

CR3 Outage Containment Repair Project - Level 3 Schedule

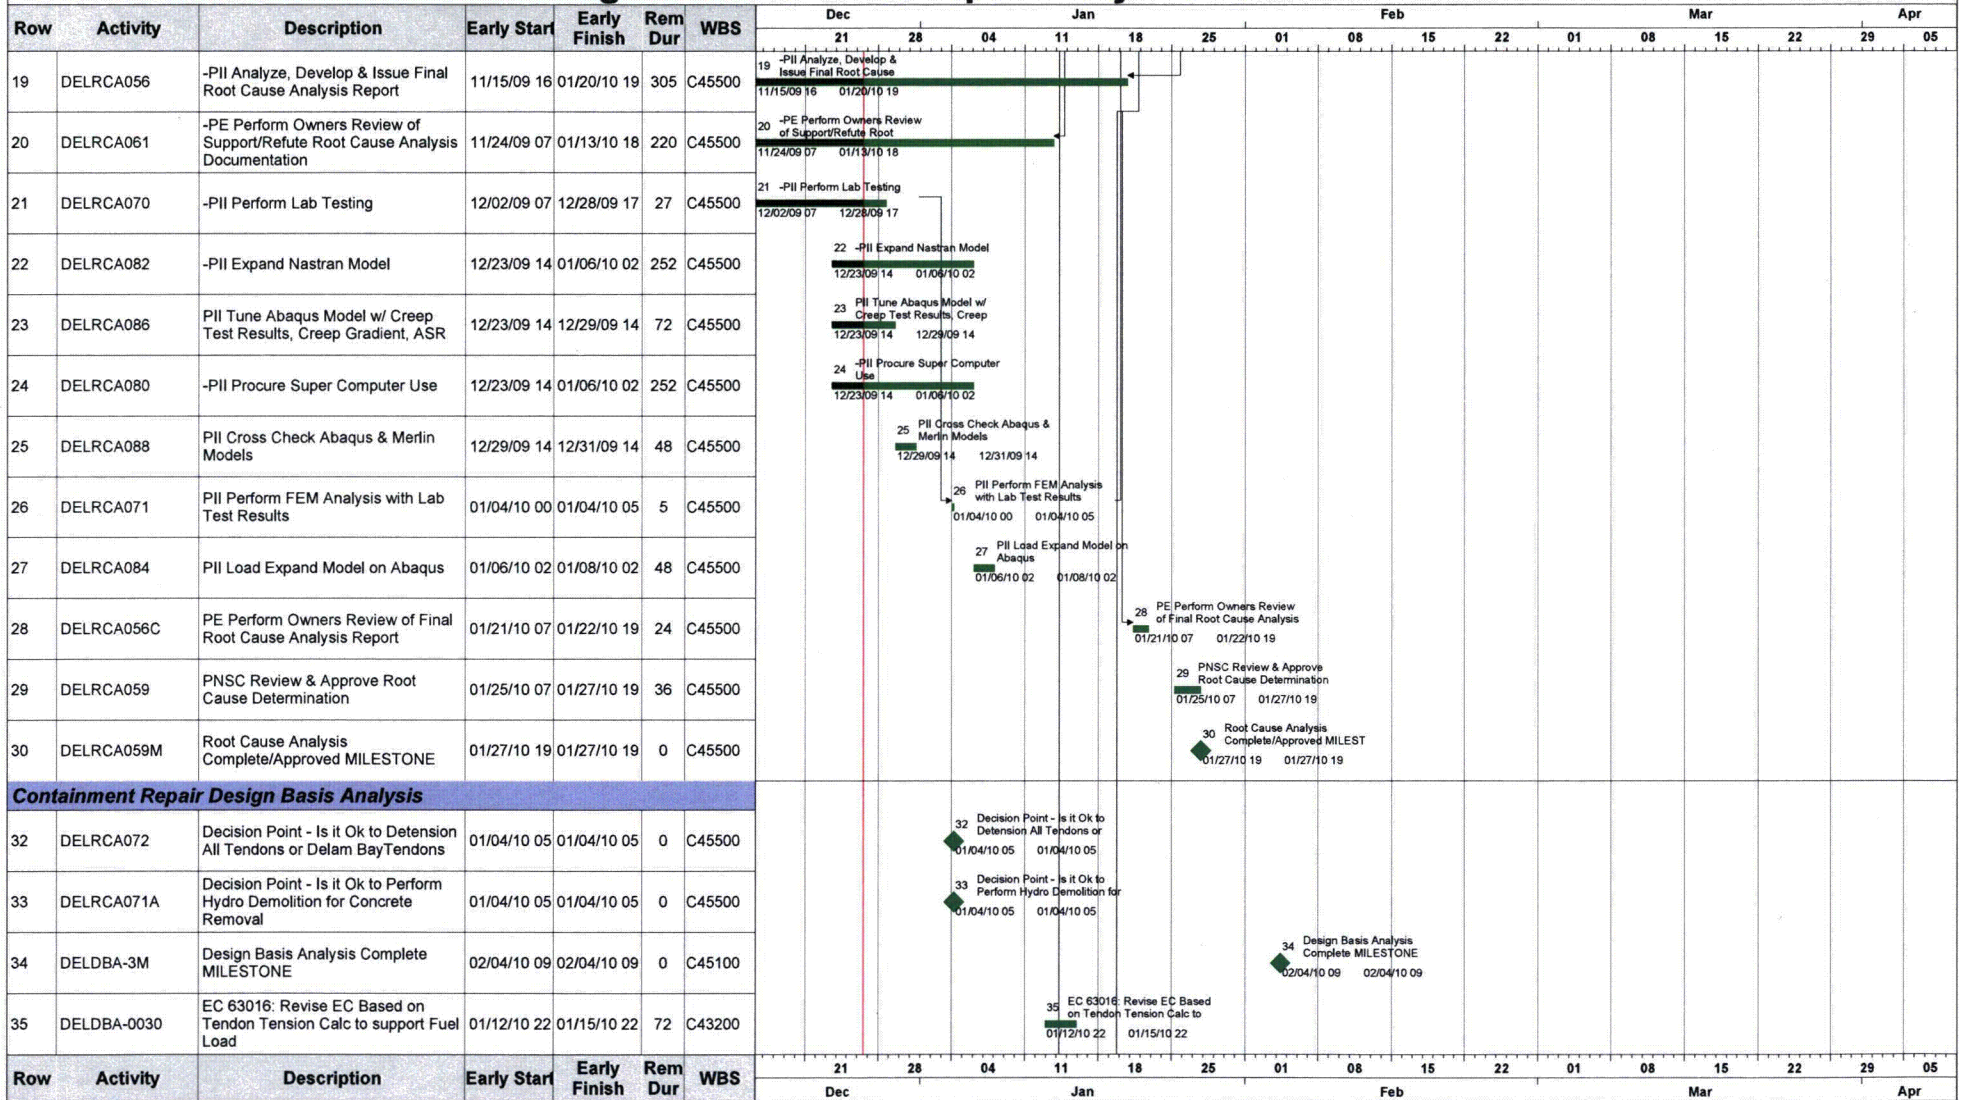

Legend:

Milestones

In-Progress

Activity

December 28, 2009 06:19:19 AM

CR3 Outage Containment Repair Project - Level 3 Schedule

Row	Activity	Description	Early Start	Early Finish	Rem Dur	WBS	Dec		Jan					Feb					Mar					Apr						
							21	28	04	11	18	25	01	08	15	22	01	08	15	22	29	05								
53	DELDBA-2M	Containment Bldg Calc Compl MILESTONE	02/04/10 09	02/04/10 09	0	C43200																								
Containment Repair Implementation Design																														
55	DELDESL1M	EC Implementation Design Complete MILESTONE	02/13/10 03	02/13/10 03	0	C45100																								
56	DELDES11710	EC 75000 PH 1 Concrete Cut: Planning Prepare W/O 01652765 Work Packages	12/26/09 14	12/28/09 14	48	C47100																								
57	DELDES21023M	EC 75218 PH 2 Detension: Incorp Final MPR Detension Calc Results into EC	12/28/09 09	12/29/09 09	24	C45100																								
58	DELDES21020M	EC 75218 PH 2 Detension: Develop 70% Pkg	01/04/10 05	01/06/10 13	56	C45100																								
59	DELDES21600	EC 75218 PH 2 Detension: ID Long Lead material to Procurement	01/06/10 09	01/06/10 13	4	C45100																								
60	DELDES21025	EC 75218 PH 2 Detension: Distribute 70% Pkg for Review	01/06/10 13	01/06/10 21	8	C45100																								
61	DELDES2111M	EC 75218 PH 2 Detension: Develop Final EC "Pkg for final DRB"	01/06/10 13	01/11/10 13	120	C45100																								
62	DELDES21027	EC 75218 PH 2 Detension: Review 70% Pkg	01/06/10 21	01/07/10 21	24	C45100																								
63	DELDES21030	EC 75218 PH 2 Detension: 70% Package Meeting	01/07/10 19	01/07/10 21	2	C45100																								
64	DELDES2120Z	EC 75218 PH 2 Detension: MILESTONE - 70% Pkg Mtg Cplt	01/07/10 21	01/07/10 21	0	C45100																								
65	DELDES2115M	EC 75218 PH 2 Detension: Mech / Struc - DV	01/11/10 13	01/13/10 13	48	C45100																								
66	DELDES2120	EC 75218 PH 2 Detension: Inter-Departmental Reviews	01/11/10 13	01/13/10 13	48	C45100																								
67	DELDES2190Z	EC 75218 PH 2 Detension: Milestone - Issued for Final Review	01/12/10 22	01/12/10 22	0	C45100																								
68	DELDES2117	EC 75218 PH 2 Detension: Incorp Verification Comments	01/13/10 13	01/14/10 13	24	C45100																								
69	DELDES2123	EC 75218 PH 2 Detension: Incorp Review Comments	01/13/10 13	01/14/10 13	24	C45100																								

Legend:

Milestones

In-Progress

Activity

CR3 Outage Containment Repair Project - Level 3 Schedule

Row	Activity	Description	Early Start	Early Finish	Rem Dur	WBS	Schedule															
							Dec	Jan	Feb	Mar	Apr											
							21	28	04	11	18	25	01	08	15	22	01	08	15	22	29	05
70	DELDES2125	EC 75218 PH 2 Detension: Supv Review Prior to Final DRB	01/14/10 13	01/14/10 17	4	C45100																
71	DELDES2125D	EC 75218 PH 2 Detension: Distrib Final DRB Pkg for Review	01/14/10 17	01/14/10 18	1	C45100																
72	DELDES2125R	EC 75218 PH 2 Detension: Review Final DRB Pkg	01/14/10 18	01/15/10 18	24	C45100																
73	DELDES21205	EC 75218 PH 2 Detension: Final DRB Meeting	01/15/10 18	01/15/10 20	2	C45100																
74	DELDES21215	EC 75218 PH 2 Detension: Incorporate Final DRB Comments	01/15/10 20	01/16/10 20	24	C45100																
75	DELDES21220	EC 75218 PH 2 Detension: Obtain Supervisor Approval	01/16/10 20	01/17/10 04	8	C45100																
76	DELDES2130Z	EC 75218 PH 2 Detension: MILESTONE - All Reviews Complete	01/16/10 20	01/16/10 20	0	C45100																
77	DELDES21225	EC 75218 PH 2 Detension: Obtain PGM Approval	01/17/10 04	01/18/10 04	24	C45100																
78	DELDES21710	EC 75218 PH 2 Detension: Planning Prepare EC Work Packages	01/18/10 04	01/21/10 04	72	C47100																
79	DELDES2140Z	EC 75218 PH 2 Detension: MILESTONE -OK to Start Field Work	01/18/10 04	01/18/10 04	0	C45100																
80	DELDES31020M	-EC 75219 PH 3 Removal: Develop 30% Design Pkg	12/09/09 07	12/28/09 12	22	C45100																
81	DELDES3115N	-EC 75219 PH 3 Removal: Revise IWE/IWL Repair Plans	12/28/09 12	01/28/10 10	370	C45100																
82	DELDES31025	EC 75219 PH 3 Removal: Distribute 30% Design Pkg for Review	12/28/09 12	12/29/09 08	8	C45100																
83	DELDES31027	EC 75219 PH 3 Removal: Review 30% Design Pkg	12/29/09 08	12/30/09 08	24	C45100																
84	DELDES31030	EC 75219 PH 3 Removal: 30% Design Review Meeting	12/30/09 06	12/30/09 08	2	C45100																
85	DELDES3120Z	EC 75219 PH 3 Removal: MILESTONE - 30% Design Review Complete	12/30/09 08	12/30/09 08	0	C45100																
86	DELDES3111M	-EC 75219 PH 3 Removal: Develop Final EC "Pkg for final DRB"	12/30/09 08	01/16/10 10	206	C45100																

December 28, 2009 06:19:19 AM

CR3 Outage Containment Repair Project - Level 3 Schedule

Row	Activity	Description	Early Start	Early Finish	Rem Dur	WBS	Schedule															
							Dec 21	28	04	11	18	25	01	08	15	22	01	08	15	22	29	05
87	DELDES3120	-EC 75219 PH 3 Removal: Inter-Departmental Reviews	01/16/10	01/22/10	144	C45100																
88	DELDES3190Z	EC 75219 PH 3 Removal: Milestone - Issued for Final Review	01/16/10	01/16/10	0	C45100																
89	DELDES3115M	-EC 75219 PH 3 Removal: Mech / Struc - DV	01/22/10	01/28/10	144	C45100																
90	DELDES3123	EC 75219 PH 3 Removal: Incorp Review Comments	01/22/10	01/24/10	07	C45100																
91	DELDES3117	EC 75219 PH 3 Removal: Incorp Verification Comments	01/28/10	01/30/10	07	C45100																
92	DELDES3125	EC 75219 PH 3 Removal: Supv Review Prior to Final DRB	01/30/10	01/30/10	11	C45100																
93	DELDES3125D	EC 75219 PH 3 Removal: Distrib Final DRB Pkg for Review	01/30/10	01/30/10	12	C45100																
94	DELDES3125R	EC 75219 PH 3 Removal: Review Final DRB Pkg	01/30/10	02/02/10	06	C45100																
95	DELDES31205	EC 75219 PH 3 Removal: Final DRB Meeting	02/02/10	02/02/10	08	C45100																
96	DELDES31215	EC 75219 PH 3 Removal: Incorporate Final DRB Comments	02/02/10	02/04/10	08	C45100																
97	DELDES31220	EC 75219 PH 3 Removal: Obtain Supervisor Approval	02/04/10	02/05/10	08	C45100																
98	DELDES3130Z	EC 75219 PH 3 Removal: MILESTONE - All Reviews Complete	02/04/10	02/04/10	08	C45100																
99	DELDES31225	EC 75219 PH 3 Removal: Obtain PGM Approval	02/05/10	02/05/10	23	C45100																
100	DELDES3140Z	EC 75219 PH 3 Removal: MILESTONE - PGM Approval	02/05/10	02/05/10	23	C45100																
101	DELDES31710	EC 75219 PH 3 Removal: Planning Prepare EC Work Packages	02/05/10	02/08/10	23	C47100																
102	DELDES41008D	EC 75220 PH 4 Replacement: 30% Design Challenge	12/30/09	12/30/09	12	C45100																
103	DELDES4111M	EC 75220 PH 4 Replacement: Develop 70% EC "Pkg for Design Challenge	01/12/10	01/21/10	11	C45100																

Row	Activity	Description	Early Start	Early Finish	Rem Dur	WBS	Dec 21	28	04	11	18	25	01	08	15	22	01	08	15	22	29	05
-----	----------	-------------	-------------	--------------	---------	-----	--------	----	----	----	----	----	----	----	----	----	----	----	----	----	----	----

Legend

Milestones

In-Progress

Activity

December 28, 2009 06:19:19 AM


CR3 Outage Containment Repair Project - Level 3 Schedule

Row	Activity	Description	Early Start	Early Finish	Rem Dur	WBS	Schedule															
							Dec	Jan	Feb	Mar	Apr											
104	DELDES4-0009	EC 75220 PH 4 Replacement: AREVA Revise Existing & Create New Reinforcement Dwgs	01/15/10 09	01/20/10 23	134	C45100																
105	DELDES4-0008	EC 75220 PH 4 Replacement: AREVA Design Additional Reinforcement for Delam Area	01/15/10 09	01/20/10 23	134	C45100																
106	DELDES4-0010	EC 75220 PH 4 Replacement: AREVA Issue Reinforcement Calc/Dwgs	01/15/10 09	01/31/10 23	398	C45100																
107	DELDES4-0011	EC 75220 PH 4 Replacement: AREVA Review & Revise Calc S06-0007 for Liner Plate	01/15/10 09	01/31/10 23	398	C45100																
108	DELDES4-0024	EC 75220 PH 4 Replacement: AREVA Revise Calc S09-0044	01/15/10 09	01/31/10 23	398	C45100																
109	DELDES4-0002	EC 75220 PH 4 Replacement: SGT Revise Formwork Spec CR3-C-0002	01/15/10 09	02/02/10 23	446	C45100																
110	DELDES4-0001	EC 75220 PH 4 Replacement: SGT Revise Formwork Calc S08-0021	01/15/10 09	02/02/10 23	446	C45100																
111	DELDES4-0004	EC 75220 PH 4 Replacement: AREVA Revise Concrete Spec CR3-C-0003&Verify Mix Dsn	01/15/10 09	01/20/10 23	134	C45100																
112	DELDES41008B	EC 75220 PH 4 Replacement: Receive Design Input on Form Work from SGT	01/15/10 09	01/15/10 09	0	C45100																
113	DELDES4-0006	EC 75220 PH 4 Replacement: AREVA Design Radial Reinforcement	01/15/10 09	01/20/10 23	134	C45100																
114	DELDES4-0016	EC 75220 PH 4 Replacement: MPR Revise Calc S06-0002	01/15/10 09	01/31/10 23	398	C45100																
115	DELDES4-0021	EC 75220 PH 4 Replacement: Void Calc S08-0008	01/15/10 09	02/09/10 04	595	C45100																
116	DELDES4-0014	EC 75220 PH 4 Replacement: AREVA/MPR Revise Calc S06-0004	01/15/10 09	01/31/10 23	398	C45100																
117	DELDES4-0018	EC 75220 PH 4 Replacement: AREVA/MPR Revise Calc S06-0005	01/15/10 09	01/31/10 23	398	C45100																
118	DELDES4-0020	EC 75220 PH 4 Replacement: Void Calc S06-0006	01/15/10 09	02/09/10 04	595	C45100																
119	DELDES4-0013	EC 75220 PH 4 Replacement: Void Calc S09-0025	01/15/10 09	02/03/10 23	470	C45100																
120	DELDES4-0022	EC 75220 PH 4 Replacement: MPR Revise Calc S09-0048	01/15/10 09	01/31/10 23	398	C45100																

Legend: Milestones In-Progress Activity

December 28, 2009 06:19:19 AM

CR3 Outage Containment Repair Project - Level 3 Schedule

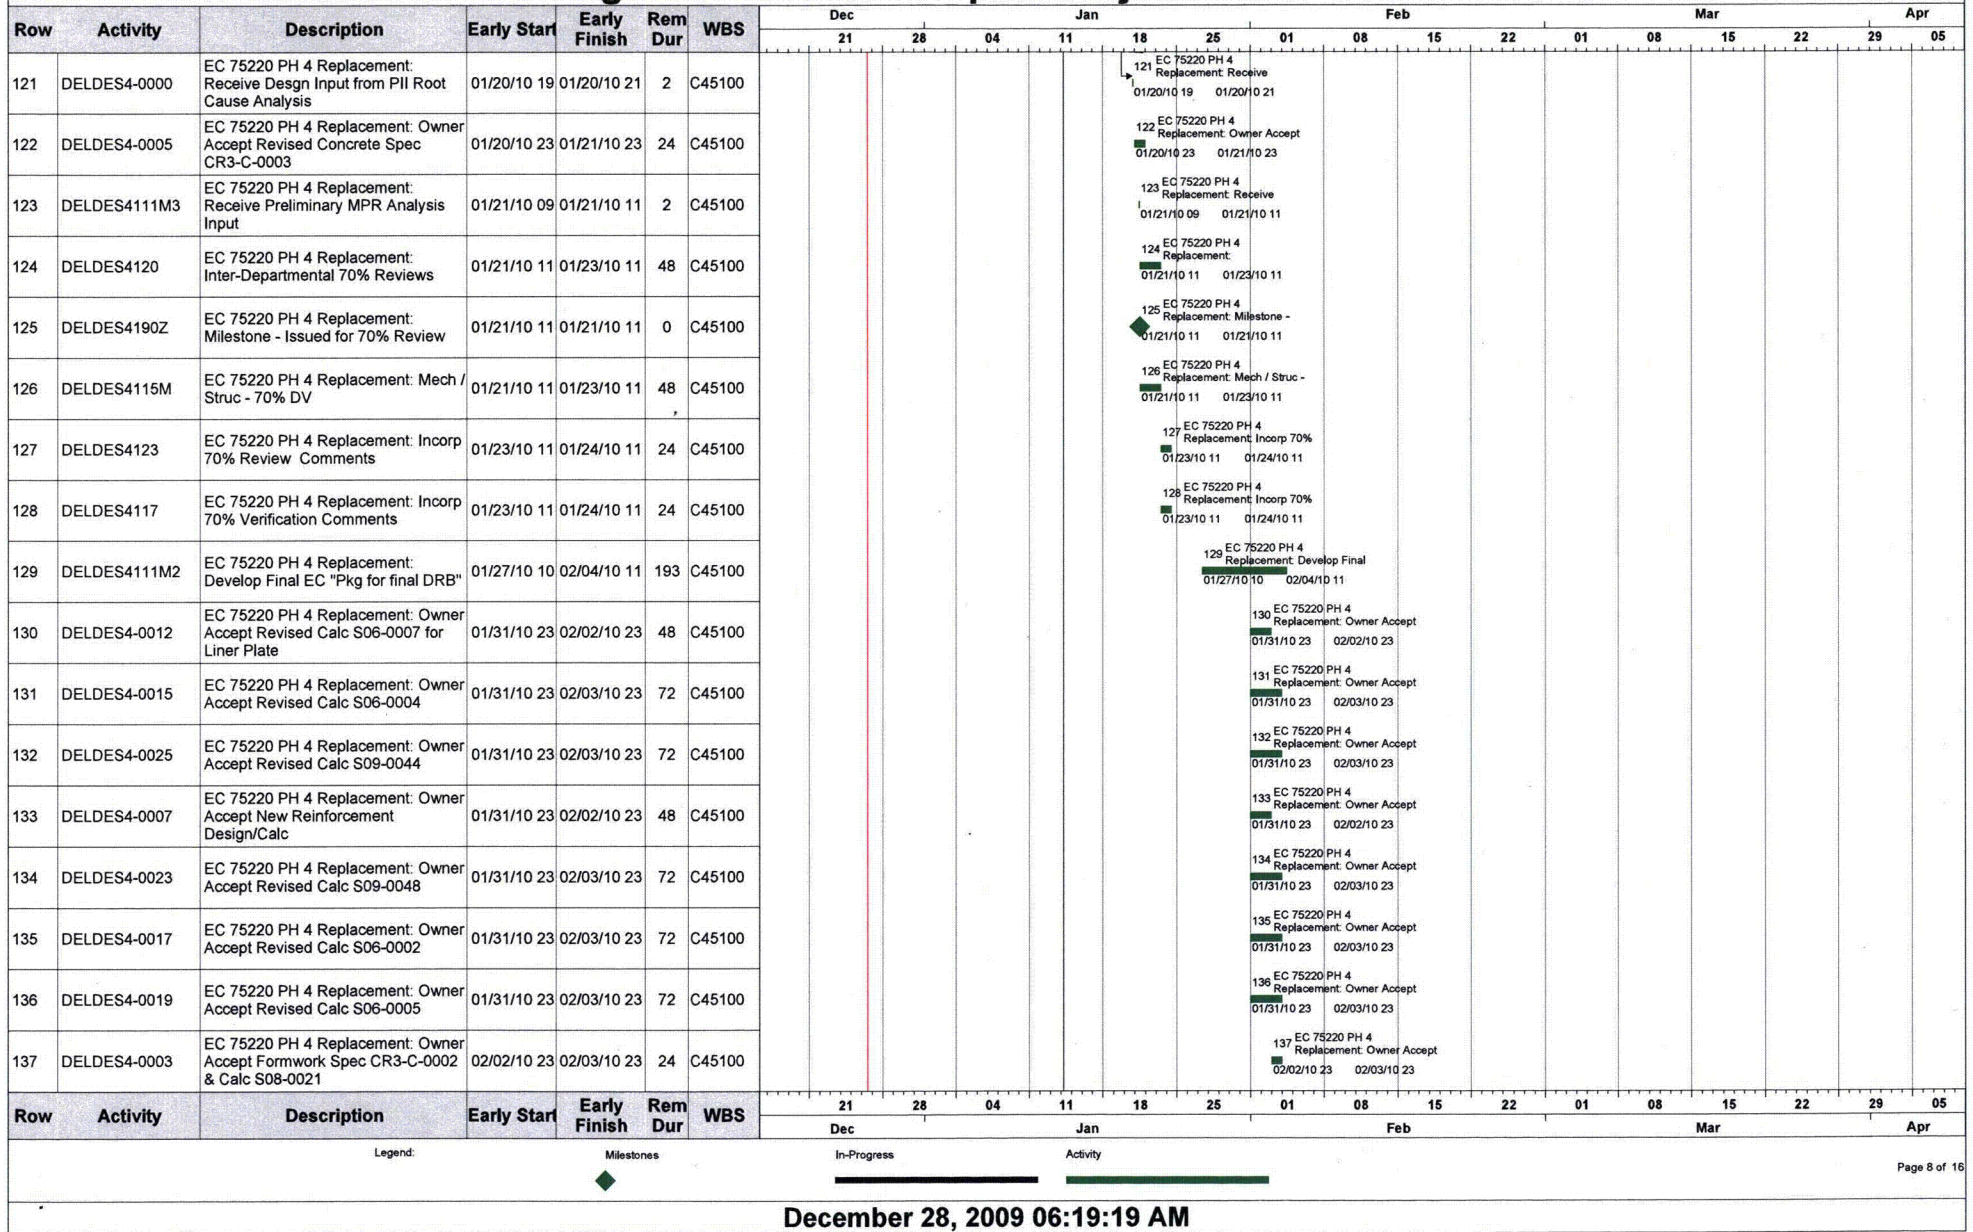

CR3 Outage Containment Repair Project - Level 3 Schedule

Row	Activity	Description	Early Start	Early Finish	Rem Dur	WBS	Schedule																
							Dec	Jan				Feb				Mar				Apr			
							21	28	04	11	18	25	01	08	15	22	01	08	15	22	29	05	
138	DELDES4111M1	EC 75220 PH 4 Replacement: Receive Approved MPR Analysis Input	02/04/10	09 02/04/10	11	2	C45100							138 EC 75220 PH 4 Replacement: Receive 02/04/10 09 02/04/10 11									
139	DELDES4120A	EC 75220 PH 4 Replacement: Final Inter-Departmental Reviews	02/04/10	11 02/08/10	12	97	C45100							139 EC 75220 PH 4 Replacement: Final 02/04/10 11 02/08/10 12									
140	DELDES4115M1	EC 75220 PH 4 Replacement: Final Mech / Struc - DV	02/04/10	11 02/08/10	12	97	C45100							140 EC 75220 PH 4 Replacement: Final Mech / 02/04/10 11 02/08/10 12									
141	DELDES4123A	EC 75220 PH 4 Replacement: Incorp Final Review Comments	02/08/10	12 02/09/10	12	24	C45100							141 EC 75220 PH 4 Replacement: Incorp Final 02/08/10 12 02/09/10 12									
142	DELDES4117F	EC 75220 PH 4 Replacement: Incorp Final Verification Comments	02/08/10	12 02/09/10	12	24	C45100							142 EC 75220 PH 4 Replacement: Incorp Final 02/08/10 12 02/09/10 12									
143	DELDES4125	EC 75220 PH 4 Replacement: Supv Review Prior to Final DRB	02/09/10	12 02/09/10	16	4	C45100							143 EC 75220 PH 4 Replacement: Supv Review 02/09/10 12 02/09/10 16									
144	DELDES4125D	EC 75220 PH 4 Replacement: Distrib Final DRB Pkg for Review	02/09/10	16 02/09/10	17	1	C45100							144 EC 75220 PH 4 Replacement: Distrib Final 02/09/10 16 02/09/10 17									
145	DELDES4125R	EC 75220 PH 4 Replacement: Review Final DRB Pkg	02/09/10	17 02/10/10	17	24	C45100							145 EC 75220 PH 4 Replacement: Review Final 02/09/10 17 02/10/10 17									
146	DELDES41205	EC 75220 PH 4 Replacement: Final DRB Meeting	02/10/10	17 02/10/10	19	2	C45100							146 EC 75220 PH 4 Replacement: Final DRB Me 02/10/10 17 02/10/10 19									
147	DELDES41215	EC 75220 PH 4 Replacement: Incorporate Final DRB Comments	02/10/10	19 02/11/10	19	24	C45100							147 EC 75220 PH 4 Replacement: Incorporate 02/10/10 19 02/11/10 19									
148	DELDES4130Z	EC 75220 PH 4 Replacement: MILESTONE - All Reviews Complete	02/11/10	19 02/11/10	19	0	C45100							148 EC 75220 PH 4 Replacement: MILESTONE - 02/11/10 19 02/11/10 19									
149	DELDES41220	EC 75220 PH 4 Replacement: Obtain Supervisor Approval	02/11/10	19 02/12/10	03	8	C45100							149 EC 75220 PH 4 Replacement: Obtain 02/11/10 19 02/12/10 03									
150	DELDES41225	EC 75220 PH 4 Replacement: Obtain PGM Approval	02/12/10	03 02/13/10	03	24	C45100							150 EC 75220 PH 4 Replacement: Obtain PGM A 02/12/10 03 02/13/10 03									
151	DELDES41710	EC 75220 PH 4 Replacement: Planning Prepare EC Work Packages	02/13/10	03 02/16/10	03	72	C47100							151 EC 75220 PH 4 Replacement: Planning 02/13/10 03 02/16/10 03									
152	DELDES4140Z	EC 75220 Replacement MILESTONE - PGM Approval	02/13/10	03 02/13/10	03	0	C45100							152 EC 75220 Replacement MILESTONE - PGM Approv 02/13/10 03 02/13/10 03									
153	DELDES510Z	EC 75221 PH 5 Retension: MILESTONE - "Start Project"	01/15/10	07 01/15/10	07	0	C45100							153 EC 75221 PH 5 Retension: MILESTONE - "Start Project" 01/15/10 07 01/15/10 07									
154	DELDES51005	EC 75221 PH 5 Retension: Prep / Cplt Validation Plan w/Supv	01/15/10	07 01/15/10	09	2	C45100							154 EC 75221 PH 5 Retension: Prep / Cplt Validation Plan w/ 01/15/10 07 01/15/10 09									

Row	Activity	Description	Early Start	Early Finish	Rem Dur	WBS	Dec	Jan	Feb	Mar	Apr
-----	----------	-------------	-------------	--------------	---------	-----	-----	-----	-----	-----	-----

Legend: Milestones In-Progress Activity

December 28, 2009 06:19:19 AM

CR3 Outage Containment Repair Project - Level 3 Schedule

Row	Activity	Description	Early Start	Early Finish	Rem Dur	WBS	Schedule Gantt Chart																											
							Dec	21	28	04	11	18	25	01	08	15	22	01	08	15	22	29	05	Apr										
155	DELDES51008	EC 75221 PH 5 Retension: Develop Project Tm / Kick-Off Mtg	01/15/10 09	01/15/10 11	2	C45100	155 EC 75221 PH 5 Retension: Develop Project Tm / Kick-Off Mtg 01/15/10 09 01/15/10 11																											
156	DELDES51020M	EC 75221 PH 5 Retension: Develop Draft Pkg for Conceptual DRB	01/15/10 11	01/21/10 00	133	C45100	156 EC 75221 PH 5 Retension: Develop Draft Pkg for Conceptual DRB 01/15/10 11 01/21/10 00																											
157	DELDES51600	EC 75221 PH 5 Retension: ID Long Lead material to Procurement	01/20/10 20	01/21/10 00	4	C45100	157 EC 75221 PH 5 Retension: ID Long Lead material to Procurement 01/20/10 20 01/21/10 00																											
158	DELDES51025	EC 75221 PH 5 Retension: Distribute Conceptual DRB Pkg for Review	01/21/10 00	01/21/10 08	8	C45100	158 EC 75221 PH 5 Retension: Distribute Conceptual DRB Pkg for Review 01/21/10 00 01/21/10 08																											
159	DELDES5111M	EC 75221 PH 5 Retension: Develop Final EC "Pkg for final DRB"	01/21/10 00	01/22/10 12	36	C45100	159 EC 75221 PH 5 Retension: Develop Final EC "Pkg for final DRB" 01/21/10 00 01/22/10 12																											
160	DELDES51027	EC 75221 PH 5 Retension: Review Conceptual DRB Pkg	01/21/10 08	01/22/10 08	24	C45100	160 EC 75221 PH 5 Retension: Review Conceptual DRB Pkg 01/21/10 08 01/22/10 08																											
161	DELDES51030	EC 75221 PH 5 Retension: Conceptual DRB Meeting	01/22/10 06	01/22/10 08	2	C45100	161 EC 75221 PH 5 Retension: Conceptual DRB Meeting 01/22/10 06 01/22/10 08																											
162	DELDES5120Z	EC 75221 PH 5 Retension: MILESTONE - Conceptual DRB Mtg Cplt / Waived	01/22/10 08	01/22/10 08	0	C45100	162 EC 75221 PH 5 Retension: MILESTONE - Conceptual DRB Mtg Cplt / Waived 01/22/10 08 01/22/10 08																											
163	DELDES5115M	EC 75221 PH 5 Retension: Mech / Struc - DV	01/22/10 12	01/26/10 12	96	C45100	163 EC 75221 PH 5 Retension: Mech / Struc - DV 01/22/10 12 01/26/10 12																											
164	DELDES5120	EC 75221 PH 5 Retension: Inter-Departmental Reviews	01/22/10 12	01/26/10 12	96	C45100	164 EC 75221 PH 5 Retension: Inter-Departmental Reviews 01/22/10 12 01/26/10 12																											
165	DELDES5190Z	EC 75221 PH 5 Retension: Milestone - Issued for Final Review	01/22/10 12	01/22/10 12	0	C45100	165 EC 75221 PH 5 Retension: Milestone - Issued for Final Review 01/22/10 12 01/22/10 12																											
166	DELDES5117	EC 75221 PH 5 Retension: Incorp Verification Comments	01/26/10 12	01/29/10 13	73	C45100	166 EC 75221 PH 5 Retension: Incorp Verification Comments 01/26/10 12 01/29/10 13																											
167	DELDES5123	EC 75221 PH 5 Retension: Incorp Review Comments	01/26/10 12	01/29/10 13	73	C45100	167 EC 75221 PH 5 Retension: Incorp Review Comments 01/26/10 12 01/29/10 13																											
168	DELDES5125	EC 75221 PH 5 Retension: Supv Review Prior to Final DRB	01/29/10 13	01/29/10 17	4	C45100	168 EC 75221 PH 5 Retension: Supv Review Prior to Final DRB 01/29/10 13 01/29/10 17																											
169	DELDES5125D	EC 75221 PH 5 Retension: Distrib Final DRB Pkg for Review	01/29/10 17	01/29/10 18	1	C45100	169 EC 75221 PH 5 Retension: Distrib Final DRB Pkg for Review 01/29/10 17 01/29/10 18																											
170	DELDES5125R	EC 75221 PH 5 Retension: Review Final DRB Pkg	01/29/10 18	01/30/10 18	24	C45100	170 EC 75221 PH 5 Retension: Review Final DRB Pkg 01/29/10 18 01/30/10 18																											
171	DELDES51205	EC 75221 PH 5 Retension: Final DRB Meeting	01/30/10 18	01/30/10 20	2	C45100	171 EC 75221 PH 5 Retension: Final DRB Meeting 01/30/10 18 01/30/10 20																											

Legend:	Milestones	In-Progress	Activity	
	◆	▬	▬	

December 28, 2009 06:19:19 AM


CR3 Outage Containment Repair Project - Level 3 Schedule

Row	Activity	Description	Early Start	Early Finish	Rem Dur	WBS	Schedule																														
							Dec 21	28	04	11	18	25	01	08	15	22	01	08	15	22	29	05	Mar	01	08	15	22	29	05	Apr	01	08	15	22	29	05	
172	DELDES51215	EC 75221 PH 5 Retension: Incorporate Final DRB Comments	01/30/10 20	01/31/10 20	24	C45100																													172 EC 75221 PH 5 Retension: Incorporate Final DRB Com 01/30/10 20 01/31/10 20		
173	DELDES51220	EC 75221 PH 5 Retension: Obtain Supervisor Approval	01/31/10 20	02/01/10 04	8	C45100																														173 EC 75221 PH 5 Retension: Obtain Supervisor Approval 01/31/10 20 02/01/10 04	
174	DELDES5130Z	EC 75221 PH 5 Retension: MILESTONE - All Reviews Complete	01/31/10 20	01/31/10 20	0	C45100																														174 EC 75221 PH 5 Retension: MILESTONE - All Reviews C 01/31/10 20 01/31/10 20	
175	DELDES51225	EC 75221 PH 5 Retension: Obtain PGM Approval	02/01/10 04	02/02/10 04	24	C45100																														175 EC 75221 PH 5 Retension: Obtain PGM Approval 02/01/10 04 02/02/10 04	
176	DELDES5140Z	EC 75221 PH 5 Retension: MILESTONE - PGM Approval	02/02/10 04	02/02/10 04	0	C45100																														176 EC 75221 PH 5 Retension: MILESTONE - PGM Approv 02/02/10 04 02/02/10 04	
177	DELDES51710	EC 75221 PH 5 Retension: Planning Prepare EC Work Packages	02/02/10 04	02/05/10 04	72	C47100																														177 EC 75221 PH 5 Retension: Planning Prepare EC Work P 02/02/10 04 02/05/10 04	
Containment Repair Specification Design																																					
179	DELDES016	-Develop EC-ED 75309 For Concrete & Rebar	11/18/09 07	12/31/09 19	125	C45100																														179 -Develop EC-ED 75309 For Concrete & Rebar 11/18/09 07 12/31/09 19	
180	DELDES016M	EC-ED 75309 For Concrete & Rebar Compl MILESTONE	12/31/09 19	12/31/09 19	0	C45100																														180 EC-ED 75309 For Concrete & Rebar Compl MILESTONE 12/31/09 19 12/31/09 19	
181	DELDES000M	Specification Design Complete MILESTONE	12/31/09 19	12/31/09 19	0	C45100																														181 Specification Design Complete MILESTONE 12/31/09 19 12/31/09 19	
Containment Repair Contracting / Subcontracting / Procurement																																					
183	DELCONL1M	Contracting/Subcontracting/Procurement Complete MILESTONE	01/29/10 17	01/29/10 17	0	C51400																														183 Contracting/Subcontracting/ Procurement Complete MILE 01/29/10 17 01/29/10 17	
Containment Repair EPC Contract																																					
185	DELCON23	-Develop Contract SGT	12/04/09 07	01/05/10 15	56	C15100																														185 -Develop Contract SGT 12/04/09 07 01/05/10 15	
186	DELCON26	Contract Mailed to SGT for signature	01/05/10 15	01/05/10 15	0	C15100																															186 Contract Mailed to SGT for signature 01/05/10 15 01/05/10 15
187	DELCON29	Execute Contract & Receive Signed Contract From SGT	01/06/10 07	01/07/10 15	16	C15100																															187 Execute Contract & Receive Signed Contract From SGT 01/06/10 07 01/07/10 15
188	DELCON31	SGT Contract In Place	01/07/10 15	01/07/10 15	0	C15100																															188 SGT Contract In Place 01/07/10 15 01/07/10 15
Containment Repair Subcontracting																																					
190	DELCON09M	Award Hydro-Demolition Contract Compl MILESTONE	12/26/09 14	12/26/09 14	0	C52410																														190 Award Hydro-Demolition Contract Compl MILESTON 12/26/09 14 12/26/09 14	

Row	Activity	Description	Early Start	Early Finish	Rem Dur	WBS	Schedule																													
							Dec 21	28	04	11	18	25	01	08	15	22	01	08	15	22	29	05	Mar	01	08	15	22	29	05	Apr	01	08	15	22	29	05

December 28, 2009 06:19:19 AM

CR3 Outage Containment Repair Project - Level 3 Schedule

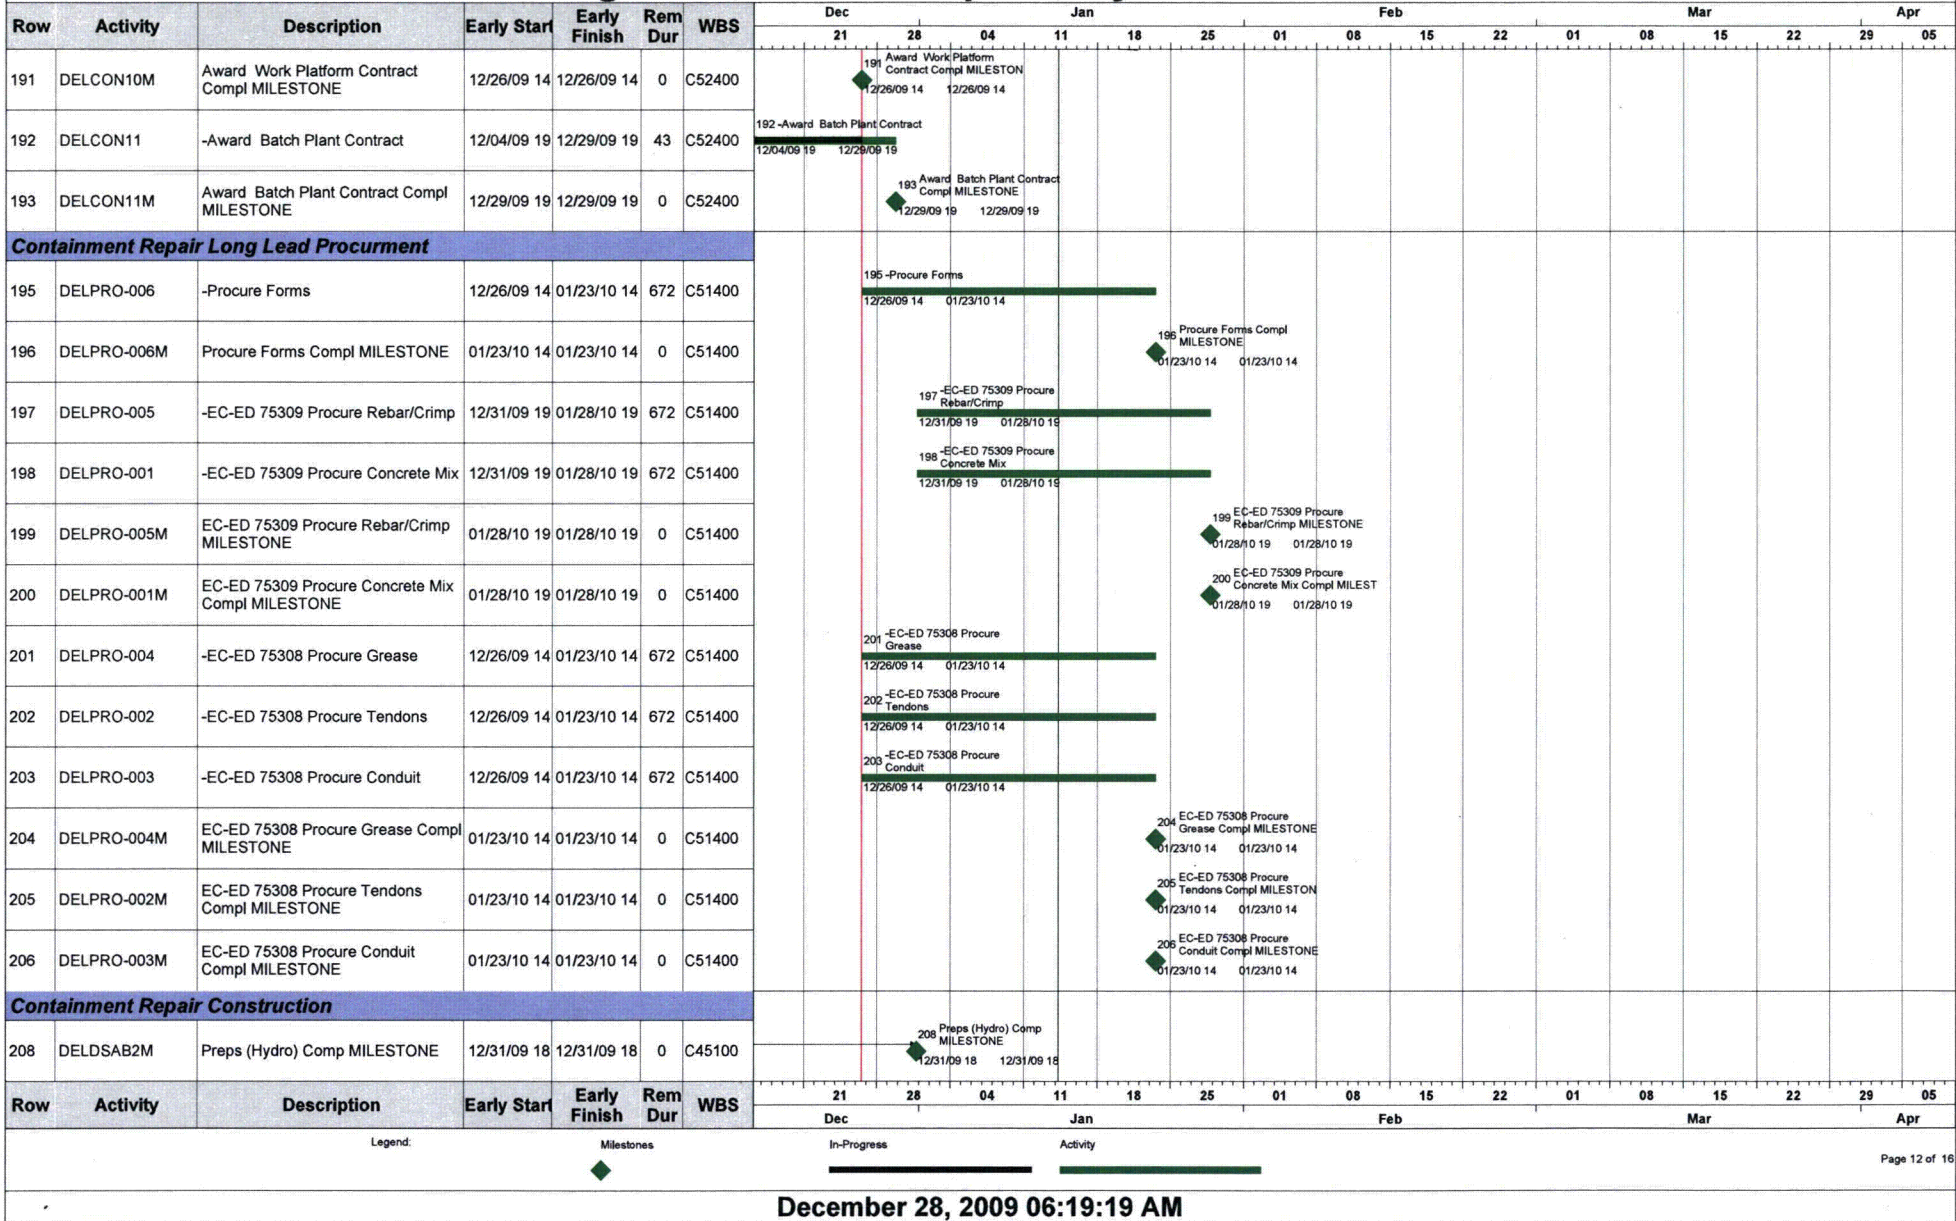

CR3 Outage Containment Repair Project - Level 3 Schedule

Row	Activity	Description	Early Start	Early Finish	Rem Dur	WBS	Gantt Chart																											
							Dec				Jan					Feb						Mar				Apr								
							21	28	04	11	18	25	01	08	15	22	01	08	15	22	29	05	12	19	26	03	10	17	24	31				
209	DELDSAB3M	Preps (Placement) Comp MILESTONE	01/07/10	01/07/10	0	C45100	<div style="text-align: center;"> <small>209 Preps (Placement) Comp MILESTONE</small> </div>																											
210	DELDSAB1M	Preps (Stablization, Hydro, Placement, Detensioning, Tensioning) Comp MILESTONE	01/15/10	01/15/10	0	C45100	<div style="text-align: center;"> <small>210 Preps (Stablization, Hydro, Placement, Detensioning, Tensioning) Comp MILESTONE</small> </div>																											
211	DELDSAB4M	Preps (Detensioning) Comp MILESTONE	01/15/10	01/15/10	0	C45100	<div style="text-align: center;"> <small>211 Preps (Detensioning) Comp MILESTONE</small> </div>																											
212	DELRPI-0030	EC 74801: Remove 8 Displacement Gauges In S/G Opening & 2 in two 4" Cores 51&81A	02/19/10	02/19/10	12	C51400	<div style="text-align: center;"> <small>212 EC 74801: Remove 8 Displacement Gauges In S/G</small> </div>																											
213	DELRPI-0031	EC 74801: Remove 22 Strain Gauges In Five 8" Cores 6AA, 30, 57A, 84A & 92	02/20/10	02/20/10	12	C51400	<div style="text-align: center;"> <small>213 EC 74801: Remove 22 Strain Gauges In Five 8"</small> </div>																											
214	DELRPI-0025	EC 74801: Dome: GPR, Prep, Form & Grout Repair at 7 Core Drill Locations	02/22/10	02/23/10	24	C51400	<div style="text-align: center;"> <small>214 EC 74801: Dome: GPR, Prep, Form & Grout Repair</small> </div>																											
215	DELRPI-123A	EC 74801: Non-Delam Bays 5-6: GPR, Prep, Form & Grout Repair at 9 Core Locations	02/23/10	02/24/10	36	C51400	<div style="text-align: center;"> <small>215 EC 74801: Non-Delam Bays 5-6: GPR, Prep, Form &</small> </div>																											
216	DELRPI-0026	EC 74801: Dome: Strip Forms at 7 Grout Repair Locations	02/24/10	02/24/10	6	C51400	<div style="text-align: center;"> <small>216 EC 74801: Dome: Strip Forms at 7 Grout Repair Loc</small> </div>																											
217	DELRPI-121A	EC 74801: Non-Delam Bays 4-5: GPR, Prep, Form & Grout Repair at 9 Core Locations	02/24/10	02/26/10	36	C51400	<div style="text-align: center;"> <small>217 EC 74801: Non-Delam Bays 4-5: GPR, Prep, Form &</small> </div>																											
218	DELRPI-123B	EC 74801: Non-Delam Bays 5-6: Strip Forms at 9 Grout Repair Locations	02/25/10	02/25/10	6	C51400	<div style="text-align: center;"> <small>218 EC 74801: Non-Delam Bays 5-6: Strip Forms at 9 Grout</small> </div>																											
219	DELRPI-124A	EC 74801: Non-Delam Bays 6-1: GPR, Prep, Form & Grout Repair at 16 Core Location	02/26/10	02/28/10	60	C51400	<div style="text-align: center;"> <small>219 EC 74801: Non-Delam Bays 6-1: GPR, Prep, Form &</small> </div>																											
220	DELRPI-121B	EC 74801: Non-Delam Bays 4-5: Strip Forms at 9 Grout Locations	02/27/10	02/27/10	6	C51400	<div style="text-align: center;"> <small>220 EC 74801: Non-Delam Bays 4-5: Strip Forms at 9 Grout</small> </div>																											
221	DELRPI-125A	EC 74801: Non-Delam Bays 1-2: GPR, Prep, Form & Grout Repair at 5 Core Locations	02/28/10	03/01/10	24	C51400	<div style="text-align: center;"> <small>221 EC 74801: Non-Delam Bays 1-2: GPR, Prep, Form &</small> </div>																											
222	DELRPI-124B	EC 74801: Non-Delam Bays 6-1: Strip Forms at 16 Grout Repair Locations	03/01/10	03/01/10	12	C51400	<div style="text-align: center;"> <small>222 EC 74801: Non-Delam Bays 6-1: Strip Forms at 16 Grout</small> </div>																											
223	DELRPI-120A	EC 74801: Non-Delam Bays 2-3: GPR, Prep, Form & Grout Repair at 8 Core Locations	03/01/10	03/03/10	36	C51400	<div style="text-align: center;"> <small>223 EC 74801: Non-Delam Bays 2-3: GPR, Prep, Form &</small> </div>																											
224	DELRPI-125B	EC 74801: Non-Delam Bays 1-2: Strip Forms at 5 Grout Repair Locations	03/02/10	03/02/10	6	C51400	<div style="text-align: center;"> <small>224 EC 74801: Non-Delam Bays 1-2: Strip Forms at 5 Grout</small> </div>																											
225	DELRPI-0004	EC 74801: Delam Bays 3-4: GPR, Prep, Form & Grout Repair at 19 Core Locations	03/03/10	03/05/10	60	C51400	<div style="text-align: center;"> <small>225 EC 74801: Delam Bays 3-4: GPR, Prep, Form & Grout</small> </div>																											

Legend:

Milestones


In-Progress

Activity



December 28, 2009 06:19:19 AM

CR3 Outage Containment Repair Project - Level 3 Schedule

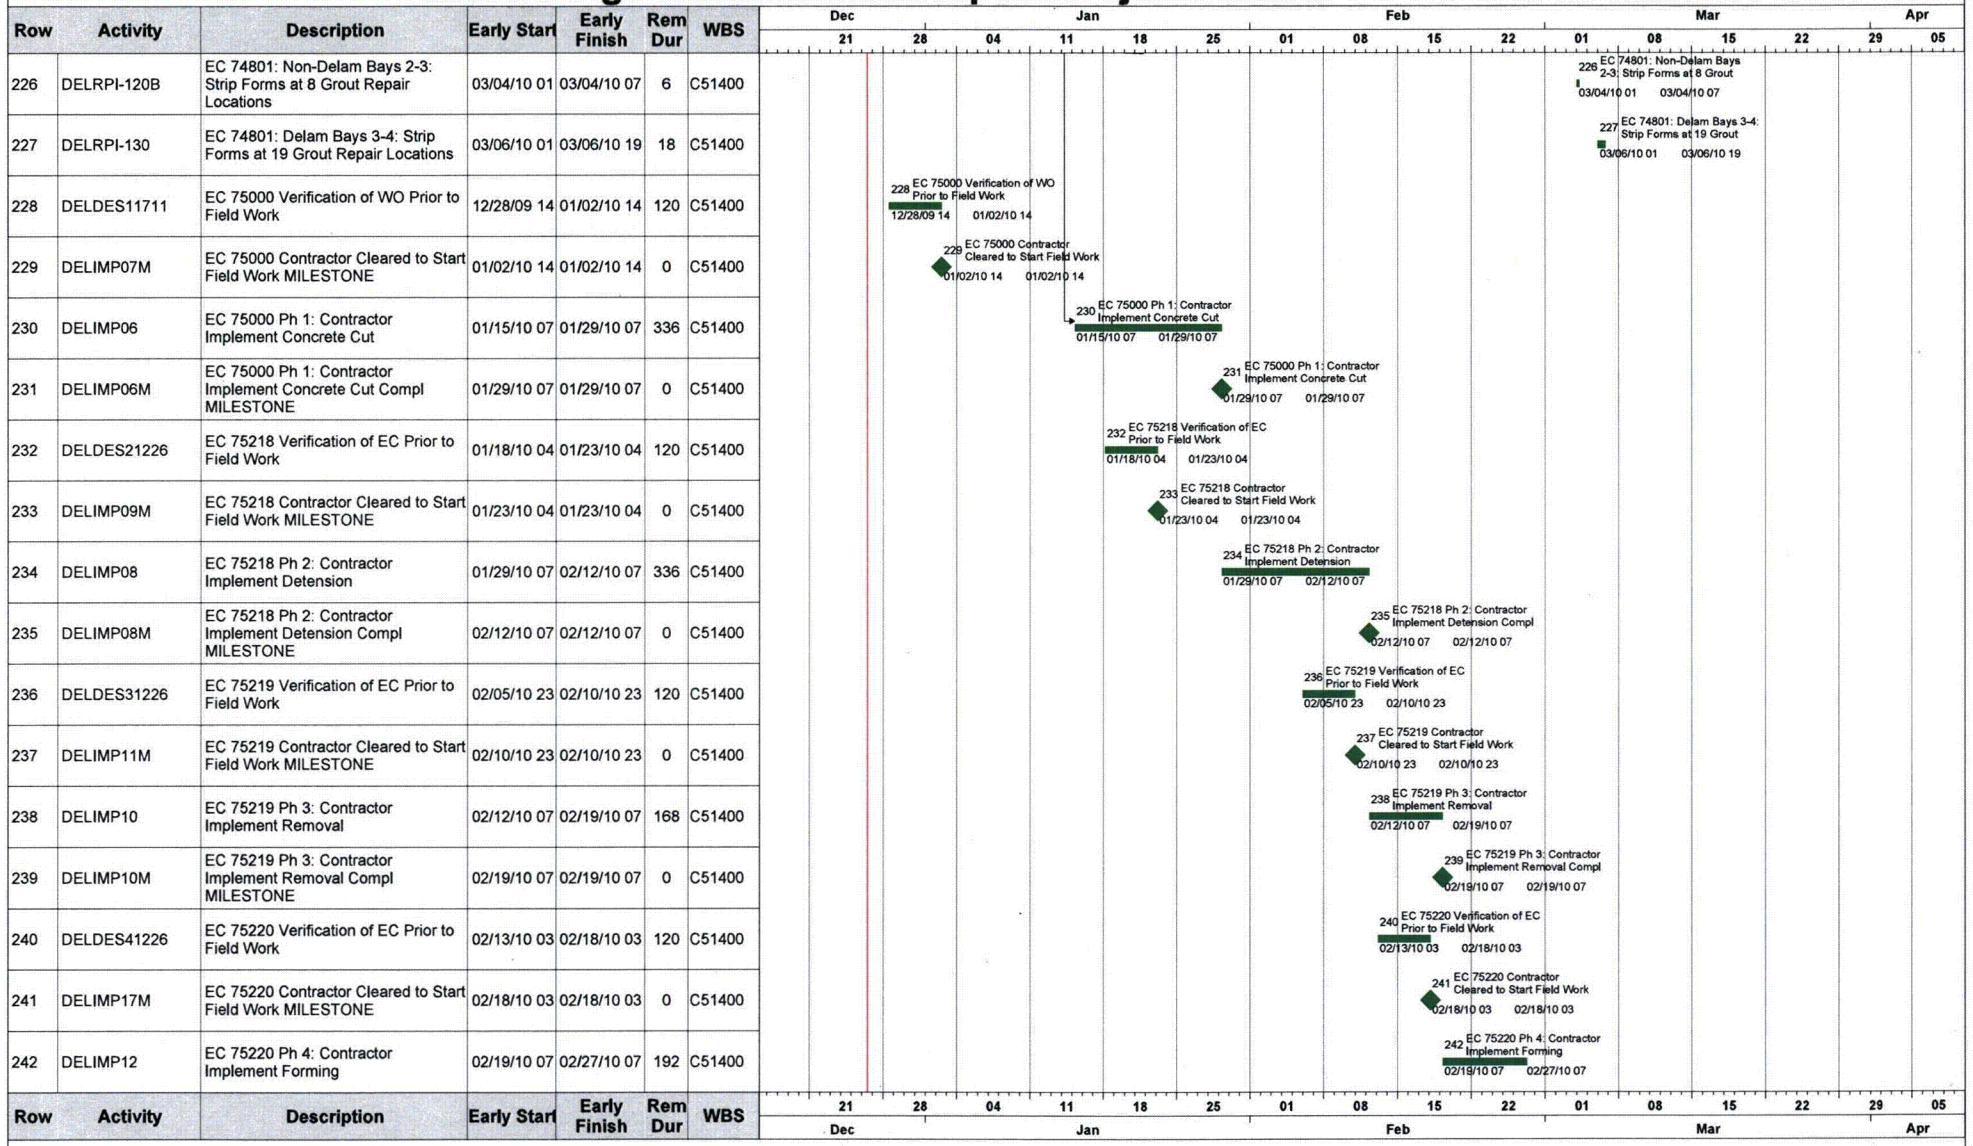

Legend:

Milestones

In-Progress

Activity

December 28, 2009 06:19:19 AM

CR3 Outage Containment Repair Project - Level 3 Schedule

Row	Activity	Description	Early Start	Early Finish	Rem Dur	WBS	Dec							Jan							Feb							Mar							Apr				
							21	28	04	11	18	25	01	08	15	22	29	05	12	19	26	02	09	16	23	30	06	13	20	27	04	11	18	25	01	08	15	22	29
243	DELIMP12M	EC 75220 Ph 4: Contractor Implement Forming Compl MILESTONE	02/27/10 07	02/27/10 07	0	C51400																																	
244	DELIMP14	EC 75220 Ph 4: Contractor Implement Placement	02/27/10 07	03/09/10 07	240	C51400																																	
245	DELIMP16	EC 75220 Ph 4: Contractor Implement Cure	03/09/10 07	03/12/10 07	72	C51400																																	
246	DELIMP14M	EC 75220 Ph 4: Contractor Implement Placement Compl MILESTONE	03/09/10 07	03/09/10 07	0	C51400																																	
247	DELIMP16M	EC 75220 Ph 4: Contractor Implement Cure Compl MILESTONE	03/12/10 07	03/12/10 07	0	C51400																																	
248	DELDES51226	EC 75221 Verification of EC Prior to Field Work	02/02/10 04	02/07/10 04	120	C45100																																	
249	DELCLOL2M	EC 75221 Contractor Cleared to Start Field Work MILESTONE	02/07/10 04	02/07/10 04	0	C45100																																	
250	DELIMP18	EC 75221 Ph 5: Contractor Implement Tension	03/12/10 15	03/21/10 15	216	C51400																																	
251	DELCLO06	Containment Repair Project Contracts Closure	03/21/10 15	03/28/10 03	156	C82100																																	
252	DELIMP20	Demob Containment Repair Project	03/21/10 15	03/28/10 15	168	C75100																																	
253	DELIMP18M	EC 75221 Ph 5: Contractor Implement Tension Compl MILESTONE	03/21/10 15	03/21/10 15	0	C51400																																	
254	DELIMPL1M	Contractor Implement Construction Complete MILESTONE	03/21/10 15	03/21/10 15	0	C51400																																	
255	DELCLO03	EC Closure	03/23/10 15	03/26/10 23	80	C81100																																	
256	DELCLOL1M	Project Closeout Complete MILESTONE	03/28/10 15	03/28/10 15	0	C81000																																	
Containment Repair Testing																																							
258	DELTST06	Perform Concrete Scan / Boring	03/21/10 15	03/23/10 15	48	C68100																																	
259	DELTST03	Interface Perform ILRT Test	03/21/10 15	03/23/10 15	48	C68100																																	

December 28, 2009 06:19:19 AM

CR3 Outage Containment Repair Project - Level 3 Schedule

Row	Activity	Description	Early Start	Early Finish	Rem Dur	WBS	Gantt Chart Timeline																						
							Dec							Jan							Feb							Mar	
							21	28	04	11	18	25	01	08	15	22	01	08	15	22	29	05							
260	DELTSTL1M	Interface Testing/ILRT Complete MILESTONE	03/23/10 15	03/23/10 15	0	C68100	[Timeline visualization: Milestone diamond on 03/23/10 15]																						
261	DELCLOL12M	Interface Plant Start-up Complete MILESTONE	03/30/10 15	03/30/10 15	0	C68100	[Timeline visualization: Milestone diamond on 03/30/10 15]																						
Containment Repair Plant Startup & Testing																													
263	DELIMP2-0000	Interface Startup to Mode 4	03/23/10 15	03/25/10 15	48	C68100	[Timeline visualization: Activity bar from 03/23/10 15 to 03/25/10 15]																						
264	DELCL00-0000	Interface Startup to Mode 1/On-line	03/25/10 15	03/30/10 15	120	C68100	[Timeline visualization: Activity bar from 03/25/10 15 to 03/30/10 15]																						

Row	Activity	Description	Early Start	Early Finish	Rem Dur	WBS	Gantt Chart Timeline																													
							Dec							Jan							Feb							Mar							Apr	
							21	28	04	11	18	25	01	08	15	22	01	08	15	22	29	05														

Legend:

Milestones

In-Progress

Activity

December 28, 2009 06:19:19 AM
