
August 2019 MCCCH Construction Small Business Dashboard



Glossary: MBE—Minority-Owned Business, WBE—Women-Owned Business, ESB—Emerging Small Business, SDV - Service Disabled Veteran


*Represents adjusted GMP construction value Cumulative Construction Data from 10/31/2016 to 8/31/2019

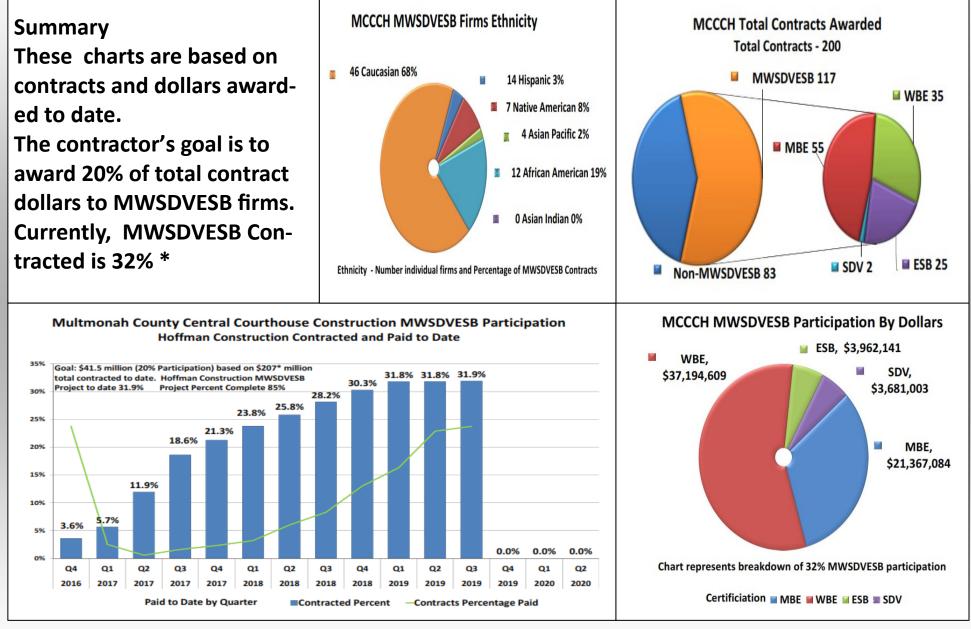

August 2019 MCCCH Construction Workforce Dashboard

Project Summary

- Total Project Apprenticeship to date is 30%
- Project Goal is 20% apprenticeship by trade
- Project Total minority male participation is 26.6% and female is 10.2%
- Project Percent Complete 82%

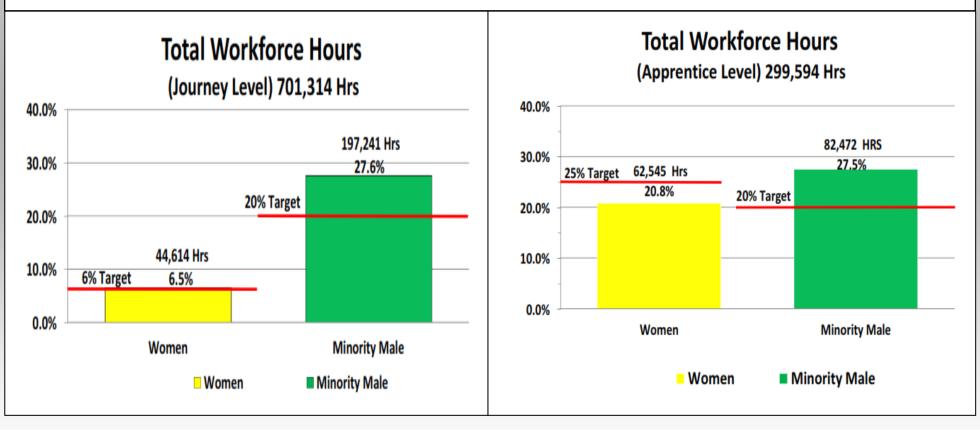


Cumulative Construction Data from 10/31/2016 to 8/31/2019

WTHP Participation for minority men and all women for apprentice and journey levels in accordance with the PLA.



Construction Workforce Dashboard

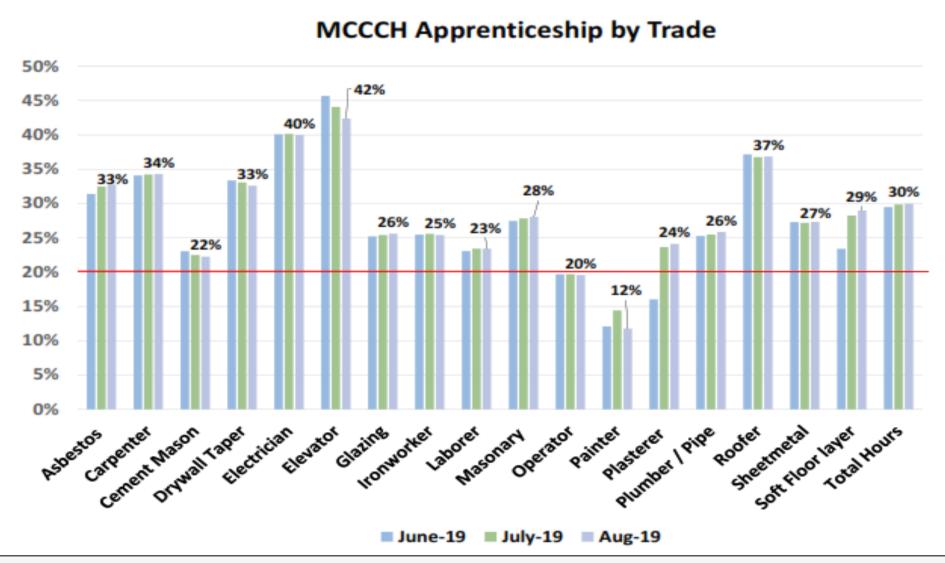


Cumulative Construction Data from 10/31/2016 to 8/31/2019 WTHP Participation for minority men and all women for apprentice and journey levels in accordance with the PLA.



Construction Workforce Dashboard

MCCCH Minority Male Journey & Apprenticeship by Trade Hours

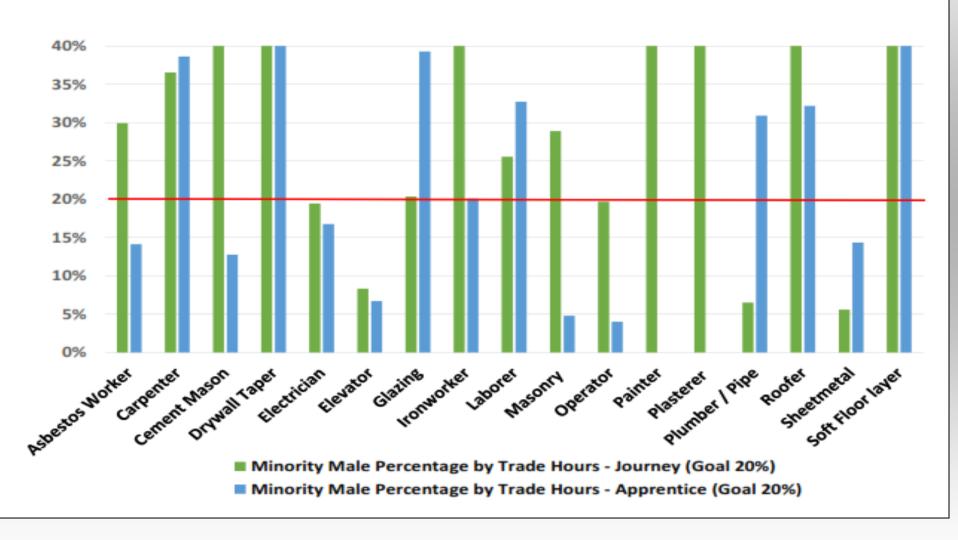


Cumulative Construction Data from 10/31/2016 to 8/31/2019 WTHP Participation for minority men and all women for apprentice and journey levels in accordance with the PLA.



Construction Workforce Dashboard



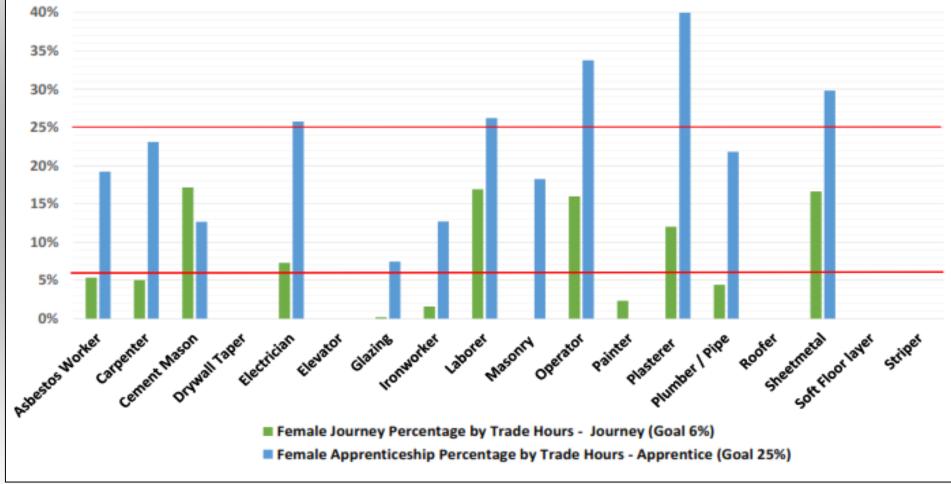


Cumulative Construction Data from 10/31/2016 to 8/31/2019 WTHP Participation for minority men and all women for apprentice and journey levels in accordance with the PLA.



Construction Workforce Dashboard

Project Summary–

- Exceeding MWSDVESB and Overall Apprenticeship Goal
- 350+ Workers Daily Diversity is Consistent
- Bid Package Buyout is Complete
- Existing MWSDVESB Subcontracts Growing
- Project Percent Complete 82%

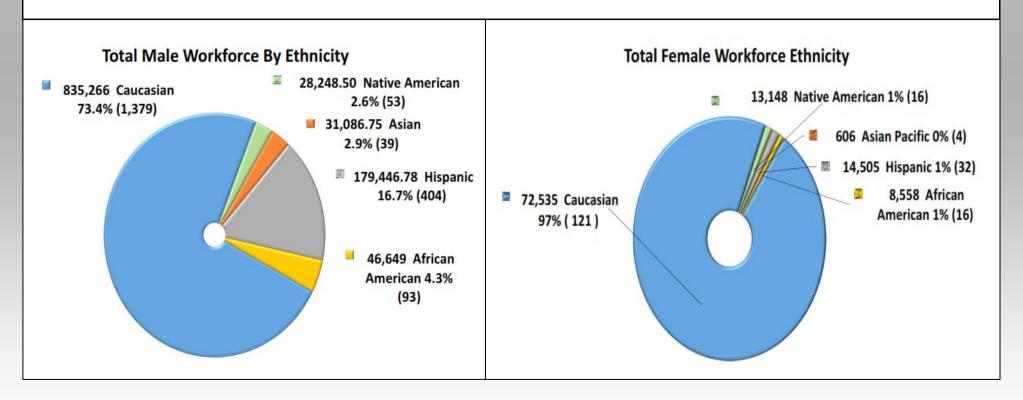



August 2019 MCCCH Construction MWSDVESB Actual vs Forecast Percentage Project Percent Complete 82%

