


Point Beach Nuclear Plant U1R28 Refueling Outage

Safety Topics for week of April 25-May 1
Theme for the week
This week's theme is Teamwork & Attitude . Good teamwork and attitude will help us complete this outage successfully!
Daily Safety Snippets
Sunday
"Sure safety can get old, but so do safe workers" A part of having a good safety attitude is never letting your guard down. Even when you are just walking around the plant, an injury is just a door slam away.
Monday
"When we're all on the same team problems aren't as big as they seem" Is your job going to be delayed by 30 minutes? Who are you going to call for help? The OCC. They can help you solve issues.
Tuesday
"Surprises belong at birthday parties not in the shop." OE17571 Braidwood It was discovered that shop personnel were grinding aluminum stock on the shop bench grinder. What's wrong with that? Aluminum flakes can adhere to the wheel, causing it to become unbalanced. Also the flakes thermally expand faster than the rest of the wheel. The potential result? A wheel fracture and that is a surprise you don't need!
Wednesday
"Teamwork by all, helps make accident rates fall" Over the last few weeks we have added many new team members to our staff. It is each of our responsibility's to coach them on the way we do business around here... SAFELY! Nothing can stop the entire organization faster than a serious injury.
Thursday
"No matter what the season, covers are in place for a reason." Do you know why quartz halogen lights have glass covers? The temperatures reached by the portable halogen floodlights may exceed 1000F. OE17708 1/6/04 Plant Hatch declared an unusual event as the result of a small fire. The fire started by hot fragments of glass blown from a halogen lamp. The cover was not in place and the resulting fragments started the fire.
Friday
"Use your head and stay alert, it keeps you from getting hurt" OE17764 Limerick On 2/3/04 an electrician received a shock on a GFCI protected line. Why did this happen? The worker failed to ensure GFCI reset properly after testing. Do you check your GFCI prior to use to make sure it is working right?
Saturday
"Safety is a six letter word but a seven day job" Remember to not let your guard down as you leave work for the day. Last week there were numerous AR s on inappropriate driving in the parking lot. Watch out for your coworker.



Point Beach Nuclear Plant Outage 1R28

DAY 24

Path



Picture

Meets



Doesn't Meet Exceeds

Supporting Operational Excellence

Outage Radiation Performance

Definition/Goal

This indicator measures cumulative dose radiation exposure and total number of personnel-contamination events (PCE's > 5000 cpm) during refueling outages. The dose indicator is measured in Rem and individual PCE events.

Analysis and Actions

Day 24 - April 27
 Actual = 1.799
 Cumulative = 42.074
 Cumulative Forecast = 43.488

Daily dose and PCE goals reforecasted on 4/23.


Meets:	<=75 Rem	Actual Cum.	
Exceeds:	<=71 Rem	Dose:	42.074 Rem
Meets: <= 18	Exceeds: <= 12	Actual PCE's:	6

Responsible Manager/Owner


Stu Thomas

3

Personnel Contamination Events

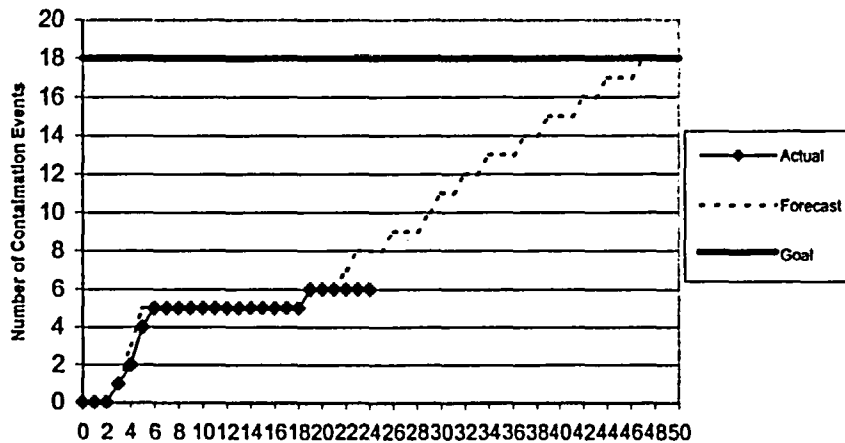

Cummulative Dose Exposure

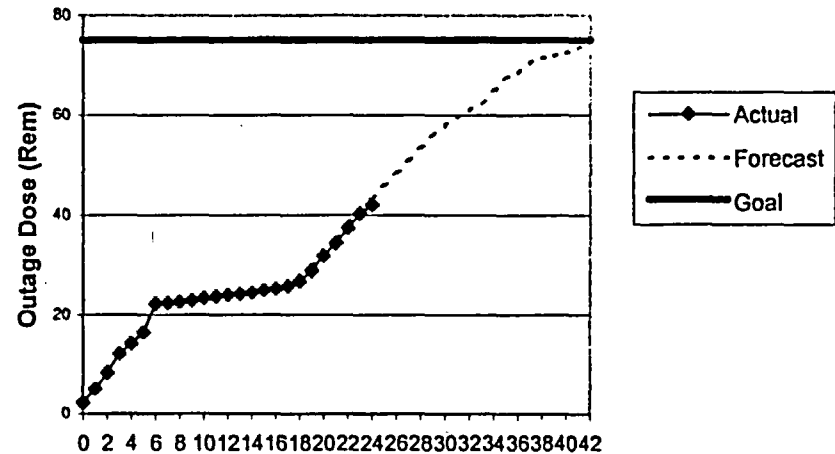

Outage Status Report

(228 of 464)

Plant: Point Beach Unit 1 Day: Wednesday Today's Date / Time: 4/28/04 1600

Outage Duration: Day 25 of Refueling Outage Number U1R28

Safety Status

Industrial - Within the last 12 hours

OSHA Recordables 0 First Aid cases 2 Significant near misses 1
Total for this outage 1 Circ Water Pump House Floor Cover Left Open.

Summary: Employee received cut to finger due to a defective chair. Band-aid applied.
Employee received a prick to a finger while turning a valve. Band-aid applied.

Radiological

Dose to date 42.074 Projected to date * 43.488 Outage Goal ≤75 R
Difference -1.414 Number of PCEs 6

Summary: * Reforecast on 4/23

Nuclear

Significant human performance errors and events in last 24 hours 0

Summary:

Plant Status

Mode: Hot Standby (Mode 3) Hot Shutdown (Mode 4) Cold Shutdown (Mode 5) Refueling Shutdown (Mode 6)
RCS: Temperature: 76 Pressure: Vented to Atmosphere RV Level: Refueling Height
Time to Boil: 25.5 hours et4

Shutdown Safety Assessment Protected Equipment:

HEAD 23 ANALYSIS
27 DATA ACQUIRED

Major Activities Completed in Last 24 Hours

- A S/G Sludge Lancing
- Continued Fuel Motion at Step 211 of 464 @ 1510 4/28/04

Critical Path and Near Critical Path Activities (Next 24 Hours)

- Continue Fuel Motion
- A and B S/G Eddy Current
- Continue Reactor Vessel Head Inspection
- B RCP Motor Work
- Remove 1X04 Low Voltage Station Transformer from Service
- Install S/G Handholes & Place in Wet Lay-up

Significant Outstanding Issues

Date	Issue	Due	Responsibility
4/03/04	Repair Blowdown Tank Leakage	4/30/04	Scott Manthei
4/04/04	1P2A Charging Pump Troubleshooting	4/30/04	Clay Hill
4/25/04	B RCP Motor Oil	5/10/04	Rick Repshas

Upcoming Major Milestones

	Scheduled		Actual			Scheduled		Actual	
	Date	Time	Date	Time		Date	Time	Date	Time
Cooldown <200°	4/03/04	2100	4/03/04	2230	RCS Fill & Vent	4/23/04	1500		
Head Lift	4/09/04	0900	4/21/04	1550	Heatup >200°	4/25/04	0900		
Refueled	4/14/04	0300			Reactor Critical	4/28/04	0800		
RV Headset	4/18/04	1900			On-Line	4/30/04	0100		

Point Beach Nuclear Plant
PBNP SHUTDOWN SAFETY ASSESSMENT AND FIRE CONDITION CHECKLIST
OUTAGE SAFETY ASSESSMENT

UNIT: 1

DATE: April 28, 2004

TIME: 1420

KEY SAFETY FUNCTIONS:

REACTIVITY:	YELLOW
CORE COOLING:	YELLOW
POWER AVAILABLE:	GREEN
INVENTORY:	GREEN
CONTAINMENT:	YELLOW
SFP COOLING:	GREEN

COMMENTS:

RCS Time to Boil is 25.5 hours
SFP Time to Boil is 21 hours (full core off-load is assumed)
Fire Protection Condition IV: Credit is taken for fire rounds as fire prevention contingency

ex 4

Defined Critical Path

U	ID	DESCRIPTION	OD	RD	Cal	U	SYS	EQID	TF	APR		
										28	29	30
										4, 6, 8, 10, 12, 14, 16, 18, 20, 22	0, 2, 4, 6, 8, 10, 12, 14, 16, 18, 20, 22	0, 2, 4, 6, 8, 10, 12, 14, 16, 18, 20, 22
25APR04 00:00										25APR04 00:00		
1	RP1C-030	FUEL MOTION AND INSERT SHUFFLE	96	53	1	1	FH	O-RP-001C	0	RP1C-030	FUEL MOTION AND INSERT SHUFFLE	30APR04 16
28APR04 00:00										28APR04 00:00		
1	EM0216638	START REPAIRS FOR P-1B HIGH BREAKAWAY	60	50	1	1	RC	P-001B-M	0	EM0216638	START REPAIRS FOR P-1B HIGH BREAKAWAY	0301756 - 30APR
30APR04 00:00										30APR04 00:00		
1	BRCP-DIS1	P-1B-M CONTINUE DISASSEMBLY OF MOTOR	48	48	1	1	RC	P-001B-M	0		BRCP-DIS1	P-1B-M CONTINUE DISASSEMBLY OF MOTOR 0301756 - 02MAY04 13:59 30APR04 14:00
1	T-6929-H	1 125V IWP 00-037-02 EM REV0-1	1	1	1	1	125V	D72-16-08	0		T-6929-H	1 125V IWP 00-037-02 EM REV0-1 0016929 - 30APR04 17:59 30APR04 17:00

Run Date

28APR04 13:57

LT-16 DEFINED CRITICAL PATH
FL-16 DEFINED CRITICAL PATH SET

Sheet 1 of 1

after 28APR04 12:00

U1R28 WORKING SCHEDULE

after 28APR04 12:00

#	U	ID	RESP	WO ST	EQID	DESCRIPTION	RD	ES	EF	RISK	MF	APR						
												Wed 28	Thu 29	Fri 30		Sat 01		
												3,10,12,14,16,18,20,22	0, 2, 4, 6, 8, 10,12,14,16,18,20,22	0, 2, 4, 6, 8, 10,12,14,16,1				
ADMINISTRATIVE SERVICES												ADM						
1	1	NRC-CALL-9	ADM		MILESTONE	O.D. CALL NRC TO WITNESS CORE MAPPING	1	30APR04 14:00	30APR04 14:59	DR-Y ML-Y ORT3-Y R-N	0							NRC-CALL-9 O.D. CA
APPLETON METERING GROUP												APM						
2	1	AP0215130	APM	76	X-02	INSPECT CAL AND SET X-02	9	28APR04 08:00A	29APR04 11:59	DR-N ML-N ORT3-N R-N	84	AP0215130	INSPECT CAL AND SET X-02					UNIT AUXILIARY TRANSFORMER 0215130
3	1	AP0216645	APM	76	E-02	1E-02 ASSIST EM WITH MEL CHECK-OUT	8	28APR04 20:00*	29APR04 03:59	DR-N ML-N ORT3-N R-N	84	AP0216645	1E-02 ASSIST EM WITH MEL CHECK-OUT					TG-01 TG VOLTAGE REGULATOR/EXCITATION EQUIPMENT
4	1	AP0215127	APM	76	X-01-A	INSPECT CAL AND SET X-01-A	16	29APR04 08:00*	30APR04 14:59	DR-N ML-N ORT3-N R-N	47	AP0215127	INSPECT CAL AND SET X-01-A					MAIN
APPLETON RELAY GROUP												APR						
5	1	AP0306103	APR	76	102-1/TG-0	APR RETEST (102-1/TG01 REPLACE PROT RELAYS)	40	28APR04 12:00	02MAY04 15:59	DR-N ML-N ORT3-N R-N	0	AP0306103	APR RETEST (102-1/TG01 REPLACE PROT RELAYS)					
6	1	AP0306104	APR	76	102-2/TG-0	APR RETEST (102-2/TG-01 R&R GEN PROT RELAYS) PT1	40	28APR04 12:00	02MAY04 15:59	DR-N ML-N ORT3-N R-N	0	AP0306104	APR RETEST (102-2/TG-01 R&R GEN PROT RELAYS) PT1					
7	1	AP0215115	APR	76	A-01	CAL 1A-01 NON-TECH SPEC RCP RELAYS	10	30APR04 13:00	01MAY04 13:59	DR-N ML-N ORT3-N R-N	0							AP0215115 CAL 1A-0 0215115
APPLETON STATION GROUP												APS						
8	0	L121DOS2	APS		F52-121	LINE 121 OUT OF SERVICE "SECOND TIME"	80*	26APR04 06:00A	01MAY04 19:59	DR-N ML-N ORT3-N R-N	0	L121	DOS2 LINE 121 OUT OF SERVICE "SECOND TIME"					
9	0	L121APS	APS		F52-121	APS INSTALL LINE 121 STRUCTURES	75	26APR04 08:00A	01MAY04 14:59	DR-N ML-N ORT3-N R-N	0	L121	APS APS INSTALL LINE 121 STRUCTURES					
10	1	AP0400600	APS	76	X-04	1X-4 REMOVE SEALING MATERIAL	3	29APR04 08:00*	29APR04 10:59	DR-Y ML-Y ORT3-N R-N	21	AP0400600	1X-4 REMOVE SEALING MATERIAL					LOW VOLTAGE STATION AUXILIARY TRANSFORMER
11	1	AP0305025A	APS	76	X-04	PERFORM CABLE DETERM	5	30APR04 08:00	30APR04 12:59	DR-N ML-N ORT3-N R-N	0	AP0305025A	PERFORM CABLE DETERM					LOW VOL
12	1	AP0400838	APS	76	X-04	1X-04 OIL SEEPAGE (CONTINGENCY W/O)	6	30APR04 08:00	30APR04 13:59	DR-N ML-N ORT3-N R-N	10	AP0400838	1X-04 OIL SEEPAGE (CONTINGENCY W/O)					LOW VC
13	1	AP0305025	APS	76	X-04	PERFORM DOBLE TEST	5	30APR04 13:00	01MAY04 08:59	DR-N ML-N ORT3-N R-N	0	AP0305025	PERFORM DOBLE TEST					
CONSTRUCTION ENGINEERING GROUP												CE						
14	0	CE0400801	CE	77	SERVICE	FLAMMABLE STORAGE LOCKER INSPECTION	4	30APR04 08:00*	30APR04 11:59	DR-Y ML-Y ORT3-Y R-N	661	CE0400801	FLAMMABLE STORAGE LOCKER INSPECTION					MISC EQUI
CONSTRUCTION ENG - K. GRASSO												CE1						
15	0	CE0306041	CE1	76	INTAKE CRI	INSPECT CRIB, INSTALL BUOYS AND FISH	30	05APR04 10:00A	01MAY04 16:59	DR-Y ML-Y ORT3-Y R-N	220	CE0306041	INSPECT CRIB, INSTALL BUOYS AND FISH					
16	1	CEDVINSP	CE1	76	CW	UNDERWATER INSPECTION OF CIRC WATER	8	21APR04 09:00A	29APR04 15:59	DR-Y ML-Y ORT3-N R-N	0	CEDVINSP	UNDERWATER INSPECTION OF CIRC WATER					CW SYSTEM MULTI AND/OR NON-NUMBER

Run Date

28APR04 13:44

LT-03 STANDARD PUBLICATION
FL-03 Execution Publication Set

Sheet 1 of 30

U1R28 WORKING SCHEDULE

#	U	ID	RESP	WO ST	EQID	DESCRIPTION	RD	ES	EF	RISK	MF	APR		
												Wed 28	Thu 29	Fri 30
												8,10,12,14,16,18,20,22	0, 2, 4, 6, 8,10,12,14,16,18,20,22	0, 2, 4, 6, 8,10,12,14,16,1
SCAFFOLDING and INSULATION - NPS												CE4		
17	1	CE44CGATR	CE4	77	IST-SISI	REM INSUL FOR FAC PROG - CTMT 44 FT GEN AREA	12	04APR04 16:00A	28APR04 23:59	DR-Y ML-Y ORT3-Y R-N	54	CE44CGATR REM INSUL FOR FAC PROG - CTMT 44 FT GEN AREA SECONDARY INSERVICE INSPECTION 0303636		
18	1	CE216164SI	CE4	76	ISOL PHASE	BUILD SCAFFOLDING FOR ISOL PHASE BUS DUCT	15	07APR04 08:00A	29APR04 02:59	DR-Y ML-Y ORT3-Y R-N	60	CE216164SI BUILD SCAFFOLDING FOR ISOL PHASE BUS DUCT ISOL PHASE DUCT 0216164		
19	1	CE08TOHTI	CE4	77	IST-SISI	REINSULATE - FAC PROG - TURB HALL 8 FT OVERHD	2	20APR04 15:00A	28APR04 13:59	DR-Y ML-Y ORT3-Y R-N	208	CE08TOHTI REINSULATE - FAC PROG - TURB HALL 8 FT OVERHD SECONDARY INSERVICE INSPECTION 0303636		
20	1	CE206957TI	CE4	76	CS-00466C	INSTALL INSULATION FOR 1CS-466C	5	26APR04 09:00A	28APR04 16:59	DR-Y ML-Y ORT3-Y R-N	30	CE206957TI INSTALL INSULATION FOR 1CS-466C 1HX-1A SG 1FT-466 HIGH SIDE ROOT 0206957		
21	1	CE08TGATI	CE4	77	IST-SISI	REINSULATE - FAC PROG - TURB HALL 8 FT GEN AREA	12	26APR04 14:00A	28APR04 23:59	DR-Y ML-Y ORT3-Y R-N	435	CE08TGATI REINSULATE - FAC PROG - TURB HALL 8 FT GEN AREA SECONDARY INSERVICE INSPECTION 0303636		
22	1	CE302178TI	CE4	82	FD-02518A	INSTALL INSULATION FOR 1FD-2518A	23	27APR04 07:00A	29APR04 14:59	DR-Y ML-Y ORT3-Y R-N	132	CE302178TI INSTALL INSULATION FOR 1FD-2518A HX-22B MSR SHELL SIDE LEVEL CONTROL 0303636		
23	1	CE934380SI	CE4	76	HS-601R-37	BUILD SCAFFOLDING FOR HS-601R-37A	4	28APR04 08:00A	28APR04 15:59	DR-Y ML-Y ORT3-Y R-N	14	CE934380SI BUILD SCAFFOLDING FOR HS-601R-37A PZR PORV HEADER SNUBBER 9934380		
24	1	CE214031SI	CE4	76	CV-00257	BUILD SCAFFOLDING FOR CV-257	5	28APR04 08:00A	28APR04 21:59	DR-Y ML-Y ORT3-Y R-N	0	CE214031SI BUILD SCAFFOLDING FOR CV-257 1T-4 VCT RELIEF TO T-8A-C CVCS HUT 0214031		
25	1	CE310576TR	CE4	21	RD-05975	REMOVE INSULATION FOR 1RD-5975	3	28APR04 09:00A	28APR04 14:59	DR-Y ML-Y ORT3-N R-N	33	REMOVE INSULATION FOR 1RD-5975 T-26 BLOWDOWN TANK VENT RUPTURE DISC		
26	1	CE26TGATI	CE4	77	IST-SISI	REINSULATE - FAC PROG - TRB HALL 26 FT GEN AREA	130	28APR04 09:00A	05MAY04 21:59	DR-Y ML-Y ORT3-Y R-N	317	REINSULATE - FAC PROG - TRB HALL 26 FT GEN AREA		
27	1	CE301695SR	CE4	82	MS-05500A	REMOVE SCAFFOLDING FOR MS-5500A	4	28APR04 12:00*	28APR04 15:59	DR-Y ML-Y ORT3-Y R-N	443	CE301695SR REMOVE SCAFFOLDING FOR MS-5500A T-94A MOISTURE PRESEPARATOR INLET BTV0301695		
28	1	P1105-SR	CE4	77	T-001	NDE/ISI - REMOVE SCAFFOLD - PZR SURGE LINE	4	28APR04 12:00*	28APR04 15:59	DR-Y ML-Y ORT3-Y R-N	393	P1105-SR NDE/ISI - REMOVE SCAFFOLD - PZR SURGE LINE PRESSURIZER TANK 0303874		
29	1	CE213009SR	CE4	82	SI-00830B	REMOVE SCAFFOLDING FOR 1SI-830B	5	28APR04 12:00*	28APR04 16:59	DR-Y ML-Y ORT3-Y R-N	350	CE213009SR REMOVE SCAFFOLDING FOR 1SI-830B T-34B SI ACCUMULATOR RELIEF 0213009		
30	1	CE400290SR	CE4	82	LG-02564	REMOVE SCAFFOLDING FOR 1LG-2564	5	28APR04 12:00*	28APR04 16:59	DR-Y ML-Y ORT3-Y R-N	442	CE400290SR REMOVE SCAFFOLDING FOR 1LG-2564 HX-22B MSR LEVEL GAUGE 0400290		
31	1	CE406275TR	CE4	76	MS-02706	REMOVE INSULATION FOR 1MS-2706	5	28APR04 12:00	28APR04 16:59	DR-Y ML-Y ORT3-N R-N	42	CE406275TR REMOVE INSULATION FOR 1MS-2706 HP TURBINE DRAIN EXTRACTION OUTLET CONTROL 0406275		
32	1	CE300872SR	CE4	76	ICP-05.052	REMOVE SCAFFOLDING FOR DTS-2282A NORTH/SOUTH	10	28APR04 12:00*	28APR04 21:59		437	CE300872SR REMOVE SCAFFOLDING FOR DTS-2282A NORTH/SOUTH SECONDARY PLANT TEMPERATURE INSTRUMENTS 0300872		
33	1	CE309006TI	CE4	76	MS-00231	INSTALL INSULATION FOR 1MS-231	10	28APR04 12:00*	28APR04 21:59	DR-Y ML-Y ORT3-Y R-N	305	CE309006TI INSTALL INSULATION FOR 1MS-231 HX-1A SG HEADER ST-2029 INLET 0309006		
34	1	CE944161SR	CE4	76	DPS-05933	REMOVE SCAFFOLDING FOR 1DPS-5933	6	28APR04 14:00	28APR04 19:59	DR-Y ML-Y ORT3-Y R-N	0	CE944161SR REMOVE SCAFFOLDING FOR 1DPS-5933 T-149-1/2 DRN BOTTLE HIGH DPS INTERLOCK 9944161		
35	1	CE213464SR	CE4	76	CC-00779	REMOVE SCAFFOLDING FOR 1CC-779	4	28APR04 16:00	28APR04 19:59	DR-Y ML-Y ORT3-Y R-N	439	CE213464SR REMOVE SCAFFOLDING FOR 1CC-779 1T-12 CC SURGE TANK RELIEF TO WASTE HUT		

after 28APR04 12:00

U1R28 WORKING SCHEDULE

after 28APR04 12:00

#	U	ID	RESP	WO ST	EQID	DESCRIPTION	RD	ES	EF	RISK	MF	APR			
												Wed 28	Thu 29	Fri 30	
												8,10,12,14,16,18,20,22	0, 2, 4, 6, 8, 10,12,14,16,18,20,22	0, 2, 4, 6, 8,10,12,14,16,1	
SCAFFOLDING and INSULATION - NPS												CE4			
36	1	CE305085TR	CE4	76	LS-02376	REMOVE INSULATION FOR 1LS-2376	4	28APR04 17:00*	28APR04 20:59	DR-Y ML-Y ORT3-Y R-N	156	CE305085TR	REMOVE INSULATION FOR 1LS-2376		
37	1	CE309503TI	CE4	82	CS-00066	INSTALL INSULATION FOR 1CS-66	6	28APR04 17:00*	28APR04 22:59	DR-Y ML-Y ORT3-Y R-N	0	CE309503TI	INSTALL INSULATION FOR 1CS-66		
38	1	CE300874SR	CE4	76	ICP-05.054	REMOVE SCAFFOLDING FOR ICP 5.54	10	28APR04 20:00	29APR04 09:59	DR-Y ML-Y ORT3-Y R-N	429	CE300874SR	REMOVE SCAFFOLDING FOR ICP 5.54		
39	1	CE406159SI	CE4	76	FD-00196A	BUILD SCAFFOLD TO WORK VALVE 1FD-196A	2	28APR04 22:00*	28APR04 23:59	DR-Y ML-Y ORT3-Y R-N	0	CE406159SI	BUILD SCAFFOLD TO WORK VALVE 1FD-196A		
40	1	CE215202SR	CE4	76	P-001A-M	REMOVE SCAFFOLDING FOR P-1A-M	4	28APR04 23:00	29APR04 02:59	DR-Y ML-Y ORT3-Y R-N	341	CE215202SR	REMOVE SCAFFOLDING FOR P-1A-M		
41	1	CE309503SR	CE4	82	CS-00066	REMOVE SCAFFOLDING FOR 1CS-66	4	28APR04 23:00*	29APR04 02:59	DR-Y ML-Y ORT3-Y R-N	432	CE309503SR	REMOVE SCAFFOLDING FOR 1CS-66		
42	1	CE406159TR	CE4	76	FD-00196A	REMOVE INSULATION TO WORK VALVE	2	29APR04 00:00	29APR04 01:59	DR-Y ML-Y ORT3-Y R-N	2	CE406159TR	REMOVE INSULATION TO WORK VALVE 1FD-196A		
43	1	CE212702TI	CE4	76	MS-00220	INSTALL INSULATION FOR 1MS-220	10	29APR04 00:00	29APR04 10:59	DR-Y ML-Y ORT3-Y R-N	376	CE212702TI	INSTALL INSULATION FOR 1MS-220		
44	1	CE305025SI	CE4	76	X-04	BUILD SCAFFOLDING FOR X-04	16	29APR04 00:00	29APR04 19:59	DR-Y ML-Y ORT3-Y R-N	8	CE305025SI	BUILD SCAFFOLDING FOR X-04		
45	1	CE300960SR	CE4	76	1ICP-04.00	REMOVE SCAFFOLDING ICP-04.003-1 PZR / PRT	5	29APR04 03:00	29APR04 08:59	DR-Y ML-Y ORT3-Y R-N	448	CE300960SR	REMOVE SCAFFOLDING ICP-04.003-1 PZR / PRT LEVEL		
46	1	CE214034SR	CE4	82	CV-00370	REMOVE SCAFFOLDING FOR CV-370	6	29APR04 04:00	29APR04 10:59	DR-Y ML-Y ORT3-Y R-N	0	CE214034SR	REMOVE SCAFFOLDING FOR CV-370		
47	1	CE-RPI-SR	CE4	76	RPI	REMOVE SCAFFOLD FOR RPI COIL ON RX	5	29APR04 07:00	29APR04 11:59	DR-Y ML-Y ORT3-Y R-N	56	CE-RPI-SR	REMOVE SCAFFOLD FOR RPI COIL ON RX HEAD		
48	1	CE301049TI	CE4	76	FD-00006A	INSTALL INSULATION FOR 1FD-6A	8	29APR04 07:00*	29APR04 14:59	DR-Y ML-Y ORT3-Y R-N	424	CE301049TI	INSTALL INSULATION FOR 1FD-6A		
49	1	P1329-TI	CE4	77	PIPING HB-	NDE/ISI - REPLACE INSULATION - PIPING	16	29APR04 07:00*	29APR04 23:59	DR-Y ML-Y ORT3-Y R-N	364	P1329-TI	NDE/ISI - REPLACE INSULATION - PIPING NEAR B-CFC		
50	1	CE300852SR	CE4	76	ICP-05.010	REMOVE SCAFFOLDING: ACCUM VENT VALVE	6	29APR04 08:00*	29APR04 13:59	DR-Y ML-Y ORT3-Y R-N	347	CE300852SR	REMOVE SCAFFOLDING: ACCUM VENT VALVE STROKE		
51	1	P1126-TI	CE4	87	PIPING RC	NDE/ISI - REPLACE INSUL - PZR SURGE	16	29APR04 08:00*	30APR04 00:59	DR-Y ML-Y ORT3-Y R-N	0	P1126-TI	NDE/ISI - REPLACE INSUL - PZR SURGE LINE(B LOOP)		
52	1	CE933444SI	CE4	76	W-001C2-A	BUILD SCAFFOLDING FOR W-1C2-A	8	29APR04 09:00*	29APR04 16:59	DR-Y ML-Y ORT3-Y R-N	26	CE933444SI	BUILD SCAFFOLDING FOR W-1C2-A		
53	1	CE216332TI	CE4	76	FD-00204B	INSTALL INSULATION FOR 1FD-204B	10	29APR04 12:00*	29APR04 21:59	DR-Y ML-Y ORT3-Y R-N	285	CE216332TI	INSTALL INSULATION FOR 1FD-204B		
54	1	CE206768SR	CE4	76	CC-00763B	REMOVE SCAFFOLDING FOR 1CC-763B	4	29APR04 14:00	29APR04 17:59	DR-Y ML-Y ORT3-Y R-N	327	CE206768SR	REMOVE SCAFFOLDING FOR 1CC-763B		

Run Date

28APR04 13:44

LT-03 STANDARD PUBLICATION
FL-03 Execution Publication Set

Sheet 3 of 30

after 28APR04 12:00

U1R28 WORKING SCHEDULE

after 28APR04 12:00

#	U	ID	RESP	WO ST	EQID	DESCRIPTION	RD	ES	EF	RISK	MF	APR			
												Wed 28	Thu 29	Fri 30	
												9,10,12,14,16,18,20,22	0, 2, 4, 6, 8,10,12,14,16,18,20,22	0, 2, 4, 6, 8,10,12,14,16,1	
SCAFFOLDING and INSULATION - NPS												CE4			
55	1	CE303871TI	CE4	82	MS-00042	INSTALL INSULATION FOR 1MS-42	8	29APR04 17:00*	30APR04 00:59	DR-Y ML-Y ORT3-Y R-N	262				CE303871TI INSTALL INSULATION FOR 1MS-42
56	1	CE44POHTI	CE4	77	IST-SISI	REINSULATE - FAC PROG - PAB 44 FT	12	29APR04 17:00*	30APR04 05:59	DR-Y ML-Y ORT3-Y R-N	0				CE44POHTI REINSULATE - FAC PROG - PAB 44 FT OVE
57	1	CE406159TI	CE4	76	FD-00196A	INSTALL INSULATION AFTER VALVE WORK	2	29APR04 18:00	29APR04 19:59	DR-Y ML-Y ORT3-Y R-N	0				CE406159TI INSTALL INSULATION AFTER VALVE WO
58	1	CE406159SR	CE4	76	FD-00196A	REMOVE SCAFFOLD AFTER VALVE WORK	2	29APR04 20:00	29APR04 21:59	DR-Y ML-Y ORT3-Y R-N	417				CE406159SR REMOVE SCAFFOLD AFTER VALVE V
59	1	P1126-SR	CE4	87	PIPING RC	NDE/ISI - REMOVE SCAFF - PZR SURGE	6	30APR04 01:00*	30APR04 07:59	DR-Y ML-Y ORT3-Y R-N	327				P1126-SR NDE/ISI - REMOVE SCAFF - PZR
60	1	CE206957SR	CE4	76	CS-00466C	REMOVE SCAFFOLDING FOR 1CS-466C	4	30APR04 07:00*	30APR04 10:59	DR-Y ML-Y ORT3-Y R-N	408				CE206957SR REMOVE SCAFFOLDING FOR 1CS-466C
61	1	CE213699SR	CE4	82	CC-00762A	REMOVE SCAFFOLDING FOR 1CC-762A	4	30APR04 07:00*	30APR04 10:59	DR-Y ML-Y ORT3-Y R-N	422				CE213699SR REMOVE SCAFFOLDING FOR 1CC-762A
62	1	CE44POHSR	CE4	77	IST-SISI	REMOVE SCAFF FOR FAC PROG - PAB 44 FT	4	30APR04 07:00	30APR04 10:59	DR-Y ML-Y ORT3-Y R-N	276				CE44POHSR REMOVE SCAFF FOR FAC PROG - PAB 44 FT
63	1	CE214042SR	CE4	82	FD-02404	REMOVE SCAFFOLDING FOR FD-2404 / FD2413	5	30APR04 07:00*	30APR04 11:59	DR-Y ML-Y ORT3-Y R-N	407				CE214042SR REMOVE SCAFFOLDING FOR FD-2404 / FD2413
64	1	P1274-TI	CE4	87	PIPING EB-	NDE/ISI - REPLACE INSUL - PIPING NEAR	12	30APR04 07:00	30APR04 19:59	DR-Y ML-Y ORT3-Y R-N	346				P1274-TI NDE/ISI - REPLACE INSUL - PIPING NEAR
65	1	P1246-TI	CE4	77	PIPING EB-	NDE/ISI - REPLACE INSUL, SUPPORTS NEAR	16	30APR04 07:00*	30APR04 23:59	DR-Y ML-Y ORT3-Y R-N	0				P1246-TI NDE/ISI - REPLACE INSUL, SUPPORTS NEAR
66	1	CE309424SR	CE4	76	CW-00138A	REMOVE SCAFFOLDING FOR 1CW-138A	4	30APR04 09:00*	30APR04 12:59	DR-Y ML-Y ORT3-Y R-N	274				CE309424SR REMOVE SCAFFOLDING FOR 1CW-138A
67	1	CE214048TI	CE4	76	HS-CS-01	INSTALL INSULATION FOR HS-CS-01	10	30APR04 14:00*	30APR04 23:59	DR-Y ML-Y ORT3-Y R-N	0				CE214048TI INSTALL INSULATION FOR HS-CS-01
68	1	CE301716SR	CE4	82	FD-00139	REMOVE SCAFFOLDING FOR 1FD-139	4	30APR04 16:00*	30APR04 19:59	DR-Y ML-Y ORT3-Y R-N	399				CE301716SR REMOVE SCAFFOLDING FOR 1FD-139
69	1	CE214031SR	CE4	76	CV-00257	REMOVE SCAFFOLDING FOR CV-257	8	30APR04 16:00	30APR04 23:59	DR-Y ML-Y ORT3-Y R-N	263				CE214031SR REMOVE SCAFFOLDING FOR CV-257
70	1	CE214523TI	CE4	87	HX-020B	FW HEATER 4B - REINSTALL SHELL	6	30APR04 17:00*	30APR04 22:59	DR-Y ML-Y ORT3-Y R-N	264				CE214523TI FW HEATER 4B - REINSTALL SHELL
71	1	CE214522TI	CE4	77	HX-020A	FW HEATER 4A - REINSTALL SHELL	10	30APR04 17:00*	01MAY04 02:59	DR-Y ML-Y ORT3-Y R-N	260				CE214522TI FW HEATER 4A - REINSTALL SHELL
CONSTRUCTION ENG - G. GOZDZIALSKI												CE5			
72	1	CESISIPREP	CE5		IST-SISI	PREP OF SECONDARY COMPONENTS FOR FAC	50	05APR04 07:00A	30APR04 17:59	DR-Y ML-Y ORT3-Y R-N	321				CESISIPREP PREP OF SECONDARY COMPONENTS FOR FAC

Run Date

28APR04 13:44

LT-03 STANDARD PUBLICATION
FL-03 Execution Publication Set

Sheet 4 of 30

after 28APR04 12:00

U1R28 WORKING SCHEDULE

after 28APR04 12:00

#	U	ID	RESP	WO ST	EQID	DESCRIPTION	RD	ES	EF	RISK	MF	APR										
												Wed 28	Thu 29	Fri 30								
												8,10,12,14,16,18,20,22	0, 2, 4, 6, 8, 10, 12, 14, 16, 18, 20, 22	0, 2, 4, 6, 8, 10, 12, 14, 16, 1								
CONSTRUCTION ENG - G. GOZDZIALSKI												CE5										
73	1	CE0212642	CE5	76	FD-00225A	FD-225 HARD TO OPERATE, REPLACE VALVE	8	27APR04 02:00A	29APR04 07:59	DR-Y ML-Y ORT3-Y R-N	0	CE0212642	FD-225 HARD TO OPERATE, REPLACE VALVE									
74	1	CE0407589Z	CE5	20	T-026	T-026 - REMOVE PORTION OF TANK AND WEAR PLATE	9	27APR04 08:00A	29APR04 15:59	DR-Y ML-Y ORT3-Y R-N	41	CE0407589Z	T-026 - REMOVE PORTION OF TANK AND WEAR PLATE									
75	1	CE0407589A	CE5	20	T-026	T-026 - REPAIR PACKAGE PREPARATION	15	27APR04 08:00A	29APR04 16:59	DR-Y ML-Y ORT3-Y R-N	0	CE0407589A	T-026 - REPAIR PACKAGE PREPARATION									
76	1	CE0212702	CE5	76	MS-00220	1MS-220 EXCESSIVE SEAT LEAKAGE	12	28APR04 08:00A	28APR04 23:59	DR-Y ML-Y ORT3-Y R-N	0	CE0212702	1MS-220 EXCESSIVE SEAT LEAKAGE									
77	1	CE0406159	CE5	76	FD-00196A	1FD-196A VALVE LEAKS BY/CAP LEAKS	10	29APR04 08:00*	29APR04 17:59	DR-Y ML-Y ORT3-Y R-N	0			CE0406159	1FD-196A VALVE LEAKS BY/CAP LEAKS							
78	1	CE0407589	CE5	20	T-026	T-026 - REPAIR LEAK ON BLOWDOWN TANK	28	30APR04 07:00*	03MAY04 14:59	DR-Y ML-Y ORT3-Y R-N	0								CE0407589	T-026 - REPAIR LEAK ON BLOWDOWN TANK		
79	1	CE9929774	CE5	77	Z	INSTALL/MOD PLATFORMS	40	30APR04 07:00*	04MAY04 16:59	DR-Y ML-Y ORT3-Y R-N	0									CE9929774	INSTALL/MOD PLATFORMS	
80	1	CE0407724	CE5	71	RC-00526B	1RC-526B, REPAIR SWAGLOC FITTING	4	30APR04 13:00*	30APR04 16:59	DR-N ML-N ORT3-N R-N	0										CE0407724	1RC-526B, REPAIR SWAGLOC FITTING
CONSTRUCTION ENG - S. CARTER												CE6										
81	0	CE0210986	CE6	77	SEC	SEC SUPPORT MR 99-011*B	59	05APR04 07:00A	07MAY04 14:59	DR-N ML-N ORT3-N R-N	112	CE0210986	SEC SUPPORT MR 99-011*B									
82	0	CE0210989	CE6	76	SEC	SEC, INSTALL NEW EQUIP MR 99-011*E	59	05APR04 08:00A	07MAY04 14:59	DR-N ML-N ORT3-N R-N	112	CE0210989	SEC, INSTALL NEW EQUIP MR 99-011*E									
83	1	CE0306104C	CE6	76	102-2/TG-0	PERFORM FINAL CLEAN-UP IN CONTROL ROOM	6	28APR04 08:00A	28APR04 17:59	DR-Y ML-Y ORT3-N R-N	607	CE0306104C	PERFORM FINAL CLEAN-UP IN CONTROL ROOM									
CONSTRUCTION ENG - L. GAUTHIER												CE8										
84	1	CE-1600-22	CE8	76	R-1	PERFORM UNDERHEAD INSPECTION OF RX HEAD	45	23APR04 22:00A	30APR04 12:59	DR-Y ML-Y ORT3-Y R-N	0	CE-1600-22	PERFORM UNDERHEAD INSPECTION OF RX HEAD									
CHEMISTRY												CH										
85	1	CH0300359	CH	77	CHEM-SAMPL	RCS CL TSR 3.4.5.2	33	25APR04 05:00A	01MAY04 11:59	DR-N ML-N ORT3-N R-N	291	CH0300359	RCS CL TSR 3.4.5.2									
86	1	CH0300372	CH	77	CHEM-SAMPL	RCS DO TSR 3.4.5.1	44	25APR04 05:00A	02MAY04 11:59	DR-N ML-N ORT3-N R-N	280	CH0300372	RCS DO TSR 3.4.5.1									
87	1	CH0300402	CH	77	CHEM-SAMPL	RCS BORON SR 3.9.1.1	44	25APR04 05:00A	02MAY04 11:59	DR-N ML-N ORT3-N R-N	280	CH0300402	RCS BORON SR 3.9.1.1									
88	2	CH0300512	CH	77	CHEM-SAMPL	RCS DO TSR 3.4.5.1	25	26APR04 05:00A	30APR04 14:59	DR-N ML-N ORT3-N R-N	299	CH0300512	RCS DO TSR 3.4.5.1									
89	2	CH0300499	CH	77	CHEM-SAMPL	RCS CL TSR 3.4.5.2	36	26APR04 05:00A	01MAY04 14:59	DR-N ML-N ORT3-N R-N	288	CH0300499	RCS CL TSR 3.4.5.2									

Run Date 28APR04 13:44

LT-03 STANDARD PUBLICATION
FL-03 Execution Publication Set

Sheet 5 of 30

after 28APR04 12:00

U1R28 WORKING SCHEDULE

after 28APR04 12:00

#	U	ID	RESP	WO ST	EQID	DESCRIPTION	RD	ES	EF	RISK	MF	APR										
												Wed 28	Thu 29	Fri 30								
												8,10,12,14,16,18,20,22	0, 2, 4, 6, 8, 10,12,14,16,18,20,22	0, 2, 4, 6, 8, 10,12,14,16,18,20,22								
CHEMISTRY												CH										
90	0	CH0300196	CH	77	CHEM-SAMPL	BAST BORON TSR 3.5.1.2	19	26APR04 07:00A	30APR04 14:59	DR-N ML-N ORT3-N R-N	152	CH0300196	BAST BORON TSR 3.5.1.2									
91	1	CH0300386	CH	77	CHEM-SAMPL	SGBDFO GAMMA SCAN	19	26APR04 07:00A	30APR04 14:59	DR-N ML-N ORT3-N R-N	152	CH0300386	SGBDFO GAMMA SCAN									
92	1	CH0300441	CH	77	CHEM-SAMPL	RE-229 ISOTOPIC	19	26APR04 07:00A	30APR04 14:59	DR-N ML-N ORT3-N R-N	152	CH0300441	RE-229 ISOTOPIC									
93	2	CH0300525	CH	77	CHEM-SAMPL	SGBDFO GAMMA SCAN	19	26APR04 07:00A	30APR04 14:59	DR-N ML-N ORT3-N R-N	152	CH0300525	SGBDFO GAMMA SCAN									
94	2	CH0300551	CH	77	CHEM-SAMPL	RE-229 ISOTOPIC	19	26APR04 07:00A	30APR04 14:59	DR-N ML-N ORT3-N R-N	152	CH0300551	RE-229 ISOTOPIC									
95	2	CH0300565	CH	77	CHEM-SAMPL	RCS GROSS ACTIVITY SR 3.04.16.01	1	28APR04 07:00A	28APR04 12:59	DR-N ML-N ORT3-N R-N	323	CH0300565	RCS GROSS ACTIVITY SR 3.04.16.01									
96	0	CH0300232	CH	77	CHEM-SAMPL	SFP BORON SR 3.7.11.1	1	29APR04 07:00*	29APR04 07:59	DR-N ML-N ORT3-N R-N	167			CH0300232	SFP BORON SR 3.7.11.1							
97	0	CH0300245	CH	77	CHEM-SAMPL	WASTEWATER EFFLUENT COMPOSITE	1	29APR04 07:00*	29APR04 07:59	DR-N ML-N ORT3-N R-N	167			CH0300245	WASTEWATER EFFLUENT COMPOSITE							
98	1	CH0300461	CH	77	CHEM-SAMPL	RWST BORON SR 3.05.04.3	1	29APR04 07:00*	29APR04 07:59	DR-N ML-N ORT3-N R-N	167			CH0300461	RWST BORON SR 3.05.04.3							
99	2	CH0300583	CH	77	CHEM-SAMPL	RCS H-3 TSR 3.4.1.1	1	29APR04 07:00*	29APR04 07:59	DR-N ML-N ORT3-N R-N	167			CH0300583	RCS H-3 TSR 3.4.1.1							
100	2	CH0300590	CH	77	CHEM-SAMPL	RWST BORON SR 3.05.04.3	1	29APR04 07:00*	29APR04 07:59	DR-N ML-N ORT3-N R-N	167			CH0300590	RWST BORON SR 3.05.04.3							
101	2	CH0300577	CH	77	CHEM-SAMPL	RCS DOSE EQUIVALENT I-131	6	29APR04 07:00*	29APR04 12:59	DR-N ML-N ORT3-N R-N	162			CH0300577	RCS DOSE EQUIVALENT I-131							
102	1	CAMP-113BA	CH		CAMP-113	CAMP-113 SAMPLE B STEAM GENERATOR	3	29APR04 13:00	29APR04 15:59	DR-N ML-N ORT3-N R-N	0										CAMP-113BA CAMP-113 SAMPLE B STEAM GENERATOR (SPA	
103	1	CAMP-113AA	CH		CAMP-113	CAMP-113 SAMPLE A STEAM GENERATOR	3	29APR04 19:00	29APR04 21:59	DR-N ML-N ORT3-N R-N	0											CAMP-113AA CAMP-113 SAMPLE A STEAM GENERA
ENGINEERING - PREDICTIVE MAINTENANCE												EEP										
104	0	EE0302288	EEP	77	SW BLDG	VIBRATION ROUTE DATA - PUMP HSE AND WWT	16	29APR04 12:00*	30APR04 04:59	DR-Y ML-Y ORT3-Y R-N	612			EE0302288	VIBRATION ROUTE DATA - PUMP HSE AND WWT							EE0302288 VIBRATION ROUTE DATA - PUMP HSE AND WWT
ELECTRICAL MAINTENANCE												EM										
105	1	EM0216638	EM	40	P-001B-M	START REPAIRS FOR P-1B HIGH BREAKAWAY	50	28APR04 01:00A	30APR04 13:59	DR-N ML-N ORT3-N R-M	0	EM0216638	START REPAIRS FOR P-1B HIGH BREAKAWAY									REACT
106	1	EM0215201A	EM	76	P-001A-M	MANUFACTURE WEIGHTS (AS	2	28APR04 12:00	28APR04 13:59	DR-N ML-N ORT3-N R-N	0	EM0215201A	MANUFACTURE WEIGHTS (AS REQUIRED)									REACTOR COOLANT PUMP MOTOR 0215201
107	1	X04-015	EM		X-04	INSTALL FAST BUS TRANSFER TEMP MOD	2	28APR04 12:00*	28APR04 13:59	DR-N ML-N ORT3-N R-N	3	X04-015	INSTALL FAST BUS TRANSFER TEMP MOD									

Run Date

28APR04 13:44

LT-03 STANDARD PUBLICATION
FL-03 Execution Publication Set

Sheet 6 of 30

U1R28 WORKING SCHEDULE

#	U	ID	RESP	WO ST	EQID	DESCRIPTION	RD	ES	EF	RISK	MF	APR							
												Wed 28	Thu 29	Fri 30		Sat 01		Sun 02	
ELECTRICAL MAINTENANCE													EM						
108	1	EM0302132C	EM	76	LO-00291	P-059B - PERFORM CLEANING OF MOTOR TERMS	4	28APR04 12:00	28APR04 15:59	DR-Y ML-Y ORT3-Y R-N	43	EM02132C	P-059B - PERFORM CLEANING OF MOTOR TERMS						
109	0	EM0305175	EM	77	35-E	MONTHLY FUNCTIONAL CHECK/INSPECTION	6	28APR04 12:00*	28APR04 17:59	DR-N ML-N ORT3-N R-N	644	EM0305175	MONTHLY FUNCTIONAL CHECK/INSPECTION						
110	1	EM0215202	EM	76	P-001A-M	P-1A-M PERFORM OIL CHANGE	10	28APR04 12:00*	28APR04 22:59	DR-N ML-N ORT3-N R-N	0	EM0215202	P-1A-M PERFORM OIL CHANGE						
111	1	EM0216165D	EM	77	HX-001A	REMOVE POWER SUPPLIES FROM SLUDGE TRAILER	10	28APR04 12:00	28APR04 22:59	DR-Y ML-Y ORT3-N R-N	568	EM0216165D	REMOVE POWER SUPPLIES FROM SLUDGE TRAILER						
112	1	EM0203130	EM	76	W-001D2-M	1W-1D2-M CLEAN CONNECTIONS	16	28APR04 12:00*	29APR04 04:59	DR-N ML-N ORT3-N R-N	0	EM0203130	1W-1D2-M CLEAN CONNECTIONS						
113	1	EM-BMFP-03	EM	76	P-028B-M	P28B REMOVE MOTOR TOP COVER	6	28APR04 12:00	29APR04 08:59	DR-Y ML-Y ORT3-N R-M	0	EM-BMFP-03	P28B REMOVE MOTOR TOP COVER						
114	1	EM0400344	EM	76	P-028A-M	1P-28A-M PUMP END MOTOR BEARING LEAKING	10	28APR04 12:00*	29APR04 12:59	DR-Y ML-Y ORT3-Y R-N	4	EM0400344	1P-28A-M PUMP END MOTOR BEARING LEAKING						
115	0	EM0301792	EM	76	A52-DHVR-3	BREAKER MAINTENANCE 3000-01 (A52-01)	24	28APR04 12:00*	29APR04 13:59	DR-N ML-N ORT3-N R-N	0	EM0301792	BREAKER MAINTENANCE 3000-01 (A52-01)						
116	1	EM0407780A	EM	76	Z-013	Z-013 PERFORM REPAIRS TO SMALL HOOK CIRCUITRY	36	28APR04 12:00	30APR04 02:59	DR-Y ML-Y ORT3-N R-N	51	EM0407780A	Z-013 PERFORM REPAIRS TO SMALL HOOK CIRCUITRY						
117	0	EM0306113A	EM	76	D72-16-15	IWP-037-08 REPL 1MOB-031 - 1MOB-041	16	28APR04 13:00	29APR04 04:59	DR-N ML-N ORT3-N R-N	0	EM0306113A	IWP-037-08 REPL 1MOB-031 - 1MOB-041						
118	1	EM0215201	EM	76	P-001A-M	ADJUST BALANCE WEIGHTS (IF REQUIRED)	2	28APR04 14:00	28APR04 15:59	DR-N ML-N ORT3-N R-N	0	EM0215201	ADJUST BALANCE WEIGHTS (IF REQUIRED)						
119	1	EM0304544	EM	76	POS-00466	POS-466 INSTALL WEEP HOLE IN FLEX CONDUIT	4	28APR04 18:00*	28APR04 21:59	DR-N ML-N ORT3-N R-N	0	EM0304544	POS-466 INSTALL WEEP HOLE IN FLEX CONDUIT						
120	1	EM0216167	EM	76	E-01	INSPECT AND MAINTAIN EXCITER FUSES PER MWP 104.	10	28APR04 18:00*	29APR04 18:59	DR-N ML-N ORT3-N R-M	0	EM0216167	INSPECT AND MAINTAIN EXCITER FUSES PER MWP 104.						
121	0	EM0304874	EM	76	A52-DHVR-1	1P-01A BREAKER MAINTENANCE 1200-31 (A52-04)	24	28APR04 18:00*	30APR04 23:59	DR-Y ML-Y ORT3-N R-N	0	EM0304874	1P-01A BREAKER MAINTENANCE 1200-31 (A52-04)						
122	1	EM0215215	EM	76	RG-01	CLEAN AND INSP OF NEUTRAL GROUNDING TRANS CUBE	5	28APR04 20:00*	29APR04 00:59	DR-Y ML-Y ORT3-N R-N	0	EM0215215	CLEAN AND INSP OF NEUTRAL GROUNDING TRANS CUBE						
123	1	EM-8480I	EM	76	RPI	AT HEAD RPI COIL RESISTANCE/INDUCTANC	10	28APR04 20:00*	29APR04 05:59	DR-N ML-N ORT3-N R-M	0	EM-8480I	AT HEAD RPI COIL RESISTANCE/INDUCTANC						
124	1	EM-8480J	EM	76	R-1	AT HEAD CRDM COIL RESISTANCE/INDUCTANC	10	28APR04 20:00*	29APR04 05:59	DR-N ML-N ORT3-N R-M	0	EM-8480J	AT HEAD CRDM COIL RESISTANCE/INDUCTANC						
125	1	EM0216168	EM	76	E-02	1RMP 9375, VOLTAGE REGULATOR CABINET	36	28APR04 20:00*	30APR04 10:59	DR-N ML-N ORT3-N R-N	0	EM0216168	1RMP 9375, VOLTAGE REGULATOR CABINET						
126	1	EM0216645	EM	76	E-02	1E-02 REPAIR / RECAL / REPLACE MEL	36	28APR04 20:00*	30APR04 10:59	DR-N ML-N ORT3-N R-N	0	EM0216645	1E-02 REPAIR / RECAL / REPLACE MEL						

after 28APR04 12:00

U1R28 WORKING SCHEDULE

after 28APR04 12:00

#	U	ID	RESP	WO ST	EQID	DESCRIPTION	RD	ES	EF	RISK	MF	APR			
												Wed 28	Thu 29	Fri 30	
												8,10,12,14,16,18,20,22	0, 2, 4, 6, 8,10,12,14,16,18,20,22	0, 2, 4, 6, 8,10,12,14,16,18	
ELECTRICAL MAINTENANCE												EM			
127	1	EM0305572	EM	76	POS-00476	INSTALL WEEP HOLE IN FLEX CONDUIT	4	28APR04 22:00*	29APR04 01:59	DR-Y ML-Y ORT3-N R-N	0	EM0305572	INSTALL WEEP HOLE IN FLEX CONDUIT		
128	1	EM0215199B	EM	76	P-001A-M	P-001A FINAL PMT PER 9002-12	10	28APR04 23:00*	29APR04 09:59	DR-N ML-N ORT3-N R-N	0	EM0215199B	P-001A FINAL PMT PER 9002-12		
129	1	EM0216164C	EM	76	ISOL PHASE	PRE-MAINTENANCE MEGGER OF ISOPHASE	3	29APR04 02:00	29APR04 04:59	DR-N ML-N ORT3-N R-N	0	EM0216164C	PRE-MAINTENANCE MEGGER OF ISOPHASE BUS		
130	1	EM0203130A	EM	76	W-001D2-M	1W-1D2-M PERFORM BUMP FOR ROTATION	1	29APR04 07:00	29APR04 07:59	DR-N ML-N ORT3-N R-N	89	EM0203130A	1W-1D2-M PERFORM BUMP FOR ROTATION		
131	0	EM0306113B	EM	76	D72-16-15	IWP-037-08 EM PMT OF 1MOB-031 - 1MOB-041	2	29APR04 07:00	29APR04 08:59	DR-N ML-N ORT3-N R-N	0	EM0306113B	IWP-037-08 EM PMT OF 1MOB-031 - 1MOB-041		
132	1	EM9604321A	EM	78	FH-CTC-08	FH-CTC-08 PEPLACE CAVITY LGT FIXTURE	6	29APR04 07:00*	29APR04 12:59	DR-N ML-N ORT3-N R-N	555	EM9604321A	FH-CTC-08 PEPLACE CAVITY LGT FIXTURE		
133	1	EM-BMFPCL2	EM	76	P-028B-M	CONTINUE P28B INPLACE CLEANING	27	29APR04 09:00	02MAY04 08:59	DR-Y ML-Y ORT3-N R-M	0	EM-BMFPCL2	CONTINUE P28B INPLACE CLEANING (ROTOR & STATC		
134	1	EAMRCP-B1	EM	76	P-001A-M	REPLACE 'A' RCP FLOOR PANEL	2	29APR04 10:00	29APR04 11:59	DR-Y ML-Y ORT3-N R-N	443	EAMRCP-B1	REPLACE 'A' RCP FLOOR PANEL		
135	1	EM0215203	EM	76	P-001A-M	P-001A-M - 2ND MCE TEST (1A52-04/1A-01)	3	29APR04 11:00*	29APR04 13:59	DR-Y ML-Y ORT3-N R-N	317	EM0215203	P-001A-M - 2ND MCE TEST (1A52-04/1A-01)		
136	1	EM0407727	EM	05	C-041	C-041 INSTALL LOCK NUTS ON BUS BAR	8	29APR04 12:00*	29APR04 19:59		677	EM0407727	C-041 INSTALL LOCK NUTS ON BUS BAR		
137	0	EM9925005	EM	76	A52-DHVR-3	3000-1 1X02-1A01 CELL SWITCH INSPECTION	1	29APR04 13:00	29APR04 13:59	DR-N ML-N ORT3-N R-N	132	EM9925005	3000-1 1X02-1A01 CELL SWITCH INSPECTION		
138	0	EM0304872	EM	76	A52-DHVR-1	1P-025A BREAKER MAINTENANCE 1200-40	24	29APR04 14:00*	02MAY04 10:59	DR-N ML-N ORT3-N R-N	0	EM0304872	1P-025A BREAKER MAINTENANCE 1200-40 (A5		
139	1	EM0306574A	EM	76	MOB-004	PERFORM PRE-INSTALL CHECK ON BREAKERS	8	29APR04 16:00	30APR04 00:59	DR-N ML-N ORT3-N R-N	0	EM0306574A	PERFORM PRE-INSTALL CHECK ON BREAK		
140	1	EM0306578A	EM	76	Y-04-01	PERFORM PRE-INSTALL CHECK ON BREAKERS	10	29APR04 16:00*	30APR04 02:59	DR-N ML-N ORT3-N R-N	0	EM0306578A	PERFORM PRE-INSTALL CHECK ON BREAK		
141	1	EM0215218	EM	76	W-001A1-M	W-1A1-M INSPECT EQUALIZATION VALVE	1	29APR04 20:00*	29APR04 20:59	DR-Y ML-Y ORT3-N R-N	0	EM0215218	W-1A1-M INSPECT EQUALIZATION VA		
142	1	EM0215246	EM	76	62/A01	CAL AND TEST 62/A01 RELAY PER 1RMP	6	30APR04 07:00	30APR04 12:59	DR-N ML-N ORT3-N R-N	0	EM0215246	CAL AND TEST 62/A01		
143	1	EM-8480H	EM	76	R-1	CLEAN CONOSEAL PORTS	15	30APR04 13:00	01MAY04 04:59	DR-N ML-N ORT3-N R-N	0	EM-8480H	CLEAN C		
144	1	BRCP-DIS1	EM	40	P-001B-M	P-1B-M CONTINUE DISASSEMBLY OF	48	30APR04 14:00	02MAY04 13:59	DR-N ML-N ORT3-N R-M	0	BRCP-DIS1	P-1B-M		
145	1	BRCP-CL1	EM	40	P-001B-M	P-1B-M PERFORM CLEANING OF PARTS	48	30APR04 14:00	02MAY04 17:59	DR-N ML-N ORT3-N R-M	185	BRCP-CL1	P-1B-M		

after 28APR04 12:00

U1R28 WORKING SCHEDULE

after 28APR04 12:00

#	U	ID	RESP	WO ST	EQID	DESCRIPTION	RD	ES	EF	RISK	MF	APR			
												Wed 28	Thu 29	Fri 30	
ENGINEERING PROGRAMS - TEST SERVICES												EPT			
162	1	EP0301957	EPT	76	HX-001B	EDDY CURRENT TEST STEAM GEN B - 1 SHIFT	22	17APR04 07:00A	30APR04 11:59	DR-N ML-Y ORT3-N R-N	0	EP0301957	EDDY CURRENT TEST STEAM GEN B - 1 SHIFT		
163	1	EP0301962A	EPT	76	HX-020A	HX-020A - EDDY CURRENT	24	23APR04 08:00A	30APR04 15:59	DR-Y ML-Y ORT3-Y R-N	11	EP0301962A	HX-020A - EDDY CURRENT REVIEW/RERUN		
164	1	EP0301965	EPT	76	HX-023B	HX-023B - EDDY CURRENT INSPECT	2	27APR04 08:00A	28APR04 13:59	DR-Y ML-Y ORT3-Y R-N	0	EP0301965	HX-023B - EDDY CURRENT INSPECT LUBE OIL COOLER		
165	1	EP0301964	EPT	76	HX-023A	HX-023A - EDDY CURRENT INSPECT	6	28APR04 14:00	29APR04 09:59	DR-Y ML-Y ORT3-Y R-N	0	EP0301964	HX-023A - EDDY CURRENT INSPECT LUBE OIL COOLER		
166	1	EP0301965A	EPT	76	HX-023B	HX-023B - EDDY CURRENT	12	28APR04 14:00	29APR04 15:59	DR-Y ML-Y ORT3-Y R-N	11	EP0301965A	HX-023B - EDDY CURRENT REVIEW/RERUN		
167	1	EP0301964A	EPT	76	HX-023A	HX-023A - EDDY CURRENT	10	29APR04 10:00	30APR04 09:59	DR-Y ML-Y ORT3-Y R-N	0	EP0301964A	HX-023A - EDDY CURRENT REVIEW/RERUN		
168	1	EP0302114A	EPT	77	SC-1A	SC-1A - INSTALL COND TUBE SHIELDS (1A)	3	30APR04 10:00*	30APR04 12:59	DR-Y ML-Y ORT3-Y R-N	0	EP0302114A	SC-1A - INSTALL COND TUBE SHIELDS (1A)		
169	1	EP0301956T	EPT	76	HX-001A	1HX-1A PLUG S/G TUBES	12	30APR04 12:00	01MAY04 00:59	DR-N ML-Y ORT3-N R-N	0	EP0301956T	1HX-1A PLUG S/G TUBES		
170	1	EP0301957T	EPT	76	HX-001B	1HX-1B PLUG S/G TUBES	12	30APR04 12:00	01MAY04 00:59	DR-N ML-Y ORT3-N R-N	0	EP0301957T	1HX-1B PLUG S/G TUBES		
171	1	EE0305857	EPT	76	P-101B	1P-101B - POST MAINTENANCE	2	30APR04 13:00	30APR04 14:59	DR-Y ML-Y ORT3-Y R-N	3	EE0305857	1P-101B - POST MAINTENANCE		
172	1	EP0302115A	EPT	77	SC-1B	SC-1B - INSTALL COND TUBE SHIELDS (1B)	3	30APR04 13:00*	30APR04 15:59	DR-Y ML-Y ORT3-Y R-N	1	EP0302115A	SC-1B - INSTALL COND TUBE SHIELDS (1B)		
FACILITIES GROUP - UTILITY GROUP												FG1			
173	1	FG0212814P	FG1	76	PIPE AC 01	PIPE AC 0152N-04 STRIP/REPAINT (part 2)	45	21APR04 20:00A	30APR04 12:59	DR-Y ML-Y ORT3-Y R-N	275	FG0212814P	PIPE AC 0152N-04 STRIP/REPAINT (part 2)		
174	1	FG311887P	FG1	76	HX-021B	PAINT FD-2412	48	28APR04 16:00	30APR04 20:59	DR-Y ML-Y ORT3-N R-N	61	FG311887P	PAINT FD-2412		
175	1	FG213064P	FG1	76	MS-00010A	PAINT VALVE 1MS-10A	4	29APR04 18:00*	29APR04 21:59	DR-Y ML-Y ORT3-Y R-N	0	FG213064P	PAINT VALVE 1MS-10A		
176	1	FG212642P	FG1	76	FD-00225A	PAINT FD-225A VALVE	4	30APR04 06:00*	30APR04 09:59	DR-Y ML-Y ORT3-Y R-N	0	FG212642P	PAINT FD-225A VALVE		
177	0	FG0302075	FG1	77	MANHOLE PM	PUMP ELECTRICAL MANHOLE SUMPS	8	30APR04 06:00*	30APR04 13:59	DR-Y ML-Y ORT3-Y R-N	300	FG0302075	PUMP ELECTRICAL MANHOLE SUMPS		
178	1	FG216557P	FG1	76	FD-00282C	PAINT 1FD-282C	8	30APR04 07:00*	30APR04 14:59	DR-Y ML-Y ORT3-Y R-N	0	FG216557P	PAINT 1FD-282C		
179	1	FG0212787	FG1	76	T-001	1T-1 PAINT/INSULATE SUPPORTS	28	30APR04 09:00*	01MAY04 14:59	DR-Y ML-Y ORT3-Y R-N	286	FG0212787	1T-1 PAINT/INSULATE SUPPORTS		

after 28APR04 12:00

U1R28 WORKING SCHEDULE

after 28APR04 12:00

#	U	ID	RESP	WO ST	EQID	DESCRIPTION	RD	ES	EF	RISK	MF	APR						
												Wed 28	Thu 29	Fri 30	8,10,12,14,16,18,20,22	0, 2, 4, 6, 8, 10, 12, 14, 16, 18, 20, 22	0, 2, 4, 6, 8, 10, 12, 14, 16, 18, 20, 22	
FACILITIES GROUP - MTN MECH OPER NORTH												FG2						
180	0	FG0300152	FG2	77	VNTRN	PREPARE VNTRN SYSTEM COMPONENTS FOR	1	28APR04 06:00A	28APR04 12:59	DR-Y ML-Y ORT3-Y R-N	323	FG0300152 PREPARE VNTRN SYSTEM COMPONENTS FOR VNTRN SYSTEM MULTI AND/OR NON-NUMBERED EQUIPMENT 0300152						
FACILITIES GROUP - BOB WIENSCH												FG3						
181	1	FG0400102	FG3		SAFETY	INSTALL SAFETY CHAINS FOR PZR	2	28APR04 18:00*	28APR04 19:59		372	FG0400102 INSTALL SAFETY CHAINS FOR PZR						
RADIATION PROTECTION (OLD)												HP						
182	0	RE-234-B06	HP		HP RMS	RE-234/235 AIR SAMPLE CHANGE OUT	1	28APR04 19:00*	28APR04 19:59	DR-Y ML-Y ORT3-Y R-N	230	RE-234-B06 RE-234/235 AIR SAMPLE CHANGE OUT						
183	0	RE-211-B06	HP		HP RMS	RE-211/212 AIR SAMPLE CHANGE OUT	1	29APR04 00:00*	29APR04 00:59	DR-Y ML-Y ORT3-Y R-N	225	RE-211-B06 RE-211/212 AIR SAMPLE CHANGE OUT						
184	1	HP0301878	HP	77	RE-00126	RE-126/1RE-127/1RE-128 CALIBRATION	6	29APR04 06:00	29APR04 11:59	DR-Y ML-Y ORT3-Y R-N	148	HP0301878 RE-126/1RE-127/1RE-128 CALIBRATION						
185	1	HP7.51.6C	HP	85	HP PURGE T	PURGE RMS TRIP TEST (HPIP 7.51.6)	2	30APR04 13:00*	30APR04 14:59	DR-Y ML-Y ORT3-Y R-N	336	HP7.51.6C PURGE RMS TRIP TEST (HPIP 7.51.6) UNIT 1 CONTAINMENT HIGH RANGE RADIATION MONITORING						
I&C MAINTENANCE												IC						
186	2	ICRP1C-250	IC		O-RP-001C	RETRIEVE Z-16 CONSTANTS/REPLC BATT	2	30APR04 17:00	30APR04 19:59	DR-Y ML-Y ORT3-Y R-N	298	ICRP1C-250 RE						
I&C - C: RHODEN & R. YOUNG												IC1						
187	1	IC5.47-1	IC1	76	ICP-05.047	SECONDARY LEVEL CONTROLLERS AND SWIT	88	19APR04 11:00A	06MAY04 11:59	DR-Y ML-Y ORT3-Y R-N	0	IC5.47-1 SECONDARY LEVEL CONTROLLERS AND SWIT						
188	1	IC0302099	IC1	76	LC-02514	LC-2514 REFURBISH	88	19APR04 11:00A	07MAY04 16:59	DR-Y ML-Y ORT3-Y R-N	0	IC0302099 LC-2514 REFURBISH						
189	1	IC0305085	IC1	76	LS-02376	LS-2376 SMALL STEAM LEAK ON LVL SW	88	19APR04 11:00A	07MAY04 16:59	DR-Y ML-Y ORT3-Y R-N	0	IC0305085 LS-2376 SMALL STEAM LEAK ON LVL SW						
190	1	ICLS3579	IC1	76	LS-03579	DISASSEMBLE, CLEAN AND INSPECT LEVEL INSTRU	88	19APR04 11:00A	07MAY04 16:59	DR-Y ML-Y ORT3-Y R-N	0	ICLS3579 DISASSEMBLE, CLEAN AND INSPECT LEVEL INSTRU						
191	1	ICLS3580	IC1	76	LS-03580	DISASSEMBLE, CLEAN AND INSPECT LEVEL INSTRU	88	19APR04 11:00A	07MAY04 16:59	DR-Y ML-Y ORT3-Y R-N	0	ICLS3580 DISASSEMBLE, CLEAN AND INSPECT LEVEL INSTRU						
192	1	ICLS3581	IC1	76	LS-03581	DISASSEMBLE, CLEAN AND INSPECT LEVEL INSTRU	88	19APR04 11:00A	07MAY04 16:59	DR-Y ML-Y ORT3-Y R-N	0	ICLS3581 DISASSEMBLE, CLEAN AND INSPECT LEVEL INSTRU						
193	1	ICLS3582	IC1	76	LS-03582	DISASSEMBLE, CLEAN AND INSPECT LEVEL INSTRU	88	19APR04 11:00A	07MAY04 16:59	DR-Y ML-Y ORT3-Y R-N	0	ICLS3582 DISASSEMBLE, CLEAN AND INSPECT LEVEL INSTRU						
194	1	IC4.14	IC1	76	ICP-04.014	ICP 4.14 BA CONTROL INSTRUMENT CAL	1	25APR04 09:00A	28APR04 12:59	DR-N ML-N ORT3-N R-N	26	IC4.14 ICP 4.14 BA CONTROL INSTRUMENT CAL BORIC ACID CONTROL SYSTEM 0300834						
195	1	IC0400553B	IC1	76	SERVICE	SERVICE MAINT SUPPORT-EQ VERIFYING	20	27APR04 12:00A	03MAY04 07:59	DR-Y ML-Y ORT3-Y R-N	0	IC0400553B SERVICE MAINT SUPPORT-EQ VERIFYING						

Run Date

28APR04 13:44

LT-03 STANDARD PUBLICATION
FL-03 Execution Publication Set

Sheet 11 of 30

after 28APR04 12:00

U1R28 WORKING SCHEDULE

after 28APR04 12:00

#	U	ID	RESP	WO ST	EQID	DESCRIPTION	RD	ES	EF	RISK	MF	APR						
												Wed 28	Thu 29	Fri 30				
												8,10,12,14,16,18,20,22	0, 2, 4, 6, 8, 10,12,14,16,18,20,22	0, 2, 4, 6, 8, 10,12,14,16,18,20,22	0, 2, 4, 6, 8, 10,12,14,16,18,20,22			
I&C - J. SCHMOLDT												IC2						
214	1	IC0400343	IC2	76	PS-02142	1PS-2142 REPLACE PRESSURE SWITCH	63	27APR04 20:00A	05MAY04 01:59	DR-Y ML-Y ORT3-Y R-N	25	IC0400343	1PS-2142	REPLACE PRESSURE SWITCH				
215	1	IC5.51	IC2	76	ICP-05.051	ICP 5.51 SECONDARY VACUUM INSTRUMENTS	70	27APR04 20:00A	05MAY04 21:59	DR-Y ML-Y ORT3-Y R-N	18	IC5.51	ICP 5.51	SECONDARY VACUUM INSTRUMENTS				
216	1	IC5.63LTDN	IC2	76	1ICP-05.06	ICP-05.063 LETDOWN FLOW CALIBRATION	9	28APR04 19:00	29APR04 03:59	DR-N ML-N ORT3-Y R-N	45	IC5.63LTDN	ICP-05.063	LETDOWN FLOW CALIBRATION				
217	1	IC5.63SEAL	IC2	76	1ICP-05.06	ICP-05.063 RCP A AND B SEAL WATER INSTRU	9	28APR04 19:00*	29APR04 03:59	DR-Y ML-Y ORT3-Y R-N	0	IC5.63SEAL	ICP-05.063	RCP A AND B SEAL WATER INSTRU CAL				
218	1	IC466RBLD	IC2	76	P/P-00466	FD-466 POSITIONER REBUILD PM	24	28APR04 19:00*	01MAY04 20:59	DR-Y ML-Y ORT3-N R-N	20	IC466RBLD	FD-466	POSITIONER REBUILD PM				
219	1	IC0300862A	IC2	76	ICP-05.027	PS-6035 REPLACE SWITCH	4	29APR04 19:00*	29APR04 22:59	DR-Y ML-Y ORT3-Y R-N	36							
220	1	IC0213741	IC2	76	DPI-04835	DPI-4835 READING NEGATIVE	8	29APR04 19:00	30APR04 02:59	DR-Y ML-Y ORT3-Y R-N	24							
221	1	IC5.77	IC2	76	ICP-05.077	CONT FAN DISCHARGE FLOW SWITCHES	10	29APR04 19:00*	30APR04 04:59	DR-Y ML-Y ORT3-Y R-N	0							
222	1	ICRKCLN-4	IC2	76	I&C MISC	RACK CLEANING - CONTROL RM. RACKS	15	29APR04 19:00*	30APR04 10:59	DR-N ML-N ORT3-N R-N	7							
I&C - M. KENNETT & R. YOUNG												IC5						
223	1	IC0300795	IC5	76	I&C MISC	VISUAL INSPECTION OF RELAY RACKS	30	25APR04 09:00A	01MAY04 13:59	DR-Y ML-Y ORT3-Y R-N	36	IC0300795	VISUAL INSPECTION OF RELAY RACKS					
224	1	ICCX-PORV	IC5	76	CX	PORV OPERABILITY TEST	1	27APR04 09:00A	28APR04 12:59	DR-N ML-Y ORT3-N R-N	140	ICCX-PORV	PORV OPERABILITY TEST					
225	1	IC2.16SUP	IC5	76	ICP-02.016	ICP 2.16 OVERPRESSURE	1	28APR04 09:00A	28APR04 12:59	DR-N ML-Y ORT3-N R-M	140	IC2.16	OVERPRESSURE MITIGATION BISTABLE CHK					
226	1	ICAX-PORV	IC5	76	AX	PORV OPERABILITY TEST	1	28APR04 09:00A	28APR04 12:59	DR-N ML-Y ORT3-N R-N	180	ICAX-PORV	PORV OPERABILITY TEST					
227	1	IC4.3-5	IC5	76	1ICP-04.00	ICP-04.003-5 AUX FEED WATER FLOW INSTRU	12	28APR04 09:00A	29APR04 12:59	DR-Y ML-Y ORT3-Y R-N	136	IC4.3-5	AUX FEED WATER FLOW INSTRU CAL					
228	1	IC5.21	IC5	76	ICP-05.021	PZR LEVEL CONTROL SYSTEM CALS	14	28APR04 09:00A	29APR04 14:59	DR-N ML-Y ORT3-N R-N	46	IC5.21	PZR LEVEL CONTROL SYSTEM CALS					
229	1	IC5.50	IC5	76	ICP-05.050	ICP 5.50 SECONDARY MIDRANGE PRESSURE	58	28APR04 09:00A	04MAY04 14:59	DR-Y ML-Y ORT3-Y R-N	35	IC5.50	SECONDARY MIDRANGE PRESSURE					
230	1	IC10.46AUX	IC5	76	ICP-10.046	ICP 10.46 RDC LOGIC CAB PWR SUPPLY	20	29APR04 08:00*	30APR04 04:59	DR-Y ML-Y ORT3-Y R-N	0	IC10.46AUX	ICP 10.46 RDC LOGIC CAB PWR SUPPLY					
231	1	IC5.72	IC5	76	RDC-LOGIC	1ICP 5.72 SLAVE CYCLER AND PULSER	20	29APR04 08:00	30APR04 16:59	DR-Y ML-Y ORT3-Y R-N	28	IC5.72	ICP 5.72 SLAVE CYCLER AND PULSER					

Run Date

28APR04 13:44

LT-03 STANDARD PUBLICATION
FL-03 Execution Publication Set

Sheet 13 of 30

after 28APR04 12:00

U1R28 WORKING SCHEDULE

after 28APR04 12:00

#	U	ID	RESP	WO ST	EQID	DESCRIPTION	RD	ES	EF	RISK	MF	APR					
												Wed 28		Thu 29		Fri 30	
												8,10,12,14,16,18,20,22	0, 2, 4, 6, 8, 10,12,14,16,18,20,22	0, 2, 4, 6, 8, 10,12,14,16,1			
MECHANICAL MAINTENANCE MM1 RIDINGS/ BRITTINGHAM												MM1					
250	1	MM0305396	MM1	76	W-001B1	W-1B1 REPLACE SPRING ISOLATORS	5	24APR04 13:00A	28APR04 16:59	DR-Y ML-Y ORT3-N R-N	11	MM0305396	W-1B1 REPLACE SPRING ISOLATORS				
																	CONTAINMENT ACCIDENT RECIRCULATION FAN 0305396
251	1	MM9933443	MM1	76	W-001B2-A	W-1B2-A REPLACE BACKDRAFT DAMPER	15	25APR04 18:00A	29APR04 21:59	DR-Y ML-Y ORT3-N R-N	0	MM9933443	W-1B2-A REPLACE BACKDRAFT DAMPER				
																	CONTAINMENT COOLING FAN DIS
252	1	MM0214055	MM1	76	HX-015A	HX-15A, MOTOR COOLING COIL	28	26APR04 02:00A	30APR04 23:59	DR-Y ML-Y ORT3-N R-N	0	MM0214055	HX-15A, MOTOR COOLING COIL INTERNAL INSPECTION				
253	1	MM0305857	MM1	76	P-010B	1P-10B REPLACE ROTATING ELEMENT	17	26APR04 06:00A	29APR04 05:59	DR-Y ML-Y ORT3-N R-N	0	MM0305857	1P-10B REPLACE ROTATING ELEMENT				
																	RESIDUAL HEAT REMOVAL PUMP 0305857
254	1	MM9924975A	MM1	76	HS-1	HS-1, REBUILD & TEST SNUBBER (SHOP)	13	26APR04 06:00A	29APR04 13:59	DR-Y ML-Y ORT3-N R-N	0	MM9924975A	HS-1, REBUILD & TEST SNUBBER (SHOP)				
																	HX-1A SG MAIN STEAM LINE WEST SNUBBER 9
255	1	MM0306443	MM1	76	HX-015A1	HX-015A1, CFC COIL INTERNAL	10	26APR04 18:00A	29APR04 10:59	DR-Y ML-Y ORT3-N R-N	17	MM0306443	HX-015A1, CFC COIL INTERNAL INSP/CLEANING				
																	CONTAINMENT ACCIDENT RECIRC HEAT EXCHANG
256	1	MM0306444	MM1	76	HX-015A2	HX-015A2, CFC COIL INTERNAL	10	26APR04 20:00A	29APR04 10:59	DR-Y ML-Y ORT3-N R-N	17	MM0306444	HX-015A2, CFC COIL INTERNAL INSP/CLEANING				
																	CONTAINMENT ACCIDENT RECIRC HEAT EXCHANG
257	1	MM0306445	MM1	76	HX-015A3	HX-015A3, CFC COIL INTERNAL	11	27APR04 04:00A	29APR04 11:59	DR-Y ML-Y ORT3-N R-N	16	MM0306445	HX-015A3, CFC COIL INTERNAL INSP/CLEANING				
																	CONTAINMENT ACCIDENT RECIRC HEAT EXCHAN
258	1	MM0306446	MM1	76	HX-015A4	HX-015A4, CFC COIL INTERNAL	23	27APR04 05:00A	30APR04 12:59	DR-Y ML-Y ORT3-N R-N	4	MM0306446	HX-015A4, CFC COIL INTERNAL INSP/CLEANING				
																	CONTAINM
259	1	MM0301141	MM1	76	HX-015A5	HX-015A5, CFC COIL INTERNAL	10	27APR04 13:00A	29APR04 10:59	DR-Y ML-Y ORT3-N R-N	17	MM0301141	HX-015A5, CFC COIL INTERNAL INSP/CLEANING				
																	CONTAINMENT ACCIDENT RECIRC HEAT EXCHANG
260	1	MM0301142	MM1	76	HX-015A6	HX-015A6, CFC COIL INTERNAL	10	27APR04 14:00A	29APR04 10:59	DR-Y ML-Y ORT3-N R-N	17	MM0301142	HX-015A6, CFC COIL INTERNAL INSP/CLEANING				
																	CONTAINMENT ACCIDENT RECIRC HEAT EXCHANG
261	1	MM0301144	MM1	76	HX-015A8	HX-015A8, CFC COIL INTERNAL	10	27APR04 15:00A	29APR04 10:59	DR-Y ML-Y ORT3-N R-N	17	MM0301144	HX-015A8, CFC COIL INTERNAL INSP/CLEANING				
																	CONTAINMENT ACCIDENT RECIRC HEAT EXCHANG
262	1	MM0301143	MM1	76	HX-015A7	HX-015A7, CFC COIL INTERNAL	22	27APR04 16:00A	30APR04 11:59	DR-Y ML-Y ORT3-N R-N	5	MM0301143	HX-015A7, CFC COIL INTERNAL INSP/CLEANING				
																	CONTAINM
263	1	MM0214054A	MM1	76	HX-001B	HX-1B, CLOSE SG HANDHOLES	10	28APR04 17:00*	29APR04 03:59	DR-N ML-Y ORT3-N R-M	0	MM0214054A	HX-1B, CLOSE SG HANDHOLES				
																	STEAM GENERATOR
264	1	MM0214052A	MM1	76	HX-001A	HX-1A, CLOSE SG HANDHOLES	10	28APR04 23:00*	29APR04 08:59	DR-N ML-Y ORT3-N R-M	0	MM0214052A	HX-1A, CLOSE SG HANDHOLES				
																	STEAM GENERATOR
265	1	MM0305857B	MM1	76	P-010B	P-10B, PERFORM FINAL ALIGNMENT	6	29APR04 07:00	29APR04 12:59	DR-Y ML-Y ORT3-N R-N	0	MM0305857B	P-10B, PERFORM FINAL ALIGNMENT				
																	RESIDUAL HEAT REMOVAL PUMP
266	1	MM9934380B	MM1	76	HS-601R-37	HS-601R-37A, REINSTALL SNUBBER	3	29APR04 08:00*	29APR04 10:59	DR-Y ML-Y ORT3-N R-N	0	MM9934380B	HS-601R-37A, REINSTALL SNUBBER AFTER TESTING				
																	PZR PORV HEADER SNUBBER
267	2	MM0400329	MM1	76	P-002A	2P-2A SEAL LEAK	10	29APR04 08:00*	29APR04 17:59	DR-Y ML-Y ORT3-N R-N	0	MM0400329	2P-2A SEAL LEAK				
																	CHARGING PUMP
268	1	MM9934376A	MM1	76	HS-15	HS-15, REBUILD & TEST SNUBBER (SHOP)	30	29APR04 14:00	02MAY04 10:59	DR-Y ML-Y ORT3-N R-N	0	MM9934376A	HS-15, REBUILD & TEST SNUBBER (SHOP)				

after 28APR04 12:00

U1R28 WORKING SCHEDULE

after 28APR04 12:00

#	U	ID	RESP	WO ST	EQID	DESCRIPTION	RD	ES	EF	RISK	MF	APR					
												Wed 28	Thu 29	Fri 30			
												8,10,12,14,16,18,20,22	0, 2, 4, 6, 8, 10,12,14,16,18,20,22	0, 2, 4, 6, 8, 10,12,14,16,18,20,22			
MECHANICAL MAINTENANCE MM1 RIDINGS/ BRITTINGHAM												MM1					
269	1	MM0214187A	MM1	76	C-2	INSPECT UPPER HATCH	20	29APR04 18:00*	01MAY04 02:59	DR-Y ML-Y ORT3-N R-N	0						MM0214187A INSPECT UPPER HATCH 0214187
270	1	MM0407701	MM1	28	CV-01296	CV-1296, REMOVE CLOTH FROM PIPE	1	30APR04 09:00*	30APR04 09:59	DR-Y ML-Y ORT3-N R-N	355						MM0407701 CV-1296, REMOVE CLOTH FROM PIPE 0407701
271	1	MM0310576	MM1	21	RD-05975	1RD-5975 RUPTURE DISC CHANGE OUT	8	30APR04 12:00*	30APR04 20:59	DR-Y ML-Y ORT3-N R-N	0						MM0310576 1RD-5975 RUPTURE DISC CHANGE OUT 0310576
272	1	MM-8857A1	MM1	82	HX-015B	HX-15B, PERFORM SW LEAK CHECK & INSTALL	6	30APR04 12:00	01MAY04 06:59	DR-Y ML-Y ORT3-N R-N	0						MM-8857A1 HX-15B, PERFORM SW LEAK CHECK & INSTALL 0214064
MECHANICAL MAINTENANCE MM2 BONENFANT (BOP)												MM2					
273	1	MM0306054	MM2	76	P-028A	P-028A - CONTINUE OVERHAUL MAIN FEED	5	18APR04 11:00A	28APR04 16:59	DR-Y ML-Y ORT3-N R-N	0						MM0306054 P-028A - CONTINUE OVERHAUL MAIN FEED PUMP STEAM GENERATOR FEED PUMP 0306054
274	1	MM0311887A	MM2	76	HX-021B	1HX-21B CLOSE HX AFTER ECT	4	25APR04 06:00A	28APR04 15:59	DR-Y ML-Y ORT3-N R-N	0						MM0311887A 1HX-21B CLOSE HX AFTER ECT HP FEEDWATER HEATER 5B 0311887
275	1	MM0214048	MM2	76	HS-CS-01	HS-CS-01, REMOVE/REPLACE	14	27APR04 08:00A	29APR04 14:59	DR-Y ML-Y ORT3-N R-N	0						MM0214048 HS-CS-01, REMOVE/REPLACE SNUBBER W/REBUILT CONDENSATE LINE GB-4 SNUBBER 0214048
276	1	MM0305792	MM2	76	T-052B	T-052B - OPEN/CLEAN AND INSPECT LO	5	27APR04 14:00A	28APR04 16:59	DR-Y ML-Y ORT3-N R-N	118						MM0305792 T-052B - OPEN/CLEAN AND INSPECT LO RESERVOIR P-288 SGFP LUBE OIL RESERVOIR 0305792
277	1	MM0214129	MM2	76	P-029-T	EMERGENCY GOV INSPECTION P-29-T	6	28APR04 12:00	29APR04 06:59	DR-Y ML-Y ORT3-N R-N	14						MM0214129 EMERGENCY GOV INSPECTION P-29-T 1P-29 AUX FEEDWATER TURBINE-DRIVEN PUMP TURBINE
278	1	MM0305777	MM2	76	HX-048	1HX-48 PLUG TUBES - CONTINGENCY WO	10	28APR04 12:00*	29APR04 10:59	DR-Y ML-Y ORT3-N R-N	0						MM0305777 1HX-48 PLUG TUBES - CONTINGENCY WO GLAND STEAM CONDENSER 0305777
279	1	MM0214128	MM2	76	P-029-T	P-29-T, INSPECT IB & OB BEARING OIL COOLERS	20	28APR04 12:00*	30APR04 09:59	DR-Y ML-Y ORT3-N R-N	0						MM0214128 P-29-T, INSPECT IB & OB BEARING OIL COOLERS 1P-29 AUX FEEDWATER TURBINE-DRIVEN PUMP TURBINE
280	1	MM0207075	MM2	76	FE-00134	1FE-134 REPL FLANGE GASKETS	8	28APR04 18:00*	29APR04 01:59	DR-Y ML-Y ORT3-N R-N	25						MM0207075 1FE-134 REPL FLANGE GASKETS 1HX-3A/B NON-REGEN HX OUTLET FLOW ELEMENT
281	0	MM0403661	MM2	77	DA-03056B	DA-3056B TEST VALVE BY 5/3/04	8	29APR04 07:00*	29APR04 14:59	DR-Y ML-Y ORT3-N R-N	0						MM0403661 DA-3056B TEST VALVE BY 5/3/04 G-02 EDG T-61B START AIR RECEIVER RELIEF VALVE
282	1	MM0214094A	MM2	76	HX-048	HX-48, CLOSE HX FOR CLEANING/INSP	16	29APR04 11:00*	30APR04 15:59	DR-Y ML-Y ORT3-N R-N	0						MM0214094A HX-48, CLOSE HX FOR CLEANING/INSP GLAND STEAM CONDENSER 0214094
283	0	MM0403664	MM2	77	DA-03056C	DA-3056C TEST VALVE BY 5/3/04	8	29APR04 15:00*	29APR04 23:59	DR-Y ML-Y ORT3-N R-N	617						MM0403664 DA-3056C TEST VALVE BY 5/3/04 G-02 EDG T-61C START AIR RECEIVER RELIEF VALVE
284	1	MM0214130	MM2	76	P-029GOV-Z	CHANGE OIL P-29 GOV-Z	4	30APR04 10:00	30APR04 13:59	DR-Y ML-Y ORT3-N R-N	0						MM0214130 CHANGE OIL P-29 GOV-Z 1P-29 AUX FEEDWATER TURBINE-DRIVEN PUMP TURBINE
285	1	MM0305772	MM2	76	HX-021A	1HX-21A PLUG TUBES - CONTINGENCY WO	5	30APR04 10:00*	30APR04 14:59	DR-Y ML-Y ORT3-N R-N	0						MM0305772 1HX-21A PLUG TUBES - CONTINGENCY WO HP FEEDWATER HEATER 5B
286	0	MM0407967	MM2	74	K-026	K-26, AIR LINE LEAK	5	30APR04 12:00*	30APR04 16:59		0						MM0407967 K-26, AIR LINE LEAK SC

Run Date

28APR04 13:44

LT-03 STANDARD PUBLICATION
FL-03 Execution Publication Set

Sheet 16 of 30

after 28APR04 12:00

U1R28 WORKING SCHEDULE

after 28APR04 12:00

#	U	ID	RESP	WO ST	EQID	DESCRIPTION	RD	ES	EF	RISK	MF	APR				
												Wed 28	Thu 29	Fri 30		
MECHANICAL VALVE, VANDERVELDE/KENNEY												MMV				
305	1	MM0214031	MMV	76	CV-00257	CV-257, SWAP WITH SPARE	8	29APR04 07:00*	29APR04 14:59	DR-N ML-N ORT3-N R-N	0	MM0214031 CV-257, SWAP WITH SPARE 0214031 [REDACTED] 1T-4 VCT RELIEF TO T-8A-C CVCS HUT				
306	1	MM0303680	MMV	78	MS-02005	1MS-2005 - REMOVE VALVE TO PERFORM	10	29APR04 19:00	30APR04 04:59	DR-Y ML-Y ORT3-N R-M	0	MM0303680 1MS-2005 - REMOVE VALVE TO PERFO 0303680 [REDACTED] HX-1B SG HEADER SA				
307	1	MM0407614	MMV	76	MS-02057	1MS-2057 DID NOT MODULATE, REBUILD	20	29APR04 19:00*	01MAY04 20:59	DR-Y ML-Y ORT3-N R-N	0	MM0407614 1MS-2057 DID NOT MODULATE, REBUIL 0407614 [REDACTED]				
308	1	MM0303681	MMV	76	MS-02010	1MS-2010 - REMOVE VALVE TO PERFORM	12	30APR04 05:00	30APR04 17:59	DR-Y ML-Y ORT3-N R-M	0	MM0303681 1MS-2010 - REMOVE V 0303681 [REDACTED]				
NON-DESTRUCTIVE TESTING												NDE				
309	1	NG44CFC1ND	NDE	77	IST-SISI	NDE FOR FAC PROG - CONTAINMENT 44 FT	26	28APR04 08:00A	01MAY04 07:59	DR-Y ML-Y ORT3-Y R-N	0	NG44CFC1ND NDE FOR FAC PROG - CONTAINMENT 44 FT GEN AREA				
310	1	EP0301954	NDE	77	CV-00304B	CV-304B - CHECK VALVE CLOSURE	2	28APR04 17:00	28APR04 18:59	DR-Y ML-Y ORT3-Y R-N	20	EP0301954 CV-304B - CHECK VALVE CLOSURE RADIOGRAPHY 0301954 [REDACTED] 1P-1B RCP SEAL WATER INJECTION CHECK				
311	1	ND0304672B	NDE	76	HS-601R-73	HS-601R-73, PERFORM AS LEFT VT-3 ON	1	29APR04 11:00	29APR04 11:59	DR-Y ML-Y ORT3-Y R-N	349	ND0304672B HS-601R-73, PERFORM AS LEFT VT-3 ON SNUBBER 0304672 [REDACTED] PZR SRV RELIEF LINE SNUBBER (FORMER HS-17)				
312	1	ND9934380B	NDE	76	HS-601R-37	HS-601R-37A PERFORM AS-LEFT VT-3 ON	1	29APR04 11:00	29APR04 11:59	DR-Y ML-Y ORT3-Y R-N	169	ND9934380B HS-601R-37A PERFORM AS-LEFT VT-3 ON SNUBBER 9934380 [REDACTED] PZR PORV HEADER SNUBBER				
313	1	EP0301909	NDE	77	U1-CONTAIN	VISUAL INSPECTION OF CTMT LINER PLATE	80	30APR04 09:00*	10MAY04 08:59	DR-Y ML-Y ORT3-Y R-N	50	EP0301909 VISUAL INSPEC UNIT 1 CONTAINMENT 0301909 [REDACTED]				
314	1	EP0301951	NDE	77	CV-00295	CV-295 - CHECK VALVE CLOSURE	2	30APR04 17:00*	30APR04 18:59	DR-Y ML-Y ORT3-Y R-N	8	EP0301951 CV 0301951 [REDACTED]				
315	1	EP0301953	NDE	77	CV-00304A	CV-304A - CHECK VALVE CLOSURE	2	30APR04 17:00	30APR04 18:59	DR-Y ML-Y ORT3-Y R-N	0	EP0301953 CV 0301953 [REDACTED]				
316	1	EP0301955	NDE	77	CV-00383	CV-383 - CHECK VALVE CLOSURE	2	30APR04 17:00	30APR04 18:59	DR-Y ML-Y ORT3-Y R-N	8	EP0301955 CV 0301955 [REDACTED]				
OPERATIONS MIDSHIFT												OP1				
317	0	OP0215355	OP1	77	O-PC-MIDS	OPERATIONS MID SHIFT WEEKLY ROUTINE	6	23APR04 00:00A	29APR04 05:59	DR-Y ML-Y ORT3-N R-N	198	OP0215355 OPERATIONS MID SHIFT WEEKLY ROUTINE [REDACTED] OPERATIONS MID SHIFT WEEKLY ROUTINE 0215355				
318	0	OP0215374	OP1	77	TS-EP-001	POWER AVAILABILITY VERIFICATIONS	1	29APR04 00:00*	29APR04 00:59	DR-N ML-N ORT3-N R-N	203	OP0215374 POWER AVAILABILITY VERIFICATIONS 0215374 [REDACTED] POWER AVAILABILITY VERIFICATIONS				
319	0	OP0215400	OP1	76	O-PC-086	SAMPLE BDE BOTTOMS	1	29APR04 00:00*	29APR04 00:59	DR-N ML-N ORT3-N R-N	203	OP0215400 SAMPLE BDE BOTTOMS 0215400 [REDACTED] SAMPLE BDE BOTTOMS AND WASTE HOLDUP TANK (T-19)				
320	2	OP0216033	OP1	77	O-TS-010AB	TS-10A, U2C AIR LOCK DOOR SEAL TEST	2	30APR04 00:00*	30APR04 01:59	DR-N ML-N ORT3-N R-M	195	OP0216033 TS-10A, U2C AIR LOCK DOOR S 0216033 [REDACTED] U2 CONT AIR LOCK DOOR S				
321	0	OP0215356	OP1	77	O-PC-MIDS	OPERATIONS MID SHIFT WEEKLY ROUTINE	49	30APR04 00:00*	06MAY04 06:59	DR-N ML-N ORT3-N R-N	148	OP0215356 OPERATIONS MID SHIFT WEEK OPERATIONS MID SHIFT WEEKLY ROUTINE 0215356 [REDACTED]				

Run Date

28APR04 13:44

LT-03 STANDARD PUBLICATION
FL-03 Execution Publication Set

Sheet 18 of 30

after 28APR04 12:00

U1R28 WORKING SCHEDULE

after 28APR04 12:00

#	U	ID	RESP	WO ST	EQID	DESCRIPTION	RD	ES	EF	RISK	MF	APR					
												Wed 28	Thu 29	Fri 30			
												8,10,12,14,16,18,20,22	0, 2, 4, 6, 8, 10,12,14,16,18,20,22	0, 2, 4, 6, 8, 10,12,14,16,18,20,22	0, 2, 4, 6, 8, 10,12,14,16,18,20,22	0, 2, 4, 6, 8, 10,12,14,16,18,20,22	
OPERATIONS DAYSHIFT												OP2					
322	0	OP0215434	OP2	76	O-PC-DAYS	OPERATIONS DAY SHIFT WEEKLY ROUTINE	24	26APR04 08:00A	01MAY04 14:59	DR-Y ML-Y ORT3-N R-N	182	OP0215434	OPERATIONS DAY SHIFT WEEKLY ROUTINE				
323	0	OP0215590	OP2	77	O-PC-001.1	PC 1.1, MONTHLY VENTILATION CHECKS	3	28APR04 12:00*	28APR04 14:59		203	OP0215590	PC 1.1, MONTHLY VENTILATION CHECKS				
324	0	OP0301340	OP2	77	O-PC-012.4	G-02 COOLANT SAMPLING	1	30APR04 08:00	30APR04 08:59	DR-N ML-N ORT3-N R-N	20						OP0301340 G-02 COOLANT S 0301340 G-02 EMERGEN
325	0	OP0301382	OP2	75	G-02-GOV	OBTAIN G-02 EDG GOVERNOR OIL SAMPLE	1	30APR04 08:00	30APR04 08:59	DR-N ML-N ORT3-N R-N	20						OP0301382 OBTAIN G-02 EDG 0301382 G-02 EDG GOVE
326	0	OP0301383	OP2	77	O-PC-012.2	G-02 EDG VIBRATION (QUARTERLY)	1	30APR04 08:00	30APR04 08:59	DR-N ML-N ORT3-N R-N	20						OP0301383 G-02 EDG VIBRAT 0301383 G-02 EMERGEN
327	0	OP0301343	OP2	77	O-TS-082	TS-82, G-02 EMERGENCY DIESEL	6	30APR04 08:00*	30APR04 13:59	DR-N ML-N ORT3-N R-M	0						OP0301343 TS-82, G-02 EMER 0301343 G-02 EM
OPERATIONS SWINGSHIFT												OP3					
328	0	OP0215624	OP3	77	O-PC-043.3	CLEAN SERVICE WATER STRAINERS	7	22APR04 16:00A	28APR04 22:59	DR-N ML-N ORT3-N R-N	203	OP0215624	CLEAN SERVICE WATER STRAINERS				
329	2	U2GNDR008	OP3		O-PC-021.3	DRAIN U2 MAIN ELECTRICAL	1	28APR04 16:00*	28APR04 16:59	DR-Y ML-Y ORT3-Y R-N	0	U2GNDR008	DRAIN U2 MAIN ELECTRICAL GENERATOR PER PC 21.3				
330	0	OP0215550	OP3	77	O-PC-SWING	OPS SWING SHIFT WEEKLY ROUTINE	49	28APR04 16:00*	04MAY04 22:59	DR-N ML-N ORT3-N R-N	161	OP0215550	OPS SWING SHIFT WEEKLY ROUTINE				
331	2	U2GNDR009	OP3		O-PC-021.3	DRAIN U2 MAIN ELECTRICAL	1	30APR04 16:00	30APR04 16:59	DR-Y ML-Y ORT3-Y R-N	0						U2GNDR009 DRA
332	0	OP0301450	OP3	77	O-IT-0014.	IT-14, FO TRANSFER SYSTEM PUMPS/	3	30APR04 16:00*	30APR04 18:59	DR-N ML-N ORT3-N R-M	18						OP0301450 IT-14 0301450
333	0	OP0301451	OP3	77	O-IT-0100.	IT-100, SEAT LKG TEST OF DA-200 AND	3	30APR04 16:00*	30APR04 18:59	DR-N ML-N ORT3-N R-M	18						OP0301451 IT-10 0301451
OPERATIONS												OPS					
334	1	RP1C-030	OPS		O-RP-001C	FUEL MOTION AND INSERT SHUFFLE	53	25APR04 08:00A	30APR04 16:59	DR-N ML-N ORT3-N R-M	0	RP1C-030	FUEL MOTION AND INSERT SHUFFLE				
335	1	OP9950097	OPS	76	CV-00371A-	CV-371A-S PMT STROKE PER IT 320	1	28APR04 12:00	28APR04 12:59	DR-N ML-Y ORT3-N R-N	48	OP9950097	CV-371A-S PMT STROKE PER IT 320				LETDOWN LINE CONTAINMENT ISOLATION SOLENOID 9950097
336	1	EP0403494A	OPS	76	PT-RCS-1	OPERATING SUPPORT OF INITIAL RCS	4	28APR04 12:00*	28APR04 15:59	DR-Y ML-Y ORT3-N R-N	315	EP0403494A	OPERATING SUPPORT OF INITIAL RCS WALKDOWN				REACTOR COOLANT SYSTEM (RCS) PRESSURE TEST - IN/0403494
337	1	IT-700	OPS	77	O-IT-0700	REACTOR COOLANT GAS VENT VALVES	4	28APR04 12:00*	28APR04 15:59	DR-N ML-N ORT3-N R-N	118	IT-700	REACTOR COOLANT GAS VENT VALVES				UNIT 1 REACTOR COOLANT GAS VENT VALVES (CSD) 0215924
338	1	O-RT-068B	OPS	77	O-RT-068	POST LLRT ON P-1A CCW LINES	4	28APR04 12:00	28APR04 15:59	DR-N ML-N ORT3-N R-N	299	O-RT-068B	POST LLRT ON P-1A CCW LINES (CONTINGENCY)				CCW TO AND FROM P-1A (P-15/P-17) 0216001
339	1	IT-320AX	OPS	77	O-IT-0320A	CV-294 LIFT TEST (SEAL RETURN)	4	28APR04 15:00	28APR04 19:59	DR-N ML-N ORT3-N R-N	0	IT-320AX	CV-294 LIFT TEST (SEAL RETURN)				RCP SEAL RET PIPE PENETR THERMAL RELIEF CHECK TE

Run Date 28APR04 13:44

LT-03 STANDARD PUBLICATION
FL-03 Execution Publication Set

Sheet 19 of 30

after 28APR04 12:00

U1R28 WORKING SCHEDULE

after 28APR04 12:00

#	U	ID	RESP	WO ST	EQID	DESCRIPTION	RD	ES	EF	RISK	MF	APR							
												Wed 28	Thu 29	Fri 30					
OPERATIONS												OPS							
340	1	X04-005	OPS		X-04	IPTE BRIEF TO DE-ENERGIZE 1X-04	1	28APR04 16:00*	28APR04 16:59	DR-N ML-N ORT3-N R-M	0	X04-005 IPTE BRIEF TO DE-ENERGIZE 1X-04 HIGH VOLTAGE STATION AUXILIARY TRANSFORMER							
341	1	OP0306894	OPS	72	AF-04000-M	1AF-4000-M PMT STROKE PER IT-8A	2	28APR04 16:00	28APR04 17:59	DR-Y ML-Y ORT3-N R-N	342	OP0306894 1AF-4000-M PMT STROKE PER IT-8A 0306894 1P-29 AFP DISCHARGE 1HX-1B SG INLET ISOLATION MO							
342	1	X04-010	OPS		X-04	CROSSTIE 1A-03 & 1A-04 TO UNIT 2	1	28APR04 17:00	28APR04 17:59	DR-N ML-N ORT3-N R-M	0	X04-010 CROSSTIE 1A-03 & 1A-04 TO UNIT 2							
343	1	X04-020	OPS		X-04	DE-ENERGIZE X-04	2	28APR04 19:00	28APR04 20:59	DR-N ML-N ORT3-N R-M	0	X04-020 DE-ENERGIZE X-04							
344	1	O-RT-027	OPS	77	O-RT-027	LLRT SEAL RTRN/EXCES	4	28APR04 20:00*	28APR04 23:59	DR-N ML-N ORT3-N R-N	74	O-RT-027 LLRT SEAL RTRN/EXCES 0215966 REACTOR COOLANT PUMP SEAL RETURN (P-11)							
345	1	O-RT-043	OPS	77	O-RT-043	LLRT CONT SAMPLING LINE	4	28APR04 20:00*	28APR04 23:59	DR-N ML-N ORT3-N R-N	389	O-RT-043 LLRT CONT SAMPLING LINE 0215979 CONTAINMENT SAMPLING LINE (F-31B)							
346	1	O-RT-034B	OPS	77	O-RT-034	POST LLRT OF NORMAL CHARGING	4	29APR04 00:00	29APR04 03:59	DR-N ML-N ORT3-N R-N	0	O-RT-034B POST LLRT OF NORMAL CHARGING 0215972 NORMAL CHARGING LINE (P-26)							
347	1	OP0215187	OPS	76	SI-00878A-	SI-878A PMT STROKE PER IT-210	1	29APR04 01:00	29APR04 01:59	DR-N ML-N ORT3-N R-N	0	OP0215187 SI-878A PMT STROKE PER IT-210 0215187 P-15B SI PUMP R-1 REACTOR VESSEL INJECTION OPER							
348	1	OP0403302	OPS	76	SI-00857B-	SI-857B PERFORM PMT STROKE PER IT 40	1	29APR04 02:00	29APR04 02:59	DR-N ML-N ORT3-N R-N	0	OP0403302 SI-857B PERFORM PMT STROKE PER IT 40 0403302 HX-11B RHR HX OUTLET TO P-15B SI PUMP SUCTION OP							
349	1	RF-490	OPS	77	O-RF-490	TEST AF EXH STACK DRAIN LINE	2	29APR04 02:00*	29APR04 03:59	DR-N ML-N ORT3-N R-N	333	RF-490 TEST AF EXH STACK DRAIN LINE 0215945 1P-29 AFP EXHAUST STACK DRAIN LINE CHECK							
350	1	O-RT-040	OPS	77	O-RT-040	LLRT P-1B SEAL SUPPLY	4	29APR04 02:00*	29APR04 05:59	DR-N ML-N ORT3-N R-N	0	O-RT-040 LLRT P-1B SEAL SUPPLY 0215977 SEAL INJECTION TO 1P-1B (P-29B)							
351	1	O-RT-030	OPS	77	O-RT-030	LLRT RCDT VENT HEADER	4	29APR04 07:00*	29APR04 10:59	DR-Y ML-Y ORT3-N R-N	329	O-RT-030 LLRT RCDT VENT HEADER 0215968 RCDT TO VENT HEADER (P-12C)							
352	1	O-RT-039	OPS	77	O-RT-039	LLRT P-1A SEAL SUPPLY	4	29APR04 07:00*	29APR04 10:59	DR-N ML-N ORT3-N R-N	29	O-RT-039 LLRT P-1A SEAL SUPPLY 0215976 SEAL INJECTION TO 1P-1A (P-29A)							
353	1	O162A-020	OPS		HX-001B	FILL S/G B TO WLU AND ADD CHEMICALS	6	29APR04 07:00	29APR04 12:59	DR-N ML-N ORT3-N R-N	0	O162A-020 FILL S/G B TO WLU AND ADD CHEMICALS Filling B S/G using auxiliary feed							
354	0	OPS-037-08	OPS	76	D72-16-15	IWP-037-08 OPS PMT & ALIGNMENT POST MOD	1	29APR04 09:00	29APR04 09:59	DR-N ML-N ORT3-N R-N	0	OPS-037-08 IWP-037-08 OPS PMT & ALIGNMENT POST MOD 0306113 PWR TO 1C-04 REACTOR AND CVCS CONTROL BOARD							
355	1	IT-531C	OPS	77	O-IT-0531	REMOVE SUMP B SCREEN	4	29APR04 10:00	29APR04 13:59	DR-N ML-N ORT3-N R-N	0	IT-531C REMOVE SUMP B SCREEN 0215919 UNIT 1 CONT SUMP B SUCTION LINE LEAK TEST							
356	1	O-RT-066C	OPS	77	O-RT-066C	LLRT CONT PRESSURE TRANSMITTER LINE	3	29APR04 11:00	29APR04 13:59	DR-N ML-N ORT3-N R-N	343	O-RT-066C LLRT CONT PRESSURE TRANSMITTER LINE 0215999 CONTAINMENT PRESSURE (P-32A)							
357	1	O162A-010	OPS		HX-001A	FILL S/G A TO WLU AND ADD CHEMICALS	5	29APR04 13:00	29APR04 17:59	DR-N ML-N ORT3-N R-N	0	O162A-010 FILL S/G A TO WLU AND ADD CHEMICALS							
358	1	O1-135B	OPS		P-010B	FILL & VENT RHR TRAIN B	8	29APR04 14:00	29APR04 22:59	DR-N ML-N ORT3-N R-N	0	O1-135B FILL & VENT RHR TRAIN B							

Run Date

28APR04 13:44

LT-03 STANDARD PUBLICATION
FL-03 Execution Publication Set

Sheet 20 of 30

after 28APR04 12:00

U1R28 WORKING SCHEDULE

after 28APR04 12:00

#	U	ID	RESP	WO ST	EQID	DESCRIPTION	RD	ES	EF	RISK	MF	APR														
												Wed 28			Thu 29				Fri 30							
												8	10	12,14,16,18,20,22	0	2	4	6	8	10	12,14,16,18,20,22	0	2	4	6	8
OPERATIONS												OPS														
359	1	OP0309955	OPS	82	G-06	PMT OF 1G-06 ROD DRIVE MG SET IAW OI 31	2	29APR04 15:00*	29APR04 16:59	DR-N ML-N ORT3-N R-N	79	OP0309955 PMT OF 1G-06 ROD DRIVE MG SET IAW OI 31 0309955 [] ROD CONTROL MG SET														
360	1	RF-070	OPS	77	O-RF-070	RF-70, CTMT FIRE HOSE SURVEILLANCE	8	29APR04 15:00	29APR04 23:59	DR-N ML-N ORT3-N R-N	74	RF-070 RF-70, CTMT FIRE HOSE SURVEILLANCE 0215935 [] FIRE HOSE AND FIRE STATION														
361	1	O-RT-052A	OPS	77	O-RT-052	PRE LLRT HX-1B SAMPLE LINE	4	29APR04 16:00	29APR04 20:59		0	O-RT-052A PRE LLRT HX-1B SAMPLE LINE 0215987 [] B STEAM GENERATOR SAMPLE ISC														
362	1	OP0300992	OPS	76	SC-00966C	PMT STROKE SC-966C PER IT 60	1	29APR04 19:00	29APR04 19:59	DR-N ML-N ORT3-N R-N	76	OP0300992 PMT STROKE SC-966C PER IT 60 0300992 [] FC HOT LEG SAMPLE SOLENOID														
363	1	IT-531B	OPS	77	O-IT-0531	LRPM RHR TO SUMP B TRAIN B	12	29APR04 23:00	30APR04 11:59	DR-N ML-N ORT3-N R-N	0	IT-531B LRPM RHR TO SUMP B TRAIN B 0215919 [] UNIT 1 CON														
364	0	OP0215147	OPS	76	AF-04023-O	AF-4023 PMT STROKE PER IT-10A	2	30APR04 01:00	30APR04 02:59	DR-N ML-N ORT3-N R-N	200	OP0215147 AF-4023 PMT STROKE PER IT 0215147 [] P-38A AFP DISCHARGE TO														
365	1	Y04PREPS	OPS		Y-04	PREPS FOR 1Y-04 OUTAGE	12	30APR04 01:00	30APR04 12:59		0	Y04PREPS PREPS FOR 1Y-04 OUTAGE []														
366	1	OP0306896	OPS	76	MS-02020-M	1MS-2020-M PMT STROKE PER IT-8A	2	30APR04 03:00	30APR04 04:59	DR-N ML-N ORT3-N R-N	278	OP0306896 1MS-2020-M PMT STROKE 0306896 [] HX-1A SG HEADER P-2														
367	1	T-TU-061M	OPS		EH	REVISE JET CLEARANCE FOR EHC AFTER OIL	2	30APR04 08:00	30APR04 09:59		608	T-TU-061M REVISE JET CLEA []														
368	1	CL10C010	OPS		CL-10C	TURBINE HALL SW VALVE LINEUPS	6	30APR04 08:00	30APR04 13:59	DR-N ML-N ORT3-N R-N	356	CL10C010 TURBINE HALL SW [] TURBIN														
369	1	OP0300957	OPS	76	WG-01788-O	WG-1788 PMT STROKE PER IT 60	1	30APR04 12:00*	30APR04 12:59	DR-Y ML-Y ORT3-N R-N	4	OP0300957 WG-1788 P 0300957 [] T-16 RCD														
370	0	OI-39C	OPS			SECURE PAB VENTILATION	2	30APR04 12:00	30APR04 13:59		0	OI-39C SECURE PA []														
371	1	OP0205513	OPS	76	B52-433E	CW-00003 PERFORM PMT STROKE	1	30APR04 13:00	30APR04 13:59	DR-N ML-N ORT3-N R-N	0	OP0205513 CW-00003 0205513 [] PWR TO														
372	1	IT-003A	OPS	77	O-IT-0003A	RHR P&V TEST IN DHR	5	30APR04 13:00	30APR04 17:59	DR-N ML-N ORT3-N R-N	0	IT-003A RHR P&V 0215886 [] R														
373	1	SOP-B41A	OPS		B-41	PREPS FOR DE-ENERGIZING 1B-41	12	30APR04 13:00	01MAY04 00:59	DR-Y ML-Y ORT3-N R-N	0	SOP-B41A PREPS F []														
374	0	OP0215146	OPS	76	AF-04021-O	AF-4021 PMT STROKE PER IT-10A	2	30APR04 14:00	30APR04 15:59	DR-N ML-N ORT3-N R-N	275	OP0215146 AF-4021 0215146 [] P-38														
375	1	SOP-B01C	OPS		B-01	IPTE BRIEF FOR 1B-01 TRANSFER	2	30APR04 14:00	30APR04 15:59	DR-N ML-N ORT3-N R-N	0	SOP-B01C IPTE BR []														
376	1	SOP-B04A	OPS		B-42	PREPARATION FOR 1B-42 OUTAGE	8	30APR04 14:00	30APR04 21:59	DR-N ML-N ORT3-N R-N	6	SOP-B04A PREPAR []														
377	1	OP9C-080	OPS		OP-9C	SECURE CONT PURGE FOR 1Y-04 OUTAGE	1	30APR04 15:00	30APR04 15:59		0	OP9C-080 SECUR []														

after 28APR04 12:00

U1R28 WORKING SCHEDULE

after 28APR04 12:00

#	U	ID	RESP	WO ST	EQID	DESCRIPTION	RD	ES	EF	RISK	MF	APR				
												Wed 28	Thu 29	Fri 30		
												8,10,12,14,16,18,20,22	0, 2, 4, 6, 8, 10,12,14,16,18,20,22	0, 2, 4, 6, 8, 10,12,14,16,1		
OPERATIONS												OPS				
378	1	OP0300958	OPS	76	WG-01789-O	WG-1789 PMT STROKE PER IT 60	1	30APR04 16:00*	30APR04 16:59	DR-Y ML-Y ORT3-N R-N	0					OP0300958 WG-0300958 T-1
379	1	OP9C-070	OPS		OP-9C	SECURE CONTAINMENT PURGE FOR IWP	1	30APR04 16:00	30APR04 16:59	DR-N ML-N ORT3-N R-N	0					OP9C-070 SEC []
380	1	RF-400	OPS	77	O-RF-400	REFUELING CAVITY SKIMMER PUMP FILTER	3	30APR04 17:00	30APR04 20:59	DR-N ML-N ORT3-N R-N	325					RF-400 RE 0215943 []
381	1	O-RT-053B	OPS	77	O-RT-053	LLRT RCDT TO GAS ANALYZER - POST ORT	4	30APR04 17:00	30APR04 21:59	DR-N ML-N ORT3-N R-N	297					O-RT-053B LL 0215988 []
382	1	PT-FP-001	OPS	77	PT-FP-001	TEST CONTAINMENT FIRE DETECTORS	8	30APR04 17:00*	01MAY04 17:59	DR-N ML-N ORT3-N R-N	104					PT-FP-001 TE 0216009 []
PRODUCTION PLANNING												PPG				
383	1	SIB01Z	PPG		MILESTONE	CLOSE HHSI B LOOP WORK WINDOW	0	29APR04 05:00	29APR04 04:59	DR-N ML-N ORT3-N R-N	0			SIB01Z CLOSE HHSI B LOOP WORK WINDOW [] [] END HIGH HEAD SAFETY INJECTION B LOOP WORK		
384	1	MSB24Z	PPG		MILESTONE	END S/G B CL-1E WORK INSIDE CONTAINMENT	0	29APR04 16:00	29APR04 15:59	DR-N ML-N ORT3-N R-N	0			MSB24Z END S/G B CL-1E WORK INSIDE CONTAINMENT [] [] S/G B SECONDARY & FEED/STEAM/BLOWDOWN		
385	1	MSB25A	PPG		MILESTONE	START S/G B CL-1E WORK OUTSIDE	0	29APR04 16:00	29APR04 15:59	DR-N ML-N ORT3-N R-N	0			MSB25A START S/G B CL-1E WORK OUTSIDE CONTAINMENT [] [] S/G B SECONDARY & FEED/STEAM/BLOWDOWN		
386	1	MSA24Z	PPG		MILESTONE	END S/G A CL-1E WORK INSIDE CONTAINMENT	0	29APR04 22:00	29APR04 21:59	DR-N ML-N ORT3-N R-N	0			MSA24Z END S/G A CL-1E WORK INSIDE CONTAINMENT [] [] S/G B SECONDARY & FEED/STEAM/BLOWDOWN		
387	1	MSA25A	PPG		MILESTONE	START S/G A CL-1E WORK OUTSIDE	0	29APR04 22:00	29APR04 21:59	DR-N ML-N ORT3-N R-N	0			MSA25A START S/G A CL-1E WORK OUTSIDE CONTAINMENT [] [] S/G B SECONDARY & FEED/STEAM/BLOWDOWN		
388	1	SWT01Z	PPG		MILESTONE	CLOSE TURBINE SERVICE WATER WORK	0	30APR04 08:00	30APR04 07:59	DR-N ML-N ORT3-N R-N	0			SWT01Z CLOSE TURBINE SERVICE WATER WORK [] [] TURBINE BUILDING		
389	1	FUELMOVE4	PPG		MILESTONE	REACTOR REFUELED	0		30APR04 16:59	DR-N ML-N ORT3-N R-N	656			FUELMOVE4 REACTOR REFUELED []		
390	1	SIA01U	PPG		MILESTONE	END OF SIA TRAIN ALIGNED AS REACTIVITY	0	30APR04 17:00	30APR04 16:59	DR-N ML-N ORT3-N R-N	0			SIA01U END OF SIA TRAIN ALIGNED AS REACTIVITY []		
391	1	RP1B-071	PPG		O-RP-001B	RELAX CLOSURE POST CORE SHUFFLE	1	30APR04 17:00	30APR04 17:59	DR-N ML-N ORT3-N R-N	79			RP1B-071 RELAX CLOSURE POST CORE SHUFFLE []		
REACTOR ENGINEERING												PRE				
392	1	RP1C-180	PRE		RP-1C	CORE MAPPING	2	30APR04 17:00	30APR04 19:59	DR-N ML-N ORT3-N R-N	0					RP1C-180 CORE MAPPING []
RADIATION PROTECTION												RP				
393	2	RP-F32SMPL	RP		PBF-4013E	COLLECT CHARCOAL SAMPLE FROM F-32	5	29APR04 08:00*	29APR04 12:59	DR-Y ML-Y ORT3-Y R-N	145			RP-F32SMPL COLLECT CHARCOAL SAMPLE FROM F-32 CLEANUP FACILITY []		
394	1	RP1C-010B	RP		O-RP-001C	DEPOST REFUEL BARRIERS	5	30APR04 17:00	30APR04 22:59	DR-Y ML-Y ORT3-Y R-N	0					RP1C-010B DEPOST REFUEL BARRIERS []

after 28APR04 12:00

U1R28 WORKING SCHEDULE

after 28APR04 12:00

#	U	ID	RESP	WO ST	EQID	DESCRIPTION	RD	ES	EF	RISK	MF	APR				
												Wed 28	Thu 29	Fri 30		
												9,10,12,14,16,18,20,22	0, 2, 4, 6, 8, 10,12,14,16,18,20,22	0, 2, 4, 6, 8, 10,12,14,16,18		
SITE DESIGN STRUCTURAL (CIVIL)												SDS				
395		SD_GSI-191	SDS		CONT	ENGINEERING WALKDOWN - SUMP INTRUSION ISSUES	51	08APR04 08:00A	06MAY04 14:59	DR-Y ML-Y ORT3-Y R-N	48	SD_GSI-191 ENGINEERING WALKDOWN - SUMP INTRUSION ISSUES				
SECURITY GROUP												SEC				
396	1	SECCW03	SEC	76	B52-433E	SECURITY OFFICER REQUIRED FOR CW-0003 STROKE	1	30APR04 13:00	30APR04 13:59	DR-N ML-N ORT3-N R-N	129	SECCW03 SECURITY 0205513 PWR TC				
SITE PROGRAMS												SP				
397	1	SP-EVAL1	SP	76	R-1	REVIEW / EVALUATE UNDERHEAD INSPECTION RESULTS	24	30APR04 13:00	01MAY04 14:59	DR-Y ML-Y ORT3-Y R-N	0	SP-EVAL1 REVIEW / 0213472				
TURBINE GENERATOR GROUP												TGG				
398	1	TGSUPPORT	TGG		TG-01-T	PROVIDE CRANE, RIGGER, AND TOOLROOM	147	13APR04 09:00A	07MAY04 18:59	DR-Y ML-Y ORT3-Y R-N	220	TGSUPPORT PROVIDE CRANE, RIGGER, AND TOOLROOM SUPPORT(PT2)				
399	1	TG0302140	TGG	76	PIPING CRO	CROSSUNDER PIPING INSPECTION / REPAIRS(PT2)	19	20APR04 11:00A	30APR04 14:59	DR-Y ML-Y ORT3-Y R-N	0	TG0302140 CROSSUNDER PIPING INSPECTION / REPAIRS(PT2) HP TU				
400	1	TG0302134B	TGG	76	MS-02027	MS-2027 - REINSTALL RH STOP VALVE	2	21APR04 08:00A	28APR04 13:59	DR-Y ML-Y ORT3-Y R-N	17	TG0302134B MS-2027 - REINSTALL RH STOP VALVE HP TURBINE RIGHT HAND STOP 0302134				
401	1	TG0215000	TGG	76	TG-01-T1	LP1 - EROSION SHIELDS OVER BRG SLOPED DRAIN LN	15	26APR04 08:00A	29APR04 16:59	DR-Y ML-Y ORT3-Y R-N	0	TG0215000 LP1 - EROSION SHIELDS OVER BRG SLOPED DRAIN LN LP1 LOW PRESSURE TURBINE 0215000				
402	1	TGHX22AASY	TGG	76	HX-022A	MSR A TUBESIDE REASSEMBLY	5	26APR04 11:00A	28APR04 16:59	DR-Y ML-Y ORT3-Y R-N	0	TGHX22AASY MSR A TUBESIDE REASSEMBLY MOISTURE SEPARATOR REHEATER 0214083				
403	1	TG0302132	TGG	76	LO-00291	LO-291 - OVERHAUL PRESSURE REDUCING VALVE	19	28APR04 07:00A	30APR04 14:59	DR-Y ML-Y ORT3-Y R-N	0	TG0302132 LO-291 - OVERHAUL PRESSURE REDUCING VALVE TURB				
404	1	TG-30760	TGG	76	TG-01-T	CHART HP SPINDLE - FINAL ASSEMBLY	15	28APR04 08:00A	29APR04 02:59	DR-Y ML-Y ORT3-Y R-N	0	TG-30760 CHART HP SPINDLE - FINAL ASSEMBLY HIGH PRESSURE TURBINE 0302153				
405	1	TG9818789	TGG	76	TG-01-T	1TG-01-T REPLACE STEAM CHEST FITTING	3	28APR04 09:00A	28APR04 14:59	DR-Y ML-Y ORT3-Y R-N	109	TG-01-T REPLACE STEAM CHEST FITTING HIGH PRESSURE TURBINE				
406	1	TG0214999	TGG	76	TG-01-T2	LP2 - EROSION SHIELDS OVER BRG SLPD DRAIN LN-PT2	30	28APR04 12:00	04MAY04 09:59	DR-Y ML-Y ORT3-Y R-N	0	TG0214999 LP2 - EROSION SHIELDS OVER BRG SLPD DRAIN LN-PT2				
407	1	TG0302262	TGG	76	HG-00055	1HG-55 REPLACE HYDROGEN REGULATOR	20	28APR04 17:00*	30APR04 02:59	DR-Y ML-Y ORT3-Y R-N	105	TG0302262 1HG-55 REPLACE HYDROGEN REGULATOR TG-01 TG HYDROGEN HE				
408	1	TG0403278	TGG	10	Z-008	GAS LEAK DOWN STREAM OF TEST SOLENOID	20	28APR04 17:00*	30APR04 02:59	DR-Y ML-Y ORT3-Y R-N	0	TG0403278 GAS LEAK DOWN STREAM OF TEST SOLENOID TG-01 TURBINE GENERAT				
409	1	TG-30710	TGG	76	TG-01-T	INSPECT GOVERNOR PEDESTAL COMPONENTS	3	29APR04 00:00	29APR04 02:59	DR-Y ML-Y ORT3-Y R-N	0	TG-30710 INSPECT GOVERNOR PEDESTAL COMPONENTS 0302153 HIGH PRESSURE TURBINE				
410	1	TG-30430	TGG	76	TG-01-T	SET GOVERNOR PED. L/H OIL SEALS	3	29APR04 07:00	29APR04 09:59	DR-Y ML-Y ORT3-Y R-N	85	TG-30430 SET GOVERNOR PED. L/H OIL SEALS 0302153 HIGH PRESSURE TURBINE				
411	1	TG-30850	TGG	76	TG-01-T	INSTALL UPPER HALF INNER STEAM GLD CASINGS	5	29APR04 07:00	29APR04 11:59	DR-Y ML-Y ORT3-Y R-N	0	TG-30850 INSTALL UPPER HALF INNER STEAM GLD CASINGS 0302153 HIGH PRESSURE TURBINE				

Run Date

28APR04 13:44

LT-03 STANDARD PUBLICATION
FL-03 Execution Publication Set

Sheet 23 of 30

after 28APR04 12:00

U1R28 WORKING SCHEDULE

after 28APR04 12:00

#	U	ID	RESP	WO ST	EQID	DESCRIPTION	RD	ES	EF	RISK	MF	APR		
												Wed 28 8,10,12,14,16,18,20,22	Thu 29 0, 2, 4, 6, 8, 10,12,14,16,18,20,22	Fri 30 0, 2, 4, 6, 8, 10,12,14,16,18
TURBINE GENERATOR GROUP												TGG		
412	1	TG-30900	TGG	76	TG-01-T	INSTALL #2-3 BEARING PEDESTAL L/H OIL SEALS	5	29APR04 07:00	29APR04 11:59	DR-Y ML-Y ORT3-Y R-N	47			TG-30900 INSTALL #2-3 BEARING PEDESTAL L/H OIL SEALS 0302153 [REDACTED] HIGH PRESSURE TURBINE
413	1	TG0302136A	TGG	76	P-037A	P-037A - REASSEMBLE MAIN OIL PUMP	6	29APR04 07:00	29APR04 12:59	DR-Y ML-Y ORT3-Y R-N	0			TG0302136A P-037A - REASSEMBLE MAIN OIL PUMP 0302136 [REDACTED] TURBINE LUBE OIL PUMP (SHAFT DRIVEN)
414	1	TGHX22BASY	TGG	76	HX-022B	MSR B TUBESIDE REASSEMBLY	7	29APR04 07:00*	29APR04 13:59	DR-Y ML-Y ORT3-Y R-N	0			TGHX22BASY MSR B TUBESIDE REASSEMBLY 0214084 [REDACTED] MOISTURE SEPARATOR REHEATER
415	1	TG-30770	TGG	76	TG-01-T	INSTALL AND TIGHTEN HP UPPER HALF BLADE RINGS	17	29APR04 12:00	30APR04 08:59	DR-Y ML-Y ORT3-Y R-N	0			TG-30770 INSTALL AND TIGHTEN HP UPPER HALF BLADE RINGS 0302153 [REDACTED] HIGH PRESSURE TURBINE
416	1	TG0302136B	TGG	76	P-037A	P-037A - REASSEMBLE ZERO SPEED ASSEMBLY	4	29APR04 13:00	29APR04 16:59	DR-Y ML-Y ORT3-Y R-N	78			TG0302136B P-037A - REASSEMBLE ZERO SPEED ASSEMBLY 0302136 [REDACTED] TURBINE LUBE OIL PUMP (SHAFT DRIVEN)
417	1	TGHX22CASY	TGG	76	HX-022C	MSR C TUBESIDE REASSEMBLY	7	29APR04 14:00*	30APR04 12:59	DR-Y ML-Y ORT3-Y R-N	0			TGHX22CASY MSR C TUBESIDE REASSEMBLY 0214085 [REDACTED] MOISTURE SEPARATOR REHEATER
418	1	TG9949102B	TGG	76	TG-01-T1	LP1 - REMOVE SCAFFOLD AFTER BELLOWS	36	29APR04 17:00	01MAY04 08:59	DR-Y ML-Y ORT3-Y R-N	0			TG9949102B LP1 - REMOVE SCAFFOLD AFTER BELLOWS 9949102 [REDACTED]
419	1	TG0216167B	TGG	76	E-01	REINSTALL DUCT FOLLOWING EXCITER FUSE INSPECTION	4	29APR04 19:00	29APR04 22:59	DR-N ML-N ORT3-N R-N	0			TG0216167B REINSTALL DUCT FOLLOWING EXCITER FUSE INSPECTION 0216167 [REDACTED] TG-01 TURBINE GENERATOR EXCITER
420	1	TG0302113A	TGG	76	HX-052	HX-052 - REINSTALL GENERATOR EXCITER COOLER	4	29APR04 23:00	30APR04 02:59	DR-Y ML-Y ORT3-Y R-N	0			TG0302113A HX-052 - REINSTALL GENERATOR EXCITER COOLER 0302113 [REDACTED] TG-01 TGE-01 EXCITER COOLER
421	1	TG-HX52-PT	TGG	76	HX-052	HX-052 - PRESS TEST GEN EXCITER COOLER	4	30APR04 07:00	30APR04 10:59	DR-Y ML-Y ORT3-Y R-N	143			TG-HX52-PT HX-052 - PRESS TEST GEN EXCITER COOLER 0302113 [REDACTED] TG-01 TGE-01 EXCITER COOLER
422	1	TG0302141	TGG	76	RO-02711	RO-2711 - INTERSTAGE ORIFICE INSPECTION	7	30APR04 07:00*	30APR04 13:59	DR-Y ML-Y ORT3-Y R-N	0			TG0302141 RO-2711 - INTERSTAGE ORIFICE INSPECTION 0302141 [REDACTED] TG-01 HORIZONTAL JOINT
423	1	TG-30690	TGG	76	TG-01-T	HAND CLEAN HP CYL HORIZONTAL JOINT	6	30APR04 08:00	30APR04 13:59	DR-Y ML-Y ORT3-Y R-N	0			TG-30690 HAND CLEAN HP CYL HORIZONTAL JOINT 0302153 [REDACTED] HIGH PRESSURE TURBINE
424	1	TG-30820	TGG	76	TG-01-T	INSTALL #2 BEARING UPPER HALF	5	30APR04 09:00	30APR04 13:59	DR-Y ML-Y ORT3-Y R-N	0			TG-30820 INSTALL #2 BEARING UPPER HALF 0302153 [REDACTED] HIGH PRESSURE TURBINE
425	1	TG-30830	TGG	76	TG-01-T	INSTALL #1 BEARING UPPER HALF	5	30APR04 09:00	30APR04 13:59	DR-Y ML-Y ORT3-Y R-N	0			TG-30830 INSTALL #1 BEARING UPPER HALF 0302153 [REDACTED] HIGH PRESSURE TURBINE
426	1	TG-8376B	TGG	76	HX-023A	HX-023A - CLOSE TURBINE LUBE OIL COOLER	10	30APR04 10:00*	30APR04 19:59	DR-Y ML-Y ORT3-Y R-N	0			TG-8376B HX-023A - CLOSE TURBINE LUBE OIL COOLER 0213957 [REDACTED]
427	1	TG0302114B	TGG	77	SC-1A	COND FINAL INTERNAL INSP (1A)	2	30APR04 13:00	30APR04 14:59	DR-Y ML-Y ORT3-Y R-N	21			TG0302114B COND FINAL INTERNAL INSP (1A) 0302114 [REDACTED] COND FINAL INTERNAL INSP (1A)
428	1	TGHX22DASY	TGG	76	HX-022D	MSR D TUBESIDE REASSEMBLY	7	30APR04 13:00*	01MAY04 09:59	DR-Y ML-Y ORT3-Y R-N	84			TGHX22DASY MSR D TUBESIDE REASSEMBLY 0214086 [REDACTED] MOISTURE SEPARATOR REHEATER
429	1	TG-30870	TGG	76	TG-01-T	INSTALL HP OUTER CYL COVER & BOLTING	15	30APR04 14:00	03MAY04 08:59	DR-Y ML-Y ORT3-Y R-N	0			TG-30870 INSTALL HP OUTER CYL COVER & BOLTING 0302153 [REDACTED] HIGH PRESSURE TURBINE
430	1	TG0302142	TGG	76	RO-02712	RO-2712 - INTERSTAGE ORIFICE INSPECTION	7	30APR04 14:00	03MAY04 12:59	DR-Y ML-Y ORT3-Y R-N	0			TG0302142 RO-2712 - INTERSTAGE ORIFICE INSPECTION 0302142 [REDACTED]

Run Date

28APR04 13:44

LT-03 STANDARD PUBLICATION
FL-03 Execution Publication Set

Sheet 24 of 30

U1R28 WORKING SCHEDULE

#	U	ID	RESP	WO ST	EQID	DESCRIPTION	RD	ES	EF	RISK	MF	APR			
												Wed 28	Thu 29	Fri 30	
WORK CONTROL CENTER												WCC			
487	0	T-1644-H	WCC		AF-4021	0 AF AF-4021 EM REV0-1	2	29APR04 16:00	29APR04 17:59		15				T-1644-H 0 AF AF-4021 EM REV0-1 0011644 0 AF AF-4021 EM REV0-1
488	1	T-2081-H	WCC		HX-001B	1 MS HX-1B WLU MMV REV1-1	2	29APR04 16:00	29APR04 17:59		1				T-2081-H 1 MS HX-1B WLU MMV REV1-1 0012081 1 MS HX-1B WLU MMV REV1-1
489	1	T-0692-R	WCC		OI-124	1 MS OI-124 OPS REV0-1	1	29APR04 18:00	29APR04 18:59		406				T-0692-R 1 MS OI-124 OPS REV0-1 0010692 1 MS OI-124 OPS REV0-1
490	1	T-2606-R	WCC		SC-966C-S	1 SC SC-966C-S IC REV0-1	1	29APR04 18:00	29APR04 18:59		0				T-2606-R 1 SC SC-966C-S IC REV0-1 0012606 1 SC SC-966C-S IC REV0-1
491	2	T-8318-R	WCC		P-2A	2 CV P-2A MM REV0-1	1	29APR04 18:00	29APR04 18:59		678				T-8318-R 2 CV P-2A MM REV0-1 0018318 2 CV P-2A MM REV0-1
492	0	T-1645-H	WCC		AF-4023	0 AF AF-4023 EM REV0-1	2	29APR04 18:00	29APR04 19:59		0				T-1645-H 0 AF AF-4023 EM REV0-1 0011645 0 AF AF-4023 EM REV0-1
493	1	T-9892-R	WCC		W-001A1	1 VNCC W-1A1/1A2 EM REV0-1	1	29APR04 21:00	29APR04 21:59	DR-Y ML-Y ORT3-Y R-N	186				T-9892-R 1 VNCC W-1A1/1A2 EM REV0-1 0009892 1 VNCC W-1A1/1A2 EM REV0-1
494	1	T-2618-H	WCC		IT-531	1 SI IT-531 P-10B OPS REV0-1	2	29APR04 21:00	29APR04 22:59		0				T-2618-H 1 SI IT-531 P-10B OPS REV0-1 0012618 1 SI IT-531 P-10B OPS REV0-1
495	1	T-7941-H	WCC		MS-2084	1 MS MS-2084 REV0-1	3	29APR04 21:00	29APR04 23:59		127				T-7941-H 1 MS MS-2084 REV0-1 0017941 1 MS MS-2084 REV0-1
496	1	T-0689-H	WCC		P-010B	1 SI P-10B IT-531 OPS REV0-1	1	29APR04 22:00	29APR04 22:59		0				T-0689-H 1 SI P-10B IT-531 OPS REV0-1 0010689 1 SI P-10B IT-531 OPS REV0-1
497	1	T-0510-R	WCC		W-1B1/1B2	1 VNCC W-1B1/1B2 MM REV0-1	3	29APR04 22:00	30APR04 00:59		80				T-0510-R 1 VNCC W-1B1/1B2 MM REV0-1 0010510 1 VNCC W-1B1/1B2 MM REV0-1
498	1	T-2080-H	WCC		HX-001A	1 MS HX-1A WLU MMV REV1-1	3	29APR04 22:00	30APR04 00:59		4				T-2080-H 1 MS HX-1A WLU MMV REV1-1 0012080 1 MS HX-1A WLU MMV REV1-1
499	1	T-6122-R	WCC		CV-00296	1 CV CV-296 MMV REV0-1	1	30APR04 00:00	30APR04 00:59		46				T-6122-R 1 CV CV-296 MMV REV0-1 0015122 1 CV CV-296 MMV REV0-1
500	0	T-1645-R	WCC		AF-4023	0 AF AF-4023 EM REV0-1	1	30APR04 01:00	30APR04 01:59		219				T-1645-R 0 AF AF-4023 EM REV0-1 0011645 0 AF AF-4023 EM REV0-1
501	1	T-2815-R	WCC		MS-2020	1 MS MS-2020 EM REV0-1	1	30APR04 02:00	30APR04 02:59		0				T-2815-R 1 MS MS-2020 EM REV0-1 0012815 1 MS MS-2020 EM REV0-1
502	1	T-7373-R	WCC		Z-8	1 TU Z-8 TGG REV0-1	1	30APR04 03:00	30APR04 03:59		669				T-7373-R 1 TU Z-8 TGG REV0-1 0017373 1 TU Z-8 TGG REV0-1
503	1	T-7043-R	WCC		P-028A-M	1 CS P-28A-M EM REV0-1	1	30APR04 04:00	30APR04 04:59	DR-Y ML-Y ORT3-Y R-N	0				T-7043-R 1 CS P-28A-M EM REV0-1 0017043 1 CS P-28A-M EM REV0-1
504	1	T-7047-H	WCC		P-028A-M	1 CS P-28A-M EM REV1-1	1	30APR04 04:00	30APR04 04:59	DR-Y ML-Y ORT3-Y R-N	0				T-7047-H 1 CS P-28A-M EM REV1-1 0017047 1 CS P-28A-M EM REV1-1
505	1	T-0964-H	WCC		62/A01	1 MRR 62/A01 RMP 9302-1 EM REV0-1	1	30APR04 05:00	30APR04 05:59		1				T-0964-H 1 MRR 62/A01 RMP 9302-1 EM REV0-1 0010964 1 MRR 62/A01 RMP 9302-1 EM REV0-1

after 28APR04 12:00

U1R28 WORKING SCHEDULE

after 28APR04 12:00

#	U	ID	RESP	WO ST	EQID	DESCRIPTION	RD	ES	EF	RISK	MF	APR								
												Wed 28	Thu 29	Fri 30						
WORK CONTROL CENTER												WCC								
525	1	T-6929-H	WCC		D72-16-08	1 125V IWP 00-037-02 EM REV0-1	1	30APR04 17:00	30APR04 17:59		0									T-6929-H 1 1 0016929 1
526	1	T-6939-H	WCC		D72-21-08	1 125V IWP 00-037-07 EM REV0-1	1	30APR04 17:00	30APR04 17:59		19									T-6939-H 1 1 0016939 1
527	1	T-8022-H	WCC		IWP	1 480V IWP 01-128*E-FN (W-13B1) EM REV0-2	1	30APR04 17:00	30APR04 17:59	DR-N ML-N ORT3-N R-N	1									T-8022-H 1 4 0018022 1
528	1	T-8439-R	WCC		RC-526B	1 RC RC-526B MM REV0-1	1	30APR04 17:00	30APR04 17:59		143									T-8439-R 1 R 0018439 1
529	1	T-8710-R	WCC			1 SI REACTIVITY PATH DSS REV0-1	1	30APR04 17:00	30APR04 17:59		419									T-8710-R 1 S 0018710 1
530	1	T-8716-R	WCC		P-15A	1 SI P-15A FLOWPATH DSS REV0-1	1	30APR04 17:00	30APR04 17:59		419									T-8716-R 1 S 0018716 1
531	0	T-8731-R	WCC		K-26	0 EBA K-26 MM REV0-1	1	30APR04 17:00	30APR04 17:59		577									T-8731-R 0 E 0018731 0
532	1	T-0721-H	WCC		Z-024A	1 FH Z-24A RP-1B OPS REV0-1	2	30APR04 17:00	30APR04 18:59		78									T-0721-H 1 F 0010721
533	1	T-2622-H	WCC		Y-04	1 Y Y-4 EM REV0-1	2	30APR04 17:00*	30APR04 18:59		0									T-2622-H 1 Y 0012622
534	1	T-2726-H	WCC		VNPSE-3213	1 VNPSE VNPSE-3213 IC REV0-1	2	30APR04 17:00	30APR04 18:59		11									T-2726-H 1 V 0012726
535	1	T-2084-H	WCC		RVLJ	1 RC RVLJ RELIEFS MMV REV0-1	4	30APR04 17:00	30APR04 20:59		10									T-2084-H 1 R 0012084
536	1	T-2083-H	WCC		PRT	1 RC PRT MMV REV0-1	5	30APR04 17:00	30APR04 21:59		11									T-2083-H 1 R 0012083
537	1	CL-2E	WCC		CL 2E	MODE 3 TO MODE 2 CHECKLIST	459*	30APR04 17:00	19MAY04 19:59	DR-N ML-N ORT3-N R-N	0									CL-2EMC
538	1	CL-2F	WCC		CL 2F	MODE 2 TO MODE 1 CHECKLIST	480*	30APR04 17:00	20MAY04 16:59	DR-N ML-N ORT3-N R-N	0									CL-2FMC

